

LIGO-India: A Decadal Assessment on Its Scope, Relevance, Progress, and Future

C. S. Unnikrishnan¹

Tata Institute of Fundamental Research, Mumbai 400005, India²

LIGO-P2200353-v3

¹With reference to my article ‘IndIGO and LIGO-India: Scope and Plans for Gravitational Wave Research and Precision Metrology in India’, Int. J. Mod. Physics D, Vol. 22, 1341010 (2013). E-mail address: unni@tifr.res.in

²Presently at School of Quantum Technology, DIAT (DRDO), Girinagar, Pune 411025. E-mail address: unni@diat.ac.in

Abstract

The LIGO-India project to build and operate an advanced LIGO (aLIGO) gravitational wave (GW) detector in India in collaboration with LIGO-USA was considered and initiated as an Indian national megascience project in 2011. The project relied on the advantage of a head start and cost saving due to the ready availability of the full aLIGO interferometer components from LIGO-USA, approved by the National Science Foundation. Procedural formalities and site selection efforts progressed since then and the provisional approval for the Indian national project was obtained in 2016, immediately following the first direct detection of gravitational waves with the aLIGO detectors. I had discussed the scope and the science case of the project, as well as the plans for its realization by 2022, in several talks and in a paper (Int. J. Mod. Physics D, Vol. 22, 1341010, 2013). With KAGRA GW detector in Japan being tuned to be part of the GW detector network, it is now the occasion to assess the progress of LIGO-India project, and evaluate its relevance and scope for gravitational wave science and astronomy. Various key factors like human-power, management, funding, schedule etc., in the implementation of the project are reassessed in the backdrop of the evolution of the global GW detector sensitivity. In what I consider as a realistic estimate, it will take more than a decade, beyond 2032, to commission the detector even with a fraction of the projected design sensitivity. I estimate that the budget for implementation will be more than doubled, to about Rs. 35 billion (>3500 crores, \$430 million). The detrimental consequences for the project are discussed, from my personal point of view, as the coordinator of the experimental and technical aspects in the 2011 LIGO-India proposal. My decadal assessment points to the eroded scientific relevance of the LIGO-India detector in the GW detector network of the next decade. However, a revamped action plan with urgency and the right leadership can make LIGO-India a late but significant success for multi-messenger astronomy for several years after 2032, because of its design similitude to the operational aLIGO detectors. For achieving this, it is imperative that the LIGO-India detector is replanned and launched in the post-O5 upgraded A[#] version, similar to the projected LIGO-USA detectors.

Keywords: Gravitational wave detectors, LIGO detectors, LIGO-India project, GW astronomy

1 Preamble

The second generation interferometric detectors of gravitational waves were the result of major upgrades in the design and implementation of the LIGO detectors in the USA and the Virgo detector in Europe, during 2009-2015. The enthusiastic surge of interest in the anticipated detection of gravitational waves (GW) with advanced LIGO (aLIGO) detectors and the advanced Virgo detector led to the LIGO-India project proposal in 2011, to build and operate a third advanced LIGO detector in India. The proposal was the realization of ‘now, or never’ about gravitational wave science and astronomy, among the physicists who initiated the proposal [1, 2, 3]. The discussions in small meetings had given birth to the *Indigo consortium* of the GW research community in India, which gained visibility of their seriousness very soon. We were encouraged, trusted, and supported by the GW community globally, and in particular by the GWIC (GW International Committee) and the scientists from the LIGO laboratory. The LIGO project came to India after an active discussion during 2010-11 on the possibility of LIGO-Australia, in which the participation of India was proposed to be a collaborating partner. The idea of LIGO-Australia was that the interferometer components that were meant for a third LIGO detector at the same site as the US-Hanford detector should be used to build the third detector at a site in Australia, which would enable the accurate localization of GW events due to the availability of a third independent detector at a large baseline distance [4]. This was a major decision that prioritized and emphasized GW astronomy, rather than just the detection of the gravitational waves. The entire infrastructure and the operation of the detector in the network were the responsibility of the host. LIGO-Australia finally turned out to be not feasible, mainly due to the funding constraints. Then the Indigo consortium and the LIGO-laboratory explored the possibility of a LIGO detector in India. A high level committee that advised the National Planning Commission of the Government of India on large and long term national projects in astronomy recommended the LIGO-India project, after multiple presentations and evaluation, fully realizing its importance and the unprecedented advantage of obtaining the full interferometer detector components from the LIGO laboratory in the USA.

The main infrastructural elements for building the detector are a suitable site, laboratory buildings and the enormous ultra-high vacuum (UHV) enclosures of the 4 km x 4 km Michelson interferometer, for which participating Indian institutions had the full responsibility. Site selection efforts

started immediately by the Indigo consortium members, even before any assurance of funding, with timely support from the Inter-University Centre for Astronomy and Astrophysics (IUCAA), Pune. The identification of a few very good sites, isolated well from common noise sources, followed after the elimination of many which were considered, based on several visits and preliminary measurements of seismic noise. When IUCAA, Pune, and the two key technologically highly endowed institutes under the Department of Atomic Energy (DAE) – The Institute for Plasma Research (IPR), Gandhinagar, and the Raja Ramanna Centre for Advanced Technology (RRCAT), Indore – agreed to take key responsibilities for the projects, things came together as a feasible project. Speedy and cautious response and support from the NSF, USA, in the form of visits of key persons and reviews of the proposal by special committees gave a concrete form to the LIGO-India project. Four senior level visits from the LIGO-Laboratory to the LIGO-India lead-institutions for technical assessment and discussions were followed by three in depth reviews by a NSF panel. All this culminated in a review and the following resolution by the National Science Board, USA, in August 2012: “Resolved, that the National Science Board authorize the Deputy Director at her discretion to approve the proposed Advanced LIGO Project change in scope, enabling plans for the relocation of an advanced detector to India”.

The responsibility for the data handling, computing as well as the important task of building and coordinating the user community for GW astronomy was also taken by IUCAA. With the technical aspects of UHV, seismic isolation and suspensions, optical assembly, control systems etc. being handled by IPR, Gandhinagar and RRCAT, Indore, the LIGO-India project had a defined institutional structure. Regular visits by senior scientists of the LIGO laboratory and planning meetings helped in charting a road map and organizing a strong user community within a short period. Hence, three significant developments happened by the time the first detection of gravitational waves was announced in early 2016; 1) the Indigo consortium and the interest in GW astronomy had grown considerably, ten-fold during 2011-2016, 2) a large number of Indian researchers were already members of the global LIGO Scientific Collaboration (LSC) and part of the discovery [5, 6], 3) a suitable site for the LIGO-India detector was identified in the state of Maharashtra and finalized (Aundha in Hingoli district, Latitude $19^{\circ} 36' 50''$ N, Longitude $77^{\circ} 01' 50''$ E, about 175 hectares). The prompt announcement by the Prime Minister of India of the formal support and approval for the project then provided the boost and fuel to go ahead. The funding responsibility, which

was estimated then as about Rs. 13 billion (Rs. 1300 Crores, \$270 million), was to be shared between the DAE and the Department of Science & Technology (DST). The contribution from NSF and the LIGO laboratory was the entire set of aLIGO detector components (except the vacuum infrastructure) including the stabilised laser, to be given in kind. The notional cost of the contribution of the LIGO laboratory and other international partners in the LIGO Scientific Collaboration was about \$ 130 million.

2 The LIGO-India Project: The Science Case

The strong science case for the LIGO-India (LI) project had been discussed on many occasions and in publications [1, 2, 7]. The project proposal itself is available at the website of LIGO-India and the Indigo consortium (gw-indigo.org). An early compilation, leaning on the contributions from many from the LIGO Scientific Collaboration as well as the Indigo Consortium, is in my 2013 overview paper, based on a talk in the Astrod symposium (2012) held in Bengaluru [2]. The most important aspect of LIGO-India is that it is the only planned detector with the design sensitivity matching the aLIGO detectors, and of identical design and technological characteristics. Therefore, if implemented, it provides assured detections with excellent source localization on a single integrated platform. The other aspects of the additional detector in the network are the significantly improved network duty cycle, improved sensitivity, and larger sky coverage. The upgraded version of the European Virgo detector was already getting commissioned for joint observations with the two LIGO detectors, and the Japanese detector KAGRA [8] was nearing completion, when the LIGO-India project was approved in 2016. The hope was that a network of all these five detectors would become operational by 2022-23.

The sensitivity of the individual detectors can be compared when stated in terms of the equivalent range for the detection of the merger of binary neutron stars (BNS). The design sensitivity of the aLIGO detectors is about 170 Mpc. With another planned upgrade with a frequency-dependent squeezed light technology and improved mirror coating, called LIGO A+, the mature sensitivity is projected to reach beyond 300 Mpc. Advanced LIGO started its operation (O1) in 2015 with a range above 60 Mpc, and progressively reached a sensitivity of 130 Mpc. The fourth observing cycle (O4) will start in 2023, with a sensitivity around 170 Mpc. The full A+ design sensitivity is

expected only after 2028. We may expect that the LIGO detectors and Virgo detector will be operating near their A+ design sensitivities of about 260-330 Mpc, and the KAGRA detector has a goal of reaching above 130 Mpc in late 2020s. The number of sources in the range goes approximately as the cube of the range (volume). The scientific relevance of the LIGO-India detector will strongly depend on its sensitivity in actual operation; *at each stage after commissioning, it needs to be at a good fraction of the LIGO-US detectors to significantly contribute to the detection and source localization in the network operation* [10]. Due to the cubical dependence of the source-rate on the strain sensitivity, a detector is relevantly useful in a network during the mature era of GW observations only if its sensitivity is at least a factor between 2 to 3 of the LIGO A+ detectors. *Thus, the LIGO-India detector needs to be sensitive at the level of 100-150 Mpc, with more than 50% duty cycle, to be scientifically relevant in the GW advanced detectors network that is expected to remain operational until the third generation 10 km scale detectors are deployed and operational, perhaps as early as 2035.*

3 The Implementation of LIGO-India

LIGO-India interferometer components are identical to the aLIGO components, already fabricated for the interferometer previously meant as a third LIGO detector at the Hanford site, with 2 km arm length. They are in storage in the US at present. These include both the passive and active vibration isolation systems, all optical components, electronics (except computers and peripherals), proprietary instruments for monitoring and characterization etc. Some of the mirrors need refiguring and re-coating in order to be suitable for the 4 km LIGO-India detector. Some components of control systems, electronics hardware and the laser source require technology upgrades. In addition, the entire package of squeezed light injection and detection is to be fabricated and set up afresh. If a more pertinent plan that follows the upgrade plans of the LIGO-USA is adopted, to make the LIGO-India detector consistent with the “A+ design” (a significant upgrade of detector components), further infrastructure and instrument modifications would be necessary [9]. The design and specifications of the LIGO-India detector, and the technical tasks for its realization, are clearly known. There are specialist engineering tasks as well as specialist commissioning tasks. Both require not only the development of specialist expertise but also a trained work cul-

ture. The need to familiarize with a rigorously specified and controlled work culture is because this is the first large scale science project in India with stringent needs of quiet and clean physical environment as well as the sustained and disciplined monitoring by a team of experts. The advanced GW detector is a dynamic complex apparatus that requires refined expertise and familiarity for managing a stable operation.

The trained manpower required to assemble and commission the LIGO-India detector is estimated to be about 70-80 members, and about half of them should be experts in various key areas of physics, engineering, and technology. A few experts from the LIGO laboratory are expected to participate in some specialized tasks, especially during the assembly of vital optical elements and commissioning, but extended direct participation will be limited because of the ambitious upgrade plans of the operating ground based detectors in the next decade. This means that the realisation of the operational LIGO-India detector is crucially dependent on the amount and quality of the expertise available and trained within the core Indian institutions involved in the project.

4 LIGO-India Today

Where is LIGO-India today? The Prime Minister of India announced the support and notional approval for the project in February 2016. However, various aspects of the project, including site selection and essential characterisation, have been anticipated and attended to since 2012 onwards. Around the same time, the KAGRA 3-km underground gravitational wave detector project in Japan had received full approval, and the construction was in full swing by 2016. The updated schedule for operation and upgrades of different advanced detectors, as projected in 2019, is compiled in the figure 1 [10, 11, 9]. The most recent laboratory that joined the joint detection program is the Japanese GW detector collaboration KAGRA. While the LIGO detectors and the Virgo detector are keeping to their upgrade plans within one or two years, KAGRA has not yet managed to get useful extragalactic sensitivity. One can see that the schedule projected for the LIGO-India detector by its management team is lagging already several years beyond what was originally envisaged. According to the announced schedule, the detector is supposed to be commissioned for operation in 2026, to join the network of advanced detectors, with the design sensitivity of about 300 Mpc by 2027.

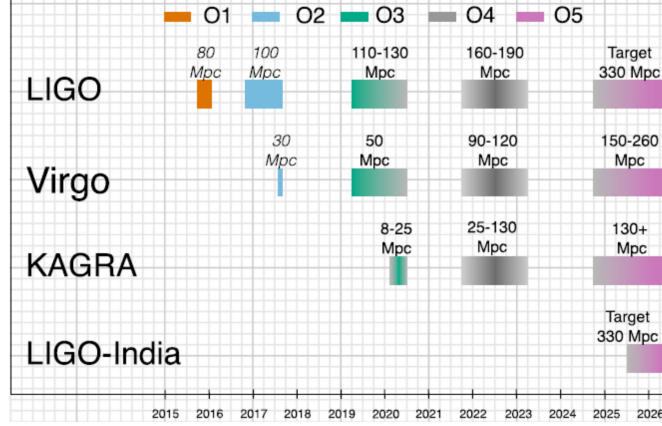


Figure 1: The projected observation schedule as of 2019 for the working LIGO and Virgo detectors and the commissioned KAGRA detector, along with the announced schedule for the implementation of the LIGO-India detector [9]. This is slightly revised more recently, without a definite projection for LIGO-India (see fig. 5).

However, an examination of the ground realities paint a completely different picture, unfortunately.

The Nobel prize advanced information document that was released after the 2017 Nobel prizes for the detection of the gravitational waves mentions LIGO-India (citing my 2013 article on the LIGO-India project and the update in arXiv:1510.06059) and the Japanese project KAGRA as the future detectors in the network [12]. KAGRA was scheduled to come online around 2018 and LIGO-India in 2022, as per the original plans. Both projects started rolling around 2012, though the KAGRA project developed from the large sized prototypes operated earlier, like the TAMA detector. The project is led by T. Kajita, who won the Nobel prize in 2015 for the discovery of atmospheric neutrino oscillations. KAGRA is an advanced detector that incorporated many new technical features. It uses cryogenic technology for cooling its mirrors to about 20 K, to suppress thermal noise and thermal lensing. It may benefit from the very low seismic noise in the underground tunnels in the Kamioka mountain. The tunnel excavation and the fabrication of the UHV beam tubes and chambers were started in 2012 and completed in 2014. It took another 4 years to complete the assembly of the interferometer and

the tests before the start of commissioning.

The KAGRA interferometer was locked for operation in 2019 and the team is still working to join network observations, initially with a fraction of the sensitivity of the aLIGO and Virgo detectors [13]. There are technical difficulties associated with the new design aspects as well as operational difficulties in maintaining the external environmental conditions stable. As another example, after decommissioning the initial LIGO interferometer, an experienced team took about 5 years to assemble and commission the aLIGO detector with the new components and vibration isolation systems, using the same infrastructure. A similar time frame was required as well to bring the upgraded version of the Virgo detector to the level of network operation.

The important point to note here is that the examples of operational detectors demonstrate that it requires 4-5 years to assemble and commission the detector with an initial working sensitivity after the completion of the basic infrastructural elements, like the levelled and stabilized land at the site, the laboratory buildings built according to stringent specifications, and the fabrication of the beam tubes and the large UHV chambers. This would be the case for even an experienced team of about 40-50 scientists, engineers and technical specialists. The delay is not mainly in fabricating the large number of components for the interferometer. It is in the careful assembly and thorough testing at each stage, because even a small compromise in the operation of individual sections is not an option. Even after achieving the stable locked operation of the interferometer, reaching a good fraction of the design sensitivity can take considerable time (typically a year or more), adding to unpredictable delays. Thus, *even in an optimistic estimate in the Indian conditions, the minimum duration required for an expert trained team to realize an advanced interferometric GW detector here with a network-worthy sensitivity is 10 years from the preparation of the site* – 4 years for the infrastructure build-up, 4 years for the assembly, tests and commissioning, and 2 years for tuning the detector for stable locking and sufficient sensitivity.

The hard lesson is that the time frame for the assembly and initial operation of the LIGO-India detector will take about 5 years *after the whole infrastructure of laboratory buildings and the UHV hardware is ready*, if we manage to have an experienced and skilled team of 50-70 people in the project by that time, at various levels.

LIGO-India today owns the required land at the chosen site. This is commendable achievement, made possible by the coordinated efforts of IUCAA, DAE, government of Maharashtra and the local administration at the dis-



Figure 2: The view of the bare site for the LIGO-India at Aundha near Hingoli, Maharashtra (2016). The lower panel depicts the vision of the site with the laboratories and the LIGO-India detector, when the construction is completed. The realistic duration to complete this transformation is another 8-10 years, in my estimate, (see also fig. 4).

trict of Hingoli. Some studies on the soil structure, seismic properties etc. have progressed. A 16 months baseline seismic survey of the site has been completed. However, the work on the land preparation for the laboratory buildings and the levelled beam tube is still in early stages. The chosen site near Hingoli is accessible by good roads (450 km from Pune, for example). Flights to the nearby town of Nanded, which already has a small airport, may become operational. LIGO-India has received the approval for construction from the state environment impact assessment authority recently. A LIGO-India office and a visitor guest house have been already set up at Hingoli.

However, the many tasks of building the infrastructure for an aLIGO detector are yet to acquire any momentum. The huge task of the fabrication of UHV chambers and the 8 km of beam tube (1.2 m diameter) requires the evaluation and finalization of the welding technology and strategy, before the fabrication can be entrusted to industrial partners. This can be a long process in India. Though the trusted choice for the welding technology is the advanced version of argon arc welding, the available technology options

have progressed very positively from the days when the LIGO beam tube was built. I had personally explored new and efficient choices like the K-TIG key-hole welding, right when I was planning and budgeting for the UHV systems in the LIGO-India proposal (in 2011). Laser welding is also a technology that has matured considerably. Several tests of both the steel material and the welding options will be required for a judicious choice that ensures long term UHV reliability. TIG welding is the chosen method for the fabrication of the UHV elements of the LIGO-India detector. A large UHV chamber with the specified design, fabricated in India, is undergoing quality tests. But, achieving the required level of ultra-high vacuum is still quite far. The advanced detector requires about a dozen such large chambers. The prototyping and testing of a beam tube section of 10 m length is yet to be done.

The LIGO-India project and the collaboration do not have a director or a project manager, even 6 years after the approval by the government of India. There is a formal management structure for monitoring the project and to coordinate activities with the LIGO laboratory in the US. However, without a leader, the project has not emerged from its formal confines. Therefore, there is no close link between the larger GW research community and the project personnel yet. There is a small funding component for small research on next generation detectors and technology, disbursed to individual researchers in universities and research institutes other than the LIGO-India core institutes. But there is no regular interaction possible yet between these researchers and the LIGO-India project team. As already mentioned, even a conservative estimate of the expert and trained human power needed to implement the LIGO-India project is about 70 to 80 participants, for the different tasks of the assembly of the detector components and vibration isolation, elaborate position metrology, UHV assembly, leak tests and certification, optical assembly and internal suspensions, control systems tests, interferometer locking and full commissioning. *At present only a fourth of this task force is available*, leading the preparatory tasks in the core institutes. The LIGO-India project has not yet started a targeted formal graduate training program. Therefore, there is no significant resource of young physicists or engineers trained, working with any of the advanced interferometer detectors, as of now.

The infrastructure of laboratory buildings and the UHV hardware installation can be readied only after the land is levelled and prepared to the stringent specifications. The work on major elements of the infrastructure

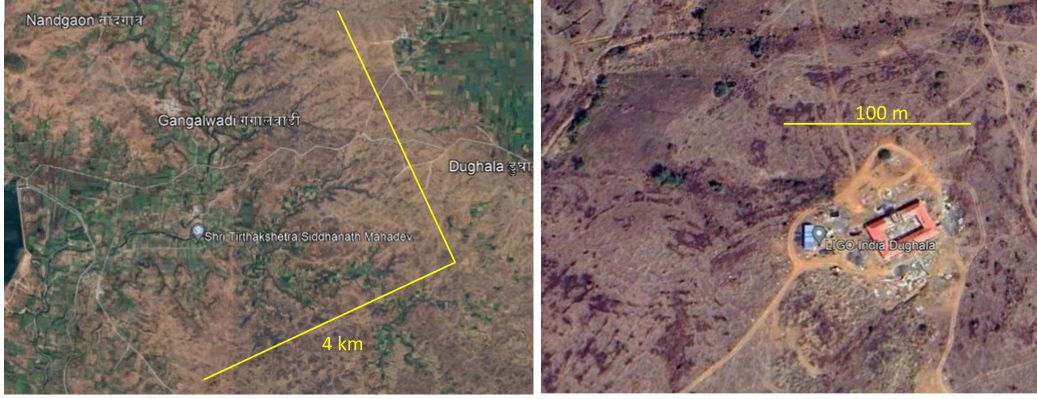


Figure 3: Left) A view of the acquired site meant for the LIGO-India detector. A sample layout of the 4 km x 4 km detector is indicated. Right) The construction status as of 2022 November, showing only a site office. The preparation of the detector site and the construction of the laboratory buildings are yet to start (*figure extracted from Google Earth*).

– the UHV chambers and beam tubes, site preparation, and the laboratory buildings – is yet to start in a scheduled manner. The proper fund flow is perhaps waiting for an updated detailed project report. This summarises the present status of the physical progress in the LIGO-India project. Based on the present status (2022), my experience in the scheduling and budgeting of the original LIGO-India proposal of 2011 enables me to make a realistic decadal assessment about the feasibility and scientific relevance of the LIGO-India gravitational wave detector project. *My revised estimate clearly shows that the network operation of the detector with a useful extragalactic sensitivity cannot be earlier than 2032, and the total cost of the project up to 2035 will be more than doubled, to about Rs. 3500 Crores (Rs. 35 billion, \$ 430 million). What is most worrisome is the obvious fact that the large delay in implementation will severely affect and diminish the scientific relevance of the project.* I will now examine the various factors that go into this decadal assessment and revised estimates.

5 LIGO-India Project Under a ‘Zeno-Effect’

The LIGO-India project was about to be launched several years ago, with the arrow well placed in the bow, still a bit unstretched. Can that arrow reach its destination when launched? First of all, one needs to wait for the ‘launcher’ leader(s). Then, as Zeno of Elea wondered, the arrow has to first reach half the distance before it can progress to the rest. But, it has to cross ‘half of half the distance’ first, etc. Can the arrow ever leave the bow?

Having studied such situations, and watched many small and big projects in India and abroad, I know that the arrow can reach the target, if only it is released. However, in a largely sequential project, the time factor becomes very important due to the paucity of experienced personnel. *Gravitational wave detectors work as a network, to achieve the ability for source localisation and to improve sensitivity and reliability of detection.* This implies that the detectors in the network ideally should have comparable sensitivities for optimum effectiveness. By the time a delayed detector reaches a good fraction of its design sensitivity, the already operational detectors will have progressed to a better sensitivity. Then the lagging detector will never catch up with the network leaders. Given the relatively small workforce of limited familiarity with the advanced detector active in the project, and the many experts who initiated the project expected to retire half-way through the project, there is a genuine Zeno-effect shadow on the project. This compromises the relevance and science case of a gravitational wave detector, meant to operate in a network.

What is an optimistic estimate of the time required to operate the LIGO-India detector at its A+ design detection sensitivity of about 250-300 Mpc for the merger of binary neutron stars? What is a reliable road map from initial commissioning to reaching the design sensitivity and how much time is required?

The preparation of the land, its transformation to the specifications and the building of the main laboratories will take about 3 years. One need not and will not wait for these tasks to be completed to start on the enormous task of fabricating the large UHV chambers and 8 km of the 1.2 m diameter beam tubes. However, the finalization of the UHV process is yet to be done and the tendering process is long. Assuming that the fabrication will start in early 2023, we can expect the completed and tested UHV components in late 2025, ready for assembly. The testing and certification of the UHV hardware is a long process and it cannot be hurried or shortened. The full

infrastructure (chambers and components in their designated positions in the buildings) can be expected sometime mid-2026. The assembly and testing of the beam tubes and their cover etc. can go parallel to the interferometer assembly. The assembly of the full interferometer will take a minimum of 3 years because of the complexity and the number of components. Thus, the interferometer could be ready for locking and commissioning only after mid-2029. Assuming that the commissioning task will be aided well by some experts from the LIGO laboratory, a reasonable estimate of locked operation is then 2030. From this point to achieving a sensitivity at which it can join network operations (50-100 Mpc for BNS merger) takes between 2-3 years. *Optimistically assuming a minimum duration for tuning up the sensitivity, the LIGO-India detector will be network ready only after 2032.* It is clear that the present projection of 2027 by the LIGO-India management is naive and not feasible. The optimistic revised date for network operation at extra-galactic sensitivity is 2033. However, the projected design sensitivity for an A+ detector (300 Mpc) can be reached, if at all, only well past 2035.

We have assumed that the presently operating detectors (aVirgo and aLIGO-USA) will be operating at their design sensitivity of about 250-300 Mpc till 2032. However, further upgrades are planned for these detectors which need to be taken into account when we discuss the relevance and science case of LIGO-India in 2032. Note that even at the sensitivity near 100 Mpc, LIGO-India will see effectively less than 1 in 25 ($<4\%$) of all events detected by the LIGO-US and the Virgo detectors (the events might be detected, but with much less statistical significance compared to other detectors). Therefore, *though operating as a useful support instrument for the network, it cannot play a decisive role in discoveries, unless the sensitivity is increased to the design sensitivity.* However, this is a long path of tuning and can take many years, by which we enter the era of next generation detectors. As indicated earlier, in my estimate based on the progress achieved in presently working advanced detectors, the LIGO-India detector can hope to reach near its design sensitivity of 250-300 Mpc only in 2035. This should be seen in the context that by 2040, the global detector network hopes to move up from the present advanced detectors to the next generation detectors like the Cosmic Explorer and the Einstein Telescope, with 8-10 times the sensitivity of the present advanced detectors.

I am not fully aware of the upgrade plan for the KAGRA detector. But, the present plan is to be a full partner in GW astronomy mission of the advanced detectors by joining the next cycle of observation called the ‘O4’

observation cycle, due in early 2023. This is a crucial time when the additional detector will help in better localization of the astrophysical sources, even with a reduced sensitivity, as long as the signal is visible in the detector with a reasonable signal-to-noise ratio.

The commissioning of an advanced detector in India by 2025-26 was a scientifically worthy and attractive goal in 2015, when the first indication of a detection came confirming the wealth of astronomy in store for the interferometric GW detectors. But, as viewed in 2022, the completion and operation of a detector after 2032 at the same level of sensitivity (about 100 Mpc) is no more a scientifically exciting goal, though its relevance as an essential instrument for precision astronomy in a multi-detector network remains intact. This is because LIGO-India is the only planned detector with a sensitivity matching the two LIGO instruments in the USA. However, the significant delay does affect its role as an instrument for discovery. *What is evident from even an optimistic estimate of the operation schedule for LIGO-India is that the detector will definitely miss the opportunity to contribute to multimessenger astronomy during the decade, 2022-2032.* This does not exclude a supportive role for LIGO-India in GW astronomy in the ensuing decade. However, the enthusiasm in the astronomy community, even within India, about such a detector will be diminished.

It is very clear that the undesirable situation of the LIGO-India detector operating always at 3-4 times less sensitivity than other detectors in the network should be avoided. However, I do not see how this unfortunate situation could be avoided in any reasonable projection of the schedule, severely affected by the past delays. This needs urgent and serious discussion and remedial measures, if there are any.

6 The Cost Factor

When the LIGO-India proposal was being prepared in 2011, we were very careful to minimize costs, and went to great lengths to find out optimal ways to keep the cost within reasonable demands. What was important in this goal was to identify expertise within the academic community and institutes, instead of delegating everything to industrial expertise. In any case, the required expertise was not available in the industrial circles. Also, timely execution was a crucial factor. Since the major costs are in UHV fabrication and certification, it is very important to compare and evaluate the cost in-

crease in steel and welding technologies etc. From 2015 to 2022, the price of stainless steel has more than doubled. This alone can increase the costs by \$80 million. When the proposal was submitted in 2011, the projected budget of about Rs. 1250 crores (\$270 million then) seemed adequate, with the understanding that a 15-20% eventual increase and revision of costs should be expected by the time it is implemented in 2020. Now in 2022, the projected costs have more than doubled. A reassessment indicates that project implementation will require about Rs. 3500 crores (about \$430 million now; the dollar has significantly increased against the Indian Rupee, by a factor 1.7). At present, the released funding in the past six years is less than 4% of the total revised cost.

The Indian government has other megascience commitments as well, both national and international. The funding required for the international ITER project on nuclear fusion (located in France), which is in construction phase, will be over 2 billion dollars (>Rs. 15000 crores, estimated as 9% of 25 billion dollars total international budget), with the expected commissioning around 2035. The INO project on the atmospheric neutrino observatory (India-based Neutrino Observatory at Teni, Tamilnadu, India) was fully approved, and funds were allocated, but it continues to face legal hurdles sustained by a hostile situation of local politics and misleading propaganda. The \$300 million project is unlikely to be realized now because all the members with experience in experimental particle physics and detector technology have either retired or are about to retire. The INO graduate training strategy has not resulted in training adequate expertise among the younger generation to take the project forward. Thus, there are no experts to lead various aspects of such a project in the next decade. Also, the science case of the project (if and when it can be realized) has weakened significantly, due to the delays and the launch of new projects on neutrino observatories elsewhere. The hyper-Kamiokande project (with the projected commissioning after 2025) is aimed at solving the outstanding problems of mass hierarchy, CP violation in neutrino sector etc. The DUNE project led by the Fermilab also has unique capabilities in answering such outstanding issues. One can gauge the relevance of the INO detector that will take 8-10 years for completion, by comparing with these other initiatives. This makes the INO project scientifically much less significant, even if all the extraneous hurdles were removed today (which is not the reality). Then there are commitments in the country in optical and radio astronomy, for international telescope projects outside the country. The hugely delayed Thirty-Meter Telescope (TMT) project for

the large optical telescope, proposed to be installed at Hawaii, is another major international commitment that exceeds Rs. 1500 cores. The (current) commitments in other astronomy projects like the Square Kilometer Array (SKA) are smaller. LIGO-India is indeed the largest ‘home’ project in basic science and astronomy ever taken up in India.

Unfortunately, the revised funding needed for LIGO-India conflicts with the present situation of decreased GDP growth in India and elsewhere. The Covid-19 pandemic is a global problem, but it will seriously affect and delay the fund flow into the mega-science projects, justifiably. No substantial quantum of funds is approved or released yet for LIGO-India because the actual spending for the large hardware and infrastructure has not yet started. In my judgement, the cost factor will significantly impact the LIGO-India schedule, at least in the early part of its execution, and will unpredictably delay the operation of the detector. *On the other hand, any decision on fully funding the project now will have to evaluate and reconsider the doubled cost factor for a project that has reduced scientific significance, when implemented for operation after 2032.*

7 A View from the Other Side

The LIGO-India project is not merely an Indian national project. It is an important multi-national collaborative effort, of setting up and operating one of three identical advanced LIGO detectors in India, in the network operation with the other two detectors in the USA, and also with the Virgo detector in Europe. An MoU was signed with the National Science Foundation and the LIGO laboratories (Caltech and MIT). It cannot be that the NSF and LIGO laboratories are unaware of the steadily diminishing scientific and astronomical relevance of the delayed LIGO-India project. In fact, the executive director of the LIGO laboratory, David Reitze, had noted in a meeting in India (Pune, 2017) that *a serious risk to LIGO-India scientific program exists if delays begin to accumulate.*

The commitment by the LIGO laboratory for providing all the interferometer components, some suitably modified, still stands. These items that are stored in safe packing await shipping to India. However, before the shipping to India takes place, the infrastructure to receive them needs to be completely ready. In the absence of timely progress on this front, what are the options at this stage?

Apart from the uncertain internal cost factor involved in the commitment of providing the interferometer components, there are even changes in the basic rules of the import of scientific equipment to India. Unless explicitly exempted, there is an additional burden of at least 18% cost as Goods and Services Tax, to be collected as additional customs duty, for equipment imported by scientific establishments. Of course, this will have to be provided as additional funding to the LIGO-India project by the Government of India itself – sort of a strange situation of giving with one hand and taking with another. But, the added administrative cost on both sides is not negligible.

Even at a reduced scientific relevance, the only possibility for gainfully using the components fabricated for a third LIGO interferometer seems to be the implementation of the LIGO-India project. In my view, there seems to be no possibility of reviving a plan like LIGO-Australia. However, a proper evaluation of the projected joint operation of the ground based detectors, estimating accurately the efficacy of the LIGO-India detector in network operation is necessary. It is clear that the LIGO-India detector will remain in a supporting role unless a straggling gap in the projected sensitivity, compared with other operational detectors, is mitigated. I will now examine a path for regaining a prominent role for LIGO-India detector.

8 LIGO-India A+

There is a well directed plan for a significant upgrade of aLIGO detectors to LIGO A+ detector, to be completed by 2026 [9, 14]. The technology additions envisaged are mature squeezed light quantum measurement and vastly improved low loss mirror coatings. There are other upgrade options as well, by adding to the interferometer baseline. Clearly, LIGO-India should directly be installed and commissioned in its A+ version, since its assembly phase is definitely after 2025. If this is not done LIGO-India will not be very relevant or useful in the network, when it is fully commissioned. Therefore, *the present understanding is that LIGO-India will be installed in its A+ version directly*. Still, LIGO-India needs to go through the long and elaborate process of assembly, commissioning, and step by step tuning of the sensitivity to reach the sensitivity suitable for the global network operation. Since it is clear that the LIGO-India detector is behind its announced schedule by at least 5 years, it is now excluded from consideration for the quantitative estimates for the efficacy (localization of sources, network duty cycle etc.) in

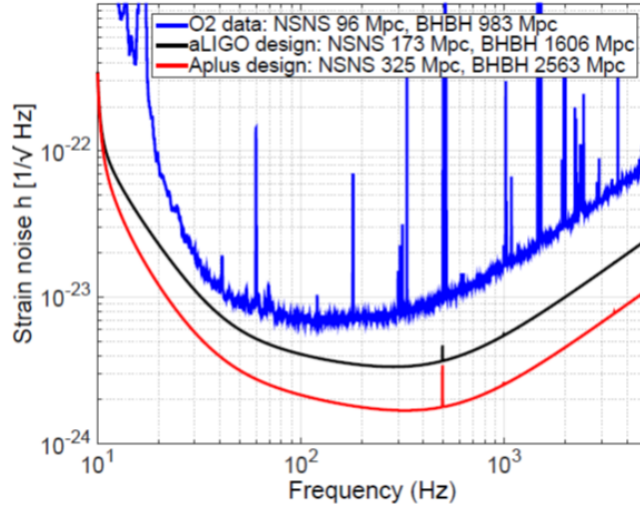


Figure 4: Projected sensitivity of the A+ upgrade in 2026, compared to the sensitivity of presently operating aLIGO detectors [9, 14].

the parameter estimation from the observations during 2026-2030.

The O5 observation cycle for the LIGO-Virgo detectors is planned during 2026-2029. The LIGO detectors will operate with A+ design during O5. However, the post-O5 operation of the LIGO detectors envisages a major upgrade called “A#” (written as A# in the rest of this paper) [15]. This is expected to operate with two times better sensitivity than A+. *I am convinced that this situation demands an immediate redefinition of the plans for LIGO-India, because it will be ready for observations only after the LIGO-A# detectors are commissioned in the USA for their post-O5 operation.* I discuss this vital point next.

9 Beyond A+: Post-O5 and LIGO-A#

Further improvement of the LIGO-USA facility beyond 2029, after the observation cycle O5, have been in discussion for some time, and two possibilities were studied. The option called “A#” involves replacing the main test mass mirrors with much heavier mirrors and suitable upgraded suspension and vibration isolation systems. The A+ version has 40 kg mirrors whereas the A# design is with 100 kg test masses, suspended on the silica fibres at twice

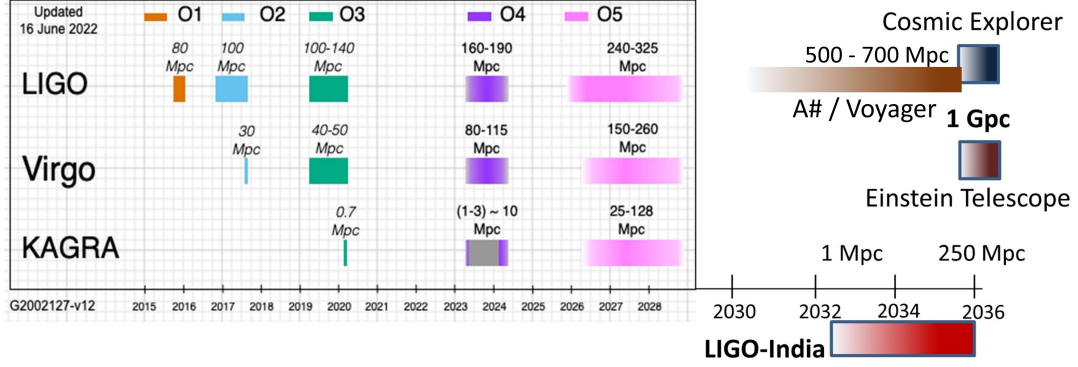


Figure 5: Revised schedule for the observation cycles with progressively increasing sensitivity of LIGO, Virgo, and KAGRA detectors, post-pandemic (LIGO document G2002127). I have added a realistic estimate for LIGO-India. By the time the LIGO-India detector is operational, gravitational wave astronomy will have entered an era of next generation detectors, like the Voyager upgrade in the LIGO facility. Post 2036, we can expect the beginnings of the 10 km class Cosmic Explorer and Einstein Telescope.

the stress levels. Also, the intra-cavity laser power at the same wavelength (1064 nm) will be increased from 750 kW to 1500 kW. This requires better reflective coatings of the mirrors, still under development. The thermal noise in the mirror coating is expected to be reduced by a factor of 2. Further, the amount of quantum squeezing of light at the detection section will be improved (from 6dB in A+) to 10 dB. These are the main upgrades that will result in the superior sensitivity of the A# design.

The A# option is at present preferred over the second option called “Voyager”, in which the existing optical elements are to be replaced with entirely new optics made of Silicon. The suspended Si mirrors will be much heavier, about 200 kg. These will be in a semi-cryogenic environment of 123 K, at which the low mechanical loss and the zero thermal expansion of Silicon will result in reduced thermal noise and thermal lensing. The same UHV infrastructure would be used for this transition to the Voyager version [16]. The high power stabilized laser will be replaced with one of longer wavelength, near 2 micron, to match the reflection characteristics of the Silicon optics. The projected improvement in sensitivity of these options is by more than a

factor of 2, or about 700 Mpc for BNS merger.

There has been no serious discussion so far about the role of LIGO-India in its A+ version during the era of A# or Voyager. If the technology tests succeed and the A# version of the LIGO-US detectors is implemented in early 2030s, LIGO-India will only have a fraction of the sensitivity of the LIGO-US detectors, when it becomes eventually operational in 2032. Therefore, a definite road map to closely participate in the LIGO developments and to follow its course needs to be framed soon. In other words, the post-O5 plan of the A# version (or Voyager) of LIGO-USA detectors makes it imperative that LIGO-India follows the same course, for operation at a good fraction of the sensitivity of the leading LIGO detectors. *Aiming to implement the lower sensitivity A+ version for LIGO-India is certainly not the right course, according to my estimate and projections, if we desire a frontline stature in the GW detector network.* However, building the detector with the A# design requires certain incremental changes in the main infrastructure (vibration isolation, UHV chambers, layout etc.) *as well as the additional funding required for the upgraded elements.*

10 Can LIGO-India be a Late Yet Significant Success?

This question has a conditional affirmative answer, which I examine now. What is definite about the LIGO-India project is that it will miss the O5 observation phase of the LIGO-Virgo-KAGRA detectors, scheduled from late 2026 for a few years. We need to look for a significant participation beyond O5. The analysis so far, especially the aspect about a reduced scientific relevance, was based on the announced projections on the systematic upgrades and developments beyond LIGO A+ design, which is the one to be implemented in LIGO-India. However, these projections naturally have some uncertainty arising from technical difficulties of cutting edge technology, as well as from external factors like funding, global social and economic situation etc., as one can understand. A very favourable aspect that guaranteed a special position for LIGO-India in the detector network was the fact that its design is identical to the two LIGO detectors in the USA, which operate at a higher sensitivity than advanced Virgo, given its smaller baseline of 3 km. The KAGRA detector at its design sensitivity cannot match with even

Virgo. Thus, the possibility of a late LIGO-India to be the crucial element in achieving localization capability of the detector network at the level of a few square degrees is real and evident, especially if KAGRA fails to achieve the promised design sensitivity beyond 130 Mpc even by 2032. The fact that LIGO-India will replicate the successful design elements of the LIGO-USA detectors is its reliable advantage. However, the duration to reach a decisive sensitivity cannot be reduced significantly from the estimate that I discussed already. Given this situation, if LIGO-India is commissioned with an initial extragalactic sensitivity larger than 10 Mpc, before 2032, and tuned up to a stable sensitivity of 300 Mpc by 2034, then it will enjoy a position of prominence with the LIGO-Virgo network for a few years, till about 2040, with progressive improvement to the design sensitivity beyond 500 Mpc. However, *it is mandatory that LIGO-India is replanned with the A# design meant for post-O5 era, rather than the less sensitive A+ design, for it to be prominent and truly relevant.* Such a major shift of focus is what I propose and advocate, because *I think that the A# design is the right option for a delayed LIGO-India.* This is certainly feasible by revamping the present structure of management and work culture, along with a determined action on all aspects of human resource development. However, this feat is crucially dependent on the availability of necessary funds and significantly augmented expert human resources, after the full approval of a revised DPR and the project within the next two years. It is a small window of opportunity. Again, the absence of a leading figure of science and technology to take the LIGO-India project forward at the required pace is clearly felt. The five factors – reliable leadership, expert human power, funding, time factor, and scientific relevance – need to be urgently addressed and reviewed carefully for any realistic strategy of execution.¹

11 Summary

In my earlier overview paper (2013) on the scope and plans for the LIGO-India gravitational wave detector, I sketched some key developments on the large canvas of the megascience project. It was then perceived as transformational for Indian science, technology and higher education, and rejuvenating

¹I am a member of the LIGO Scientific Collaboration (LSC) and the LIGO-India Scientific Collaboration (LISC). This article is based entirely on my personal perception and estimates about the LIGO-India project.

for Indian physics and astronomy. More than a decade after the LIGO-India proposal, and six years after its notional approval, the actual construction of the infrastructure and the fabrication of the critical detector elements are yet to start. This implies a shift in the schedule for implementation by several years, and the integration in the global network by a decade, to beyond 2032. Also, there are other hindering factors, like substantial cost escalation, retirement of current experts etc. The consequences for the science scope of the project and the definite erosion of the relevance of the delayed LIGO-India detector in a network operation, in the era of GW and multimessenger astronomy, are examined. The LIGO-India detector is sure to miss the seminal decades of multi-messenger astronomy, 2015-2035, when various kinds of sources are being discovered and many fundamental aspects are being tested. However, *with timely revamped action, the LIGO-India project with a A# design can still be a late yet significant success*, serving a prominent role in the detector network and precision GW astronomy for a decade after 2034. My assessment urges an immediate evaluation and restructuring of the LIGO-India project in the context of the unavoidable stretch in its schedule.

Acknowledgements

This article benefitted immensely by the suggestions and comments by David Shoemaker. I thank Martine Armand for many helpful comments.

References

- [1] Iyer, B *et al.*, LIGO-India Technical Report, LIGO document M1100296-v2 (<https://dcc.ligo.org>, 2011).
- [2] Unnikrishnan, C. S., IndIGO and LIGO-India: Scope and Plans for Gravitational Wave Research and Precision Metrology in India, *Int. Jl. Mod. Phys.*, 2013, **D22**, 1341010; arXiv:1510.06059.
- [3] Souradeep, T., Raja, S., Khan, Z., Unnikrishnan, C. S., and Iyer, B., LIGO-India – a unique adventure in Indian science, *Current Science*, 2017, **113**, 672.
- [4] LIGO-Australia - On the Crest of the Wave, The LIGO-Australia proposal, 2011, LIGO Document M110273.

- [5] Abbott, B. P. et al., Observation of Gravitational Waves from a Binary Black Hole Merger, *Phys. Rev. Lett.*, 2016, **116**, 061102.
- [6] Unnikrishnan, C. S., Double bonanza at the LIGO gravitational wave detectors, *Current Science*, 2016, **110**, 1146-1152.
- [7] Sathyaprakash, B. S. *et al.*, Scientific benefits of moving one of LIGO Hanford detectors to India, 2012, LIGO document T1200219-v1.
- [8] Akutsu, T. (for KAGRA Collaboration), Large-scale cryogenic gravitational-wave telescope in Japan: KAGRA, *Journal of Physics: Conference Series*, 2015, **610**, 012016.
- [9] Shoemaker, D. et al, Gravitational wave astronomy with LIGO and similar detectors in the next decade, *Astro2020 Science white paper*, 2019, arXiv:1904.03187
- [10] Abbott B. P. et al (LIGO-Virgo-KAGRA Collaboration), Prospects for observing and localizing gravitational-wave transients with Advanced LIGO, Advanced Virgo and KAGRA, *Living Rev Relativ.*, 2020, **23**:3.
- [11] Raychaudhury, S., Status of LIGO-India, 2018, LIGO document G1801867-v3.
- [12] <https://www.nobelprize.org/>, Scientific background: The laser interferometer gravitational-wave observatory and the first direct observation of gravitational waves, *Nobel prizes advanced information*, 2017, p14.
- [13] Akutsu, T. et al (KAGRA Collaboration), First cryogenic test operation of underground km-scale gravitational-wave observatory KAGRA, *Class. Quant. Grav.* 2019, **36** 165008.
- [14] McCuller, L., LIGO A+ upgrade status report, 2019, LIGO document G1900980.
- [15] Report from the LSC Post-O5 Study Group, 2022, LIGO document T2200287-v2.
- [16] LIGO Scientific Collaboration, The LSC-Virgo White Paper on Instrument Science, 2016, LIGO Document T1600119-v4.
