

Time-interval balancing in multi-processor scheduling of composite modular jobs (preliminary description)

Mark Sh. Levin *

The article describes a special time-interval balancing in multi-processor scheduling of composite modular jobs. This scheduling problem is close to just-in-time planning approach. First, brief literature surveys are presented on just-in-time scheduling and due-data/due-window scheduling problems. Further, the problem and its formulation are proposed for the time-interval balanced scheduling of composite modular jobs.

The illustrative real world planning example for modular home-building is described. Here, the main objective function consists in a balance between production of the typical building modules (details) and the assembly processes of the building(s) (by several teams). The assembly plan has to be modified to satisfy the balance requirements. The solving framework is based on the following: (i) clustering of initial set of modular detail types to obtain about ten basic detail types that correspond to main manufacturing conveyors; (ii) designing a preliminary plan of assembly for buildings (time interval is about 2 years); (iii) detection of unbalanced time periods, (iv) modification of the planning solution to improve the schedule balance. The framework implements a metaheuristic based on local optimization approach.

Two other applications (supply chain management, information transmission systems) are briefly described.

Keywords: multi-processor scheduling, combinatorial optimization, time-interval balancing, balanced clustering, home-building, heuristics

Contents

1	Introduction	2
2	On Just-In-Time scheduling	3
3	Time-interval balancing scheduling of modular jobs	10
4	Time-interval balanced planning in modular house-building	12
4.1	Life-cycle and home-building conveyor	12
4.2	Real world illustrative numerical example	13
5	Brief description of two other applications	29
5.1	General framework for supply chain management	29
5.2	Planning of multichannel flow in data transmission	29
6	Conclusion	30
7	Acknowledgments	30

*Mark Sh. Levin: Inst. for Inform. Transmission Problems, Russian Academy of Sciences; <http://www.mslevin.iitp.ru>;
email: mslevin@acm.org

1. Introduction

In general, some special problems are under examination in which chains/sequences of objects/items are clustered/located. For example, clustering and location of chains into bins are considered in [14]. Usually, applications of the problems correspond to planning in manufacturing systems and computing systems. It is reasonable to point out, various balanced clustering problems and balanced combinatorial optimization problems have been examined (e.g., balanced knapsack problems, balanced assignment problems, balanced bin packing problems, balanced scheduling problems). The basic author glance at balanced clustering problems is contained in [108,109]. In the paper, a special new time-interval balancing in multi-processor scheduling of composite modular jobs is examined. Here, the following hierarchy is under consideration: (1) a set of basic elements (i.e., basic modules); (2) an initial set of composite jobs/tasks (for multi-processor scheduling) consisting of the above-mentioned basic elements; and (3) the resultant multi-processor scheduling while taking into account proportion-based constraints (by proportion of the used basic elements) for each time interval.

The consideration is mainly based on a special scheduling problem for time-interval balanced assembly in modular home-building. Fig. 1 depicts a relationship of the examined problem and some close JIT scheduling/planning problems.

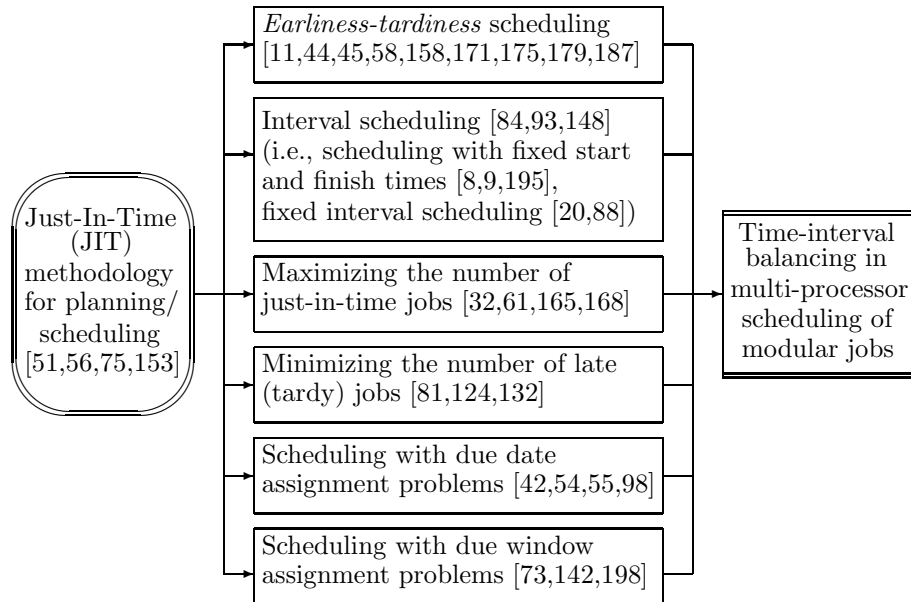


Fig. 1. Scheme of some JIT relative scheduling problems

At the end of the paper, two other application domains for the considered problem are pointed out. This material can be considered as a special part of balanced clustering domain and the author project on combinatorial clustering [104,106] including dynamic clustering [105,107] and balanced clustering [108,109].

2. On Just-In-Time scheduling

Just-In-Time (JIT) scheduling problems are mainly based on earliness-tardiness planning models [6, 7,44,45,75,98,111,152,158,159,179,187,189] and interval scheduling models [84,88,93,148]. JIT scheduling models assume an existence of job due dates and penalize both early and tardy jobs (e.g., earliness penalty/cost, tardiness cost as late charge, etc.).

Further, brief literature surveys on some research directions in the field of JIT are presented as follows:

- (a) general issues on JIT scheduling (Table 1),
- (b) JIT scheduling models (Table 2),
- (c) solving (algorithmic) approaches in JIT scheduling (Table 3), and
- (d) basic application domains of JIT scheduling (Table 4).

Table 1. General issues on JIT scheduling

No.	Issue(s)	Source(s)
1.	Basic scheduling problems (books, surveys)	[75,152,153]
2.	JIT philosophy: a literature review	[51]
3.	Some surveys on JIT systems	[94,153]
4.	Schedules for mixed-model, multi level just-in-time assembly systems	[51]
5.	JIT management of building projects	[150]
6.	JIT-KANBAN systems (literature review)	[163]
7.	Controlling just-in-sequence flow-production	[121]
8.	Design and operational issues of kanban systems (overview)	[3]
9.	Robust design methodology for Kanban system design	[131]
10.	JIT production leveling	[50]
11.	JIT manufacturing system (introduction, implementation)	[85]

Let us describe two simplified illustrative examples. Here, an initial job (task) set is given $A = \{a_1, \dots, a_i, \dots, a_n\}$, there are parameters for each job $a_i \in A$: (a) processing time $\theta(a_i)$; (b) general time interval $[0, T]$ for processing the job set A ; (c) interval for job a_i processing (i.e., early time and tardy time: $\lambda^{a_i} = [t_1^{a_i}, t_2^{a_i}]$, $t_1^{a_i} < t_2^{a_i}$; $t_1^{a_i}, t_2^{a_i} \in [0, T]$). Numerical examples are depicted as follows:

- (a) one-machine/processor scheduling (Fig. 2, Table 5), $A = \{a_1, \dots, a_7\}$, general time interval $[0, 5.0]$;
- (b) three-machine/processor scheduling (Fig. 3, Table 6), $A = \{a_1, \dots, a_{12}\}$, general time interval $[0, 5.0]$.

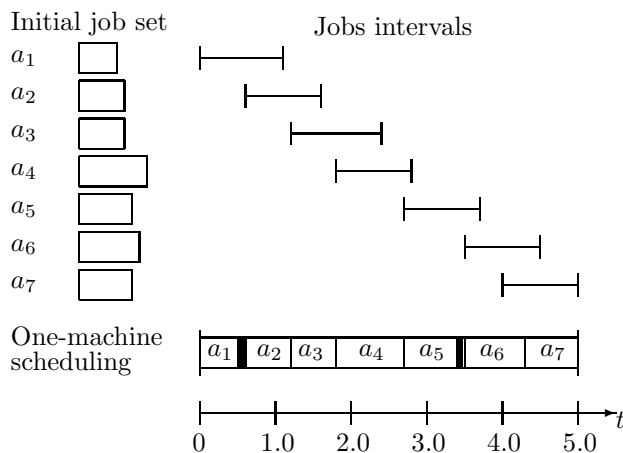


Fig. 2. Illustration for one-machine scheduling

It is reasonable to point out (separately) the basic objective functions which are usually used in JIT-like scheduling problems:

- 1. makespan (i.e., total completion time of all jobs) maximization in scheduling (e.g., [37]),
- 2. maximizing the number of JIT jobs in scheduling (e.g., [32,168]),

Table 2. JIT scheduling models

No.	Model(s)	Source(s)
1.	Maximizing the number of JIT jobs:	
1.1.	Scheduling to maximize the number of JIT jobs (survey)	[168]
1.2.	Parallel machine scheduling to maximize the weighted number of JIT jobs	[1,178]
1.3.	Scheduling of parallel identical machines to maximize the weighted number of JIT jobs	[61]
1.4.	Maximizing the number of JIT jobs in flow-shop scheduling	[32]
2.	JIT scheduling with equal-size (unit processing) jobs:	
2.1.	JIT scheduling with equal-size jobs (survey)	[174]
2.2.	Due dates assignment and JIT scheduling with equal-size jobs	[186]
2.3.	Minmax weighted earliness-tardiness with identical processing times (and two competing agents)	[49]
3.	JIT scheduling in flow shop scheduling systems:	
3.1.	JIT scheduling problem in flow shop scheduling systems	[165]
3.2.	Maximizing the number of just-in-time jobs in flow-shop scheduling	[32]
3.3.	Parameterized tractability of the just-in-time flow-shop scheduling	[60]
4.	Multicriteria JIT scheduling problems:	
4.1.	Multicriteria JIT scheduling problems	[182]
4.2.	Multi-criteria scheduling in JIT approach	[17]
4.3.	Multicriteria earliness-tardiness scheduling	[63]
4.4.	Bicriterion approach to common flow allowances due window scheduling with controllable processing times	[192,203]
4.5.	Multi-criteria scheduling with due-window assignment problem	[139]
5.	Some basic JIT scheduling problems under uncertainty:	
5.1.	Scheduling problem with uncertain parameters in just in time system	[19]
5.2.	Stochastic scheduling with minimizing the number of tardy jobs	[40]
5.3.	Minimizing the number of tardy jobs with stochastically-ordered processing times	[183]
5.4.	Stochastic single machine scheduling with quadratic early-tardy penalties	[127]
5.5.	Minimization of the weighted number of tardy jobs with random processing times and deadline	[36]
5.6.	Scheduling stochastic jobs with asymmetric earliness and tardiness penalties	[22]
5.7.	Single machine stochastic scheduling to minimize the expected number of tardy jobs using mathematical programming models	[164]
5.8.	Stochastic flow-shop scheduling with minimizing the expected number of tardy jobs	[41]
5.9.	Stochastic scheduling on parallel machines subject to random breakdowns to minimize expected costs for earliness and tardy jobs	[23]
5.10.	Single machine stochastic JIT scheduling problem subject to machine breakdowns	[180]
5.11.	Fixed interval scheduling under uncertainty	[20]
6.	Some special models:	
6.1.	Makespan minimization of multi-slot JIT scheduling on single & parallel machines	[37]
6.2.	Mixed-model, multi level JIT processes, assembly systems	[18,96,125,177]
6.3.	Maximum deviation JIT scheduling problem	[21,177]
6.4.	Online JIT scheduling framework as weighted bipartite matching	[122,152]
6.5.	Cyclic scheduling for production system under JIT delivery policy	[146]
6.6.	Two-agent single-machine scheduling problem with JIT jobs	[33]
6.7.	JIT scheduling with controllable processing times on parallel machines	[110]
6.8.	JIT scheduling with competing agents	[35]
6.9.	Single machine weighted mean squared deviation problem	[149]

Table 3. Solving (algorithmic) approaches

No.	Solving approach	Source(s)
1.	General solving approaches:	
1.1.	Sequencing approaches for mixed-model JIT production systems (review)	[38]
1.2.	Decomposition method for multi-product kanban systems with setup times and lost sales	[91]
1.3.	Decomposition algorithms for parallel machine JIT scheduling	[27]
1.4.	Dynamic programming algorithms (e.g., for mixed-model, JIT production systems)	[126,179]
1.5.	Unifying approach by goal programming approach for JIT manufacturing	[111]
1.6.	Simulation analysis of JIT techniques for production systems	[64]
2.	Constrained programming approaches:	
2.1.	Constrained programming approach for JIT scheduling	[128]
2.2.	Change constrained programming for stochastic scheduling with minimizing the number of tardy jobs	[40]
3.	Some polynomial methods:	
3.1.	Polynomial cases and PTAS for JIT scheduling on parallel machines around a common due-date	[185]
3.2.	Some new polynomial cases in JIT scheduling problems with multiple due dates	[184]
3.3.	Quadratic time algorithm to maximize the number of JIT jobs on identical parallel machines	[26]
3.4.	Polynomial algorithm for minimization of earliness, tardiness and due date penalties on uniform parallel machines with identical jobs	[39]
3.5.	FPTAS for the weighted earliness-tardiness problem	[87]
3.6.	FPTAS for the total weighted tardiness with a common due date	[78]
3.7.	Fast FPTAS for minimization of total weighted earliness and tardiness (single machine scheduling, about large common due date)	[82]
4.	Enumerative techniques (e.g., branch-and-bound (B&B), dynamic programming (DP)):	
4.1.	B&B algorithm for single machine earliness and tardiness scheduling	[157]
4.2.	B&B algorithm for minimizing earliness&tardiness costs in single-machine stochastic scheduling	[10]
4.3.	B&B algorithm for the single machine sequence-dependent group scheduling with earliness and tardiness penalties	[83]
4.4.	Faster B&B algorithm for the earliness&tardiness scheduling problem	[175]
4.5.	Branch-and-cut algorithm for single machine JIT scheduling to minimize the sum of weighted mean squared deviation of completion times with respect a common due date	[149]
4.6.	DP algorithm for scheduling mixed-model, JIT production systems	[126]
5.	Heuristic (macroheuristic) approaches (including evolutionary methods):	
5.1.	Heuristics for JIT scheduling in parallel machines	[97]
5.2.	GA for single machine scheduling with linear earliness& quadratic tardiness penalties	[189]
5.3.	Hybrid Genetic Bees Algorithm applied to single machine scheduling with earliness and tardiness penalties	[204]
5.4.	Hybrid GA-SA algorithm for JIT scheduling of multi-level assemblies	[154]
5.5.	Tabu search for JIT sequencing for mixed-model assembly lines with setups	[123]
5.6.	Tabu search in JIT scheduling problem with uncertain parameters	[19]
5.7.	Tabu search for fixed interval scheduling under uncertainty	[20]
5.8.	Local search metaheuristic for the JIT scheduling problem	[31]
5.9.	Metaheuristics for scheduling on parallel machine to minimize weighted number of early and tardy jobs	[2]
5.10.	Metaheuristics for multi-criteria scheduling with JIT approach (genetic algorithm (GA), particle swarm optimization (PSO), differential evolution (DE))	[17]
5.11.	Hybrid metaheuristics for scheduling to minimize weighted earliness-tardiness penalties on parallel identical machines	[7]

3. maximization of the weighted number of JIT jobs in scheduling (e.g., [1,61,178]),

4. minimizing the number of tardy jobs in scheduling (e.g., [40]),

5. minimization of weighted earliness and tardiness penalties in scheduling (e.g., [7,69]),

Table 4. Some JIT application domains

No.	Application domain	Source(s)
1.	JIT scheduling for production (manufacturing) systems	[75,126,130]
2.	JIT schedules for flexible transfer lines	[95]
3.	JIT scheduling for register optimization (computer design)	[156]
4.	JIT scheduling for multichannel Ethernet passive optical networks (EPONs) (online JIT scheduling framework as weighted bipartite matching)	[122,152]
5.	JIT scheduling for real-time sensor data dissemination	[117]
6.	JIT signaling for WDM optical burst switching networks	[193]
7.	Scheduling with JIT approach in transportation	[5,17]
8.	JIT management of building projects	[150]
9.	Computer wiring & bandwidth allocation of communication channels	[13,28,57,88]
10.	VLSI circuit design	[24]
11.	Timetabling (for bus drivers, for aircraft services, for class scheduling, for satellite data transmission, etc.)	[25,92,120]
12.	Identification of protein-encoding genes by spectroscopical methods	[29]
13.	Scheduling a maintenance activity	[92,143]

Table 5. Date for examples of interval scheduling

No.	Job a_i	Processing time $\theta(a_i)$	Processing interval $\lambda^{a_i} = [t_1^{a_i}, t_2^{a_i}]$	Position in schedule
1.	a_1	0.5	[0.0, 1.1]	1
2.	a_2	0.6	[0.6, 1.6]	2
3.	a_3	0.6	[1.2, 2.4]	3
4.	a_4	0.9	[1.8, 2.8]	4
5.	a_5	0.7	[2.7, 3.7]	5
6.	a_6	0.8	[3.5, 4.5]	6
7.	a_7	0.7	[4.0, 5.0]	7

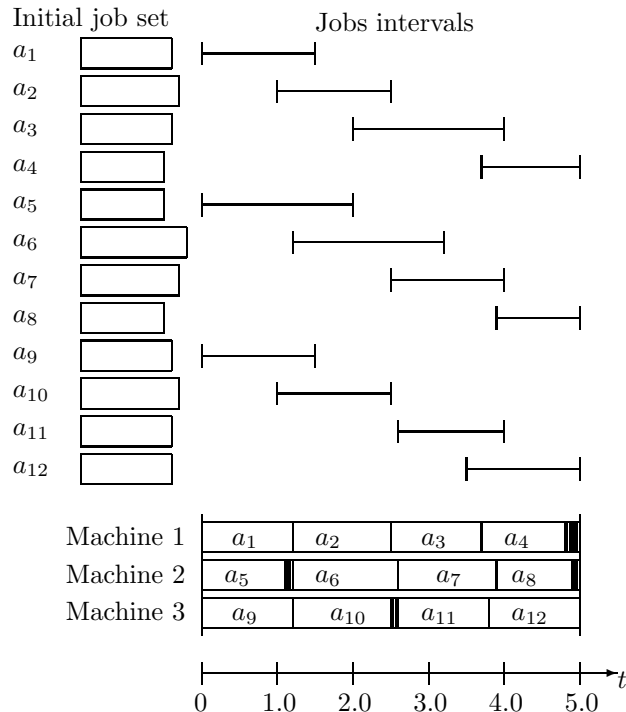
**Fig. 3.** Illustration for three-machine scheduling

Table 6. Data for examples of interval scheduling

No.	Job a_i	Processing time $\theta(a_i)$	Processing interval $\lambda^{a_i} = [t_1^{a_i}, t_2^{a_i}]$	Number of machine	Position in schedule
1.	a_1	1.2	[0.0, 1.5]	1	1
2.	a_2	1.3	[1.0, 2.5]	1	2
3.	a_3	1.2	[2.0, 4.0]	1	3
4.	a_4	1.1	[3.7, 5.0]	1	4
5.	a_5	0.7	[0.0, 2.0]	2	1
6.	a_6	0.6	[1.7, 2.7]	2	2
7.	a_7	0.7	[2.5, 4.0]	2	3
8.	a_8	1.0	[3.9, 5.0]	2	4
9.	a_9	1.2	[0.0, 1.5]	3	1
10.	a_{10}	1.3	[1.0, 2.5]	3	2
11.	a_{11}	1.2	[2.6, 4.0]	3	3
12.	a_{12}	1.2	[3.0, 5.0]	3	4

6. minimizing the weighted number of early and tardy jobs in scheduling (e.g., [69]),
7. maximum deviation in JIT scheduling problems (e.g., [21,149,177]),
8. minimization of the sum of weighted mean squared deviation of the completion times (e.g., [149]),
9. minimizing variation of production rates in JIT systems (e.g., [94])
10. minimization of the expected number of tardy jobs in scheduling (e.g., [41]),
11. minimization of expected costs for earliness and tardy jobs in scheduling (e.g., [23]).

In recent years, multicriteria JIT-like scheduling problems are under examination (i.e., combination of the objective functions above are used) (e.g., [17,63,182,192,203]).

It may be reasonable to present an example of basic problem formulations as follows. Let jobs (tasks) $A = \{a_1, \dots, a_i, \dots, a_n\}$ are non-preemptive and are scheduled on m identical machines (processors) $P = \{P_1, \dots, P_j, \dots, P_m\}$. Each P_j can handle at most one job at a time, each a_i can be completely processed on any machine. Each job a_i has parameters: (a) processing time $\theta(a_i)$, (b) a time interval (i.e., window) for its processing $\lambda^{a_i} = [t_1^{a_i}, t_2^{a_i}]$, (c) completion time in a solution S (i.e., a schedule) $C(a_i)$, (d) earliness $u(a_i) = \max\{0, t_1^{a_i} - C(a_i)\}$, (e) tardiness $v(a_i) = \max\{0, C(a_i) - t_2^{a_i}\}$. In addition, values of non-negative costs (penalties) of earliness and tardiness are given: $\alpha u(a_i)$ and $\beta v(a_i)$, respectively. The problem is (for sum of penalties):

Find a schedule S such that $F^{sum}(S) = \sum_{i=1}^n [\alpha u(a_i) + \beta v(a_i)]$ is minimized.

In the case of maximum total penalty, the objective function is:
to minimize $F^{max}(S) = \max_{1 \leq i \leq n} \{\alpha u(a_i), \beta v(a_i)\}$

In addition, it is necessary to point out combinatorial optimization models which are close to (or are used in) JIT-like scheduling problems: k -coloring, maximum weight clique, assignment/allocation, timetabling, maximum weight independent set, weighted matching (e.g., [88,122,152]).

Some simplified special JIT scheduling/planning models can be solvable by polynomial algorithms (e.g., [26,73,144,184,185,188,191]) or PTAS/FPTAS (e.g., [78,82,87,185]). In the main, the models are NP-hard (e.g., [44,45,63,73,83,148,182]) and, as a result, the following solving approaches are used: (i) enumerative methods (e.g., branch-and-bound and dynamic programming algorithms (e.g., [10,83,126]), (ii) various heuristics/metaheristics (local optimization, VNS methods, evolutionary algorithms, etc.) (e.g., [97,154]). Analogical situation (i.e., usage of enumerative algorithms and/or heuristics) exists in the filed of multicriteria JIT scheduling problems (e.g., [17,182]).

In recent decades, due-data (due-window) assignment scheduling problems have been intensively studied (Table 7, Table 8). Here, it is reasonable to point out the basic surveys [11,54,55,73,79,98]. The situation with problem complexities and the used solving methods is analogical (as it was pointed out for JIT scheduling).

Table 7. Some studies in scheduling with due-date assignment, part 1

No.	Issue(s)	Source(s)
1.	Surveys:	
1.1.	Due date quotation models and algorithms	[79]
1.2.	Survey of the state-of-the-art of common due-date assignment and scheduling	[54]
1.3.	Scheduling with due date assignment (survey)	[55]
1.4.	Scheduling with common due date, earliness and tardiness penalties for multiple machine problems	[98]
2.	Due dates assignment and JIT scheduling with unit-time or equal-size jobs:	
2.1.	Minmax earliness-tardiness costs with unit processing time jobs	[135]
2.2.	Minimizing weighted earliness-tardiness and due date cost with unit-time jobs	[138]
2.3.	Scheduling of unit-time jobs distinct due windows on parallel processors	[69]
2.4.	Due dates assignment and JIT scheduling with equal-size jobs	[186]
2.5.	Minimizing earliness, tardiness, and due-date costs for equal-sized jobs	[112]
2.6.	Minimization of earliness, tardiness and due date penalties on uniform parallel machines with identical jobs	[39]
3.	Single machine due-date assignment problems:	
3.1.	Assigning a common due-date for all the jobs (CON),	[11,54,169]
3.2.	Assigning job-dependent due-dates which are (linear) functions of the job processing times (SLK)	[52,53,68] [80,191]
3.3.	Assigning job-dependent due-dates which are penalized if exceed prespecified deadlines (DIF)	[162,166,167]
3.4.	Assigning generalized due dates (GDD)	[59,137,176]
3.5.	Minmax due-date assignment problem with lead-time cost	[133]
3.6.	Common due date assignment to minimize total penalty for the one machine scheduling problem	[147]
3.7.	Single-machine scheduling problems involving due date determination decisions	[201]
3.8.	Stochastic single machine scheduling with proportional job weights to minimize deviations of completion times from a common due date	[74]
4.	Common due-date assignment and scheduling:	
4.1.	Survey of the state-of-the-art of common due-date assignment and scheduling	[54]
4.2.	Assigning a common due-date for all the jobs (CON),	[11,54,169]
4.3.	Scheduling to a common due-date on parallel uniform processors	[42]
4.4.	Common due date assignment to minimize total penalty for one machine scheduling	[147]
4.5.	Scheduling around a small common due date	[4,62]
4.6.	Common due date assignment with generalized earliness/tardiness penalties	[86]
4.7.	Single machine scheduling with different ready times and common due date	[16]
4.8.	Single machine weighted earliness-tardiness penalty problem with a common due date	[129]
4.9.	Unrelated parallel machine scheduling with a common due date, release dates, and linear earliness and tardiness penalties	[12]
4.10.	Common due date assignment and scheduling with ready times	[30]
4.11.	Two-machine flow shop scheduling for the minimization of the mean absolute deviation from a common due date	[160]
4.12.	Scheduling on parallel identical machines to minimize weighted earliness-tardiness penalties with respect to a common due date	[7]
5.	Stochastic/uncertain scheduling with due dates:	
5.1.	Sequencing stochastic jobs on a single machine with a common due date and stochastic processing times	[161]
5.2.	Single machine scheduling with stochastic processing times or stochastic due-dates to minimize the number of early and tardy jobs	[172]
5.3.	Stochastic single machine scheduling to minimize the weighted number of early and tardy jobs (random processing time, due dates)	[173]
5.4.	Stochastic single machine scheduling with random common due date	[15]
5.5.	Stochastic single machine scheduling with proportional job weights to minimize deviations of completion times from a common due date	[74]
5.6.	Stochastic scheduling with release dates and due dates	[151,152]
5.7.	Scheduling stochastic jobs with due dates on parallel machines	[43]
5.8.	Fuzzy due-date scheduling problem with fuzzy processing times	[77]

Table 7. Some studies in scheduling with due-date assignment, part 2

No.	Issue(s)	Source(s)
6.	Special problems:	
6.1.	Group scheduling and due date assignment	[113]
6.2.	Due-date assignment on uniform machines	[141]
6.3.	Optimal coordination of resource allocation, due date assignment in scheduling	[170]
6.4.	Single machine multiple common due dates scheduling with learning effects	[190]
6.5.	Multiple common due dates assignment and scheduling problems with resource allocation and general position-dependent deterioration effect	[196]
6.6.	Dynamic due-date assignment models in flexible manufacturing systems	[76]

Table 8. Some studies in scheduling with due-window assignment

No.	Issue(s)	Source(s)
1.	Surveys:	
1.1.	Survey on scheduling problems with due windows	[73]
1.2.	Common due-window scheduling problems	[71,89]
1.3.	Due-window scheduling for parallel machines	[90]
1.4.	Minmax scheduling problems with a common due-window	[142]
2.	Single-machine scheduling with a common due window:	
2.1.	Single-machine scheduling with a common due window assignment	[67,144,198]
2.2.	Determination of common due window location in single machine scheduling	[114,116]
2.3.	Single machine scheduling problem with common due window and controllable processing times	[115]
2.4.	Single-machine due window assignment and scheduling with a common allowance and controllable job processing time	[202]
3.	Due-window assignment problems with unit-time (or equal) jobs:	
3.1.	Due-window assignment problems with unit-time jobs	[46,48]
3.2.	Due-window assignment with identical jobs on parallel uniform machines	[47]
3.3.	Due-window assignment with unit processing time jobs	[136]
3.4.	Soft due-window assignment and scheduling of unit-time jobs on parallel machines	[70]
4.	Scheduling with a common due window:	
4.1.	Common due-window scheduling	[89]
4.2.	Minmax scheduling problems with a common due-window	[142]
4.3.	Two-stage flow shop earliness and tardiness machine scheduling involving a common due window	[199]
4.4.	Two-machine flow shop scheduling with a common due window to minimize weighted number of early and tardy jobs	[200]
4.5.	Parallel machine scheduling with common due-windows	[65]
4.6.	Parallel machine scheduling and common due window assignment with job independent earliness and tardiness costs	[72]
5.	Special problems:	
5.1.	Due-window assignment problem with position-dependent processing times	[140]
5.2.	Due-window scheduling for parallel machines	[90]
5.3.	Flexible job shop scheduling with due window	[66]
5.4.	Due window assignment and resource allocation scheduling problems with learning and general positional effects	[118]
5.5.	Scheduling a maintenance activity and due-window assignment	[134]
5.6.	Scheduling problems with multiple due windows assignment	[197]
5.7.	Dynamic window-constrained scheduling of real-time streams in media servers	[194]
5.8.	Multi-criteria scheduling with due-window assignment problem	[139]
6.	Soft due-window assignment and scheduling:	
6.1.	Soft due-window assignment and scheduling on parallel machines	[68]
6.2.	Soft due-window assignment and scheduling of unit-time jobs on parallel machines	[70]

3. Time-interval balancing scheduling of modular jobs

It is assumed a three-stage system: production stage (manufacturing of a basic module set), transportation (transmission) stage, and utilization (e.g., assembly) stage. The problem consists in scheduling of composite jobs at the third stage while taking into account balance constraints of the first stage and the second stage. Note, the main goal consists in deletion of a buffer-based subsystem (as in JIT approaches) or to use a very simplified buffer-based subsystem.

First, an illustration example is described (Fig. 4). There is a set of five basic elements (details, building elements, elementary jobs, modules): $\bar{\Delta} = \{\Delta_1, \Delta_2, \Delta_3, \Delta_4, \Delta_5\}$. The elements are produced by corresponding five manufacturing organizations (e.g., producers, conveyors). The system is targeted to use (e.g., to assembly) of a specified set of four composite modular jobs (as module chains or typical modular building): $a_1 = \langle \Delta_1 \rightarrow \Delta_2 \rightarrow \Delta_3 \rangle$, $a_2 = \langle \Delta_2 \rightarrow \Delta_5 \rangle$, $a_3 = \langle \Delta_1 \rightarrow \Delta_2 \rightarrow \Delta_4 \rightarrow \Delta_5 \rangle$, $a_4 = \langle \Delta_1 \rightarrow \Delta_2 \rightarrow \Delta_2 \rightarrow \Delta_3 \rightarrow \Delta_4 \rightarrow \Delta_5 \rangle$.

In the example, the system assembly process is executed by three processors/teams (Fig. 4). The system plan (general schedule) consists of schedules for three processors (machines, teams) $S = \{S_1, S_2, S_3\}$, where a_0 denotes an “empty” element/time period: (i) team (processor) P_1 : $S_1 = \langle a_4 \rightarrow a_4 \rangle$, (ii) team (processor) P_2 : $S_2 = \langle a_2 \rightarrow a_0 \rightarrow a_3 \rightarrow a_0 \rightarrow a_3 \rangle$, and (iii) team (processor) P_3 : $S_3 = \langle a_3 \rightarrow a_1 \rightarrow a_3 \rightarrow a_0 \rangle$.

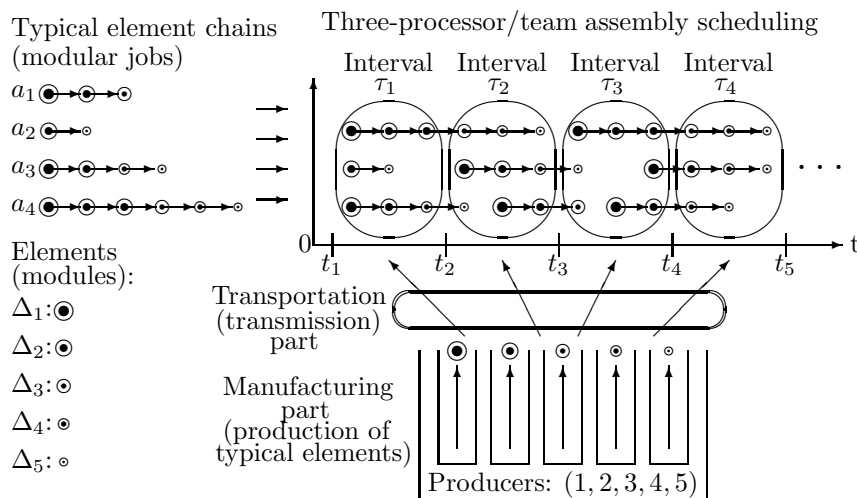


Fig. 4. Multi-processor schedule (interval balance by element structure)

The basic requirement for the general schedule S is targeted to designing the assembly schedule with balanced (by element/module structure) time intervals, here: $\tau_1 = [t_1, t_2]$, $\tau_2 = [t_2, t_3]$, $\tau_3 = [t_3, t_4]$, $\tau_4 = [t_4, t_5]$. At each time interval, elements are used (additional 6th “empty” element type is used Δ_6 , the type corresponds to “empty” element/time period a_0):

- (1) $X_{\tau_1} = \{\Delta_1, \Delta_1, \Delta_2, \Delta_2, \Delta_2, \Delta_2, \Delta_3, \Delta_5, \Delta_6\}$,
- (2) $X_{\tau_2} = \{\Delta_1, \Delta_1, \Delta_2, \Delta_2, \Delta_3, \Delta_4, \Delta_4, \Delta_5, \Delta_5\}$,
- (3) $X_{\tau_3} = \{\Delta_1, \Delta_1, \Delta_1, \Delta_2, \Delta_2, \Delta_2, \Delta_3, \Delta_5, \Delta_6\}$,
- (4) $X_{\tau_4} = \{\Delta_2, \Delta_3, \Delta_4, \Delta_4, \Delta_4, \Delta_5, \Delta_5, \Delta_5, \Delta_6\}$.

Evidently, the clustering solution is: $\tilde{X}(S) = \{X_{\tau_1}, X_{\tau_2}, X_{\tau_3}, X_{\tau_4}\}$.

The corresponding multiset estimates are (by number of basic element types [102,103]):

$$e(X_{\tau_1}) = (2, 4, 1, 0, 1, 1), e(X_{\tau_2}) = (2, 2, 1, 2, 2, 0), e(X_{\tau_3}) = (3, 3, 1, 0, 1, 1), e(X_{\tau_4}) = (0, 1, 1, 3, 3, 1).$$

The basic reference multiset estimate has to be in correspondence to an output structure (i.e., productivity) of the manufacturing (production) system (while taking into account transportation system), for example: $e_0 = (2, 3, 2, 1, 1, 0)$.

The proximity between multiset estimates ($\delta(e_0, e(X_{\tau_i}))$, $i = \overline{1, 4}$) are shown in Table 9.

Reference estimate	Cluster estimate:	$e(X_{\tau_1}) = (2, 4, 1, 0, 1, 1)$	$e(X_{\tau_2}) = (2, 2, 1, 2, 2, 0)$	$e(X_{\tau_3}) = (3, 3, 1, 0, 1, 1)$	$e(X_{\tau_4}) = (0, 1, 1, 3, 3, 1)$
$e_0 = (2, 3, 2, 1, 1, 0)$		3	3	4	15

Generally, the set of processors/team is $P = \{P_1, \dots, P_\xi, \dots, P_m\}$. The scheduling problem is:

Find the general schedule S and corresponding clustering solution $\tilde{X}(S) = \{X_{\tau_1}, X_{\tau_2}, X_{\tau_3}, \dots, X_{\tau_k}\}$ such that (i) the number of time intervals (the number k), the length of schedule, makespan) is minimized, (ii) proximity between each interval element structure and reference structure is limited (i.e., $\max_{\iota=1, \dots, k} \delta(e_0, e(X_{\tau_\iota})) \leq \delta^0$, δ^0 is a joint constraint of manufacturing and transportation part).

The general formal model is as follows (here: m processor/teams, $L(S) = k$):

$$\min L(S) = \max_{\xi=1, \dots, m} L(S_\xi) \quad s.t. \quad \max_{\iota=1, \dots, k} \delta(e_0, e(X_{\tau_\iota})) \leq \delta^0.$$

In the considered numerical example, $L(S) = 4$, $\widehat{B}(\tilde{X}(S)) = 4$.

An illustration of the examined hierarchy is depicted in Fig. 5.

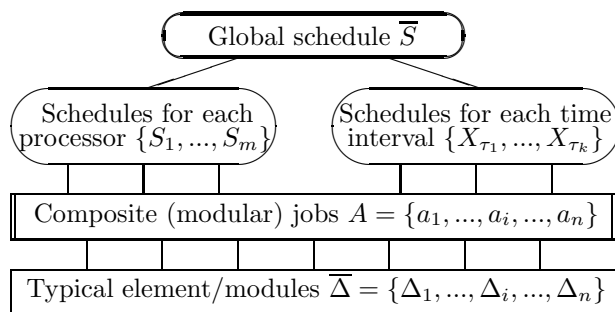


Fig. 5. Hierarchy of examined components

Clearly, many kinds (versions) of the proposed problem can be examined (e.g., various scales for the parameters estimates, various objective functions, various constraints, various levels of uncertainty). The described problem types can be useful for planning several domains: manufacturing systems, home-building systems, logistics (supply chain management), information transmission systems.

In addition, it is reasonable to point out the following notes:

Note 1. It is possible to examine various model formulations for the above-mentioned problem (i.e., various constraints, various objective functions).

Note 2. The problems of the considered kind are very complicated, i.e., NP-hard (outside some simplified cases). Evidently, additional studies of the problem complexities have to be conducted.

Note 3. Various heuristics and metaheuristics can be considered as prospective ones as the solving schemes for the problem above.

4. Time-interval balanced planning in modular house-building

4.1. Life-cycle and home-building conveyor

In general, the life cycle of home-building can be considered as the following chain of phases (Fig. 6):

0. Preliminary phase: analysis of requirements to the building, land planning, analysis of the building functionality, geological exploration, etc.

1. Ideation and design phase: (1.1) architectural design (generation of the basic architectural ideas), (1.2) construction design (real design stage to prepare design documentation).

2. Manufacturing phase: manufacturing of building details and components.

3. Transportation and assembly phase: (3.1) transportation of building components to the assembly place, (3.2) assembly of the building.

4. Utilization phase: utilization including maintenance.

5. Recycling phase: (5.1) destruction of the building, (5.2) recycling of the building components.

Modern industrial technology for modular homebuilding provides faster and lower cost building process (e.g., [99,145]). In 1980, a new system of big structural panel based homebuilding in Moscow has been suggested [119,155]. The homebuilding system was based on catalogue big structural panel elements (“method KOPE”). In the homebuilding system, a coordination (i.e., balancing) between structural panel manufacturing stage and homebuilding (assembly) stage was a bottleneck. Here, the material is targeted to the coordination above (i.e., the bottleneck). The considered planning approach is based on a real-world home-building conveyor (DSK-2, Ochakovo/Moscow, 1982) (Fig. 7) [100]:

I. Architectural part: 1.1. general architectural design, 1.2. construction design.

II. Production part: 2.1. manufacturing system (industry based manufacturing of home details-modules/structural panels), 2.2. transportation system (transportation of the details/modules to home places), 2.3. assembly systems (assembly of the building from the details/modules).

Note, preliminary stages for the conveyor involve land planning, geological exploration, etc.




Fig. 6. Scheme of general home-building life cycle




Fig. 7. Scheme of home-building conveyor (Moscow, 1982)

The result of the conveyor consists in building(s). Here, the manufacturing system is the most capitalized component of the conveyor. Thus, conveyor components as transportation and assembly have to be time-balanced (i.e., about synchronized) on the basis of time-productivity of manufacturing part. Buffers between manufacturing part and assembly is not reliable and conveyor is based on the principle “just-in-time” [56,75,130,153]. The real world time requirement (i.e., time constraint) for store of module/detail between transportation system and assembly is: \leq three days.

Finally, the examined planning problem of assembly of modular buildings is targeted to designing a balanced assembly process (i.e., time-synchronized with manufacturing process) where time unbalance is for each module/detail is \leq three days.

Further, a problem of balanced planning in house-building is examined. The problem description is based in the designed and implemented applied software planning system [100]. In general, the system involves three stages (Fig. 8): (i) manufacturing of typical building modules (details, elements, structural panels); (ii) transportation of the elements to areas of house-building (with very small buffers); and (iii) assembly of buildings. Note, the small buffers require organizational decisions as quasi “just-in-time”.

In homebuilding systems, a real time interval can be equal to one week or to ten days. In the next section (in the numerical example), the considered time interval equals one month (for simplification).




Fig. 8. Scheme of manufacturing and house-building

4.2. Real world illustrative numerical example

In this section, a realistic numerical example of a two-year plan for home-building conveyor is described (“method KOPE”, Moscow home-building system, DSK-2, Ochakovo/Moscow, 1982..1983) [100]. The example is based on FORTRAN-software that was designed by the author [100].

The following basic architectural sections (the structural modules correspond to building “column”) are used:

- (a) catalogue structural elements (corresponding to apartment): g_1, g_2, g_5, g_9 ;
- (b) composition elements (for connection of the sections) w_1, w_2, w_3, w_6, w_7 .

The following basic types of structural details (manufacturing stage) are considered: (1) literal walls (panels) d_1 , (2) separation walls (panels) for 1-st floor d_2 , (3) separation walls (panels) (2nd floor and so on) d_3 , (4) floor panels (intermediate slabs, floor slab panels) d_4 , (5) roof panels (slubs, cover bulkheads) d_5 , (6) fliers (stair flights) d_6 , (7) elements of blocks and engineering communication d_7 , (8) balcony elements d_8 . Note, real set of the basic structural details in “method KOPE” involves about 500 elements, but for the balancing problem the above-mentioned 8 basic integrated types (groups). Note, detail d_1 corresponds to the main structural detail while taking into account production subsystem because production of d_1 is the basic manufacturing process (by cost and by time). As a result, the number of the required details of this kind defines (mainly) the balance between the production stage and the assembly stage.

Here, the following typical floors are examined: (i) crawl space r_1 , (2) floor 1 r_2 , (3) bottom floor r_3 , (4) medium floor r_4 , (5) top floor r_5 , (6) next floor r_6 , (7) the upper storey r_7 , and (8) engineering storey (mechanical floor) r_8 . The construction hierarchy (i.e., hierarchical system) of structural panels-buildings is depicted in Fig. 9.

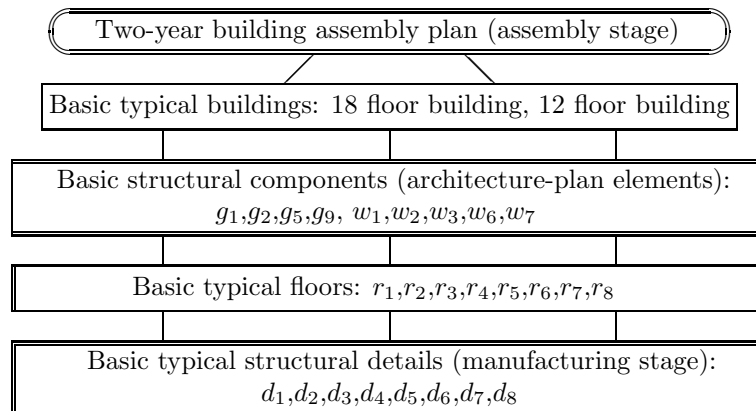


Fig. 9. Construction hierarchy: structural panels-buildings

The examined problem consists in coordination (balancing) between two stages:

1. assembly stage (i.e., two-year building assembly plan) and
2. production stage (i.e., requirements of basic typical structural details).

The suggested heuristic solving scheme for coordination (balancing) of assembly stage and production stage is based on correction of a generated initial schedule (solution) (Fig. 10).

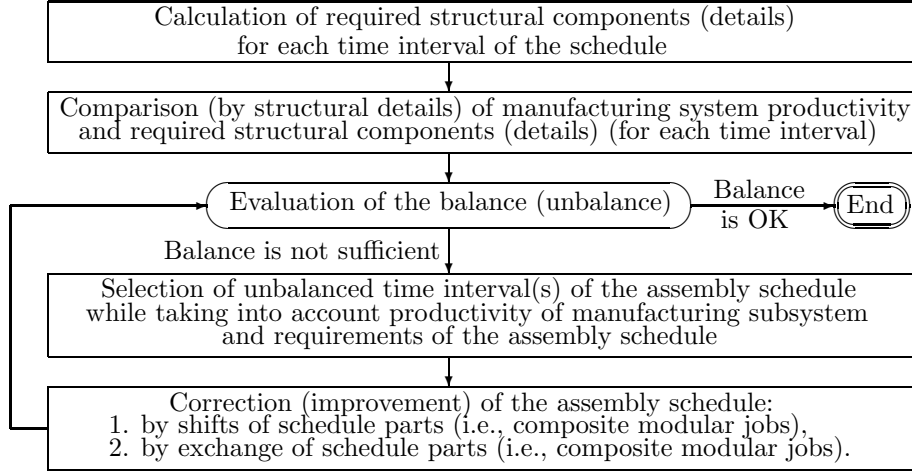


Fig. 10. Heuristic solving scheme for coordination/balancing

Table 10 contains configurations of the considered 18-floor building and 22-floor building by the typical floors (i.e., binary relation $R^{buil,r}$). An illustration of the relationships of the examined objects is depicted in Fig. 11. Further, the weighted binary relations (correspondences) $R^{r,d}$, $R^{a,g&w}$, $R^{r,g&w}$, $R^{\tau,r}$, $R^{\tau,d}$, are presented in tables. In the considered planning problem, relation $R^{\tau,d}$ is the basic one.

Table 10. Configuration of typical building by typical floors

No.	Typy of building	Typical floor:	r_1	r_2	r_3	r_4	r_5	r_6	r_7	r_8
1.	18-floor building		0	1	0	11	5	1	1	1
1.	22-floor building		0	1	4	11	5	1	1	1

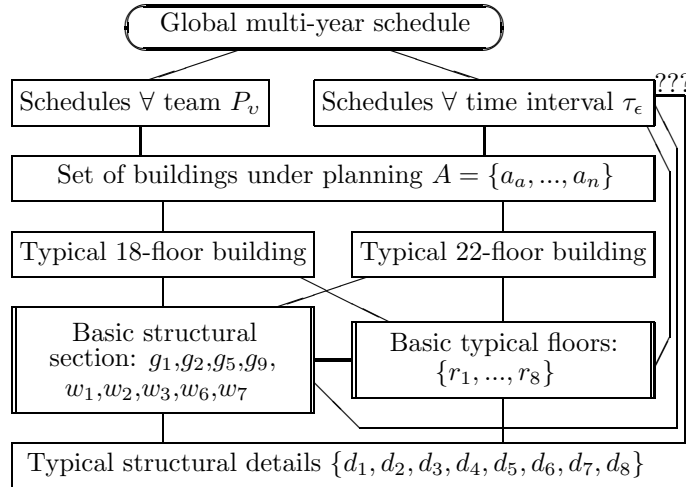


Fig. 11. Relationships of examined components

Correspondences between typical floors and basic types of structural details (manufacturing stage) for each structural section are pointed out in the following tables: (1) for structural section g_1 (Table 11), (2) for structural section g_2 (Table 12), (3) for structural section g_5 (Table 13), (4) for structural section g_9 (Table 14), (5) for structural section w_1 (Table 15), (6) for structural section w_2 (Table 16), (7) for

Table 21. Configuration of buildings by typical sections

Building	g_1	g_2	g_5	g_9	w_1	w_2	w_3	w_6	w_7
a_1	2	1	1	0	3	0	4	0	0
a_2	0	2	0	1	1	1	4	0	1
a_3	1	1	1	0	2	0	4	0	0
a_4	0	1	1	1	1	1	6	0	0
a_5	0	1	1	2	1	2	8	0	0
a_6	2	1	1	0	1	1	4	0	0
a_7	1	1	0	1	1	1	5	0	1
a_8	1	1	1	1	2	1	6	0	0
a_9	1	1	1	2	2	2	7	0	0

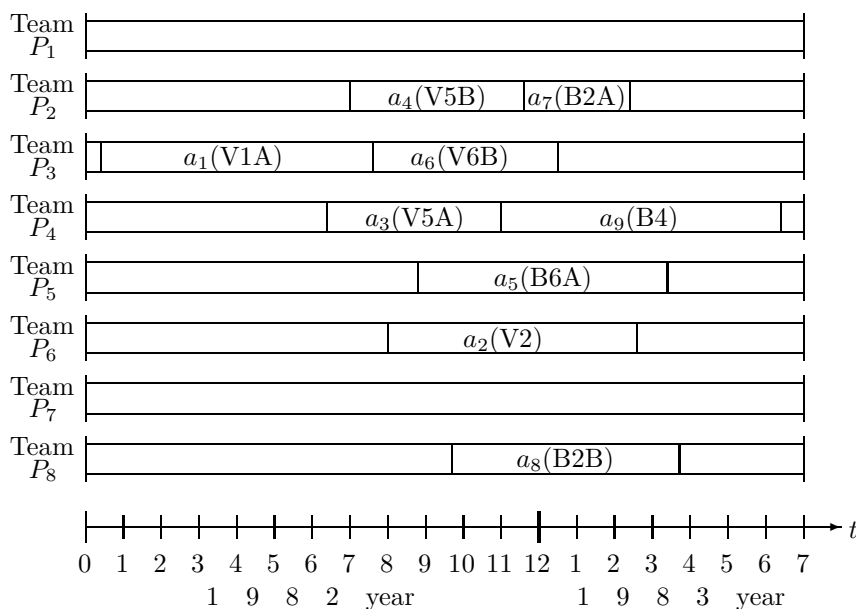
Fig. 12. Initial eight-processor schedule for assembly of buildings S^0

Table 22 contains the required structural sections for each month of the above-mentioned schedule.

Table 22. Requirements of structural sections in schedule (for each month)

No.	Month	g_1	g_2	g_5	g_9	w_1	w_2	w_3	w_6	w_7
1.	1/1982	0.091	0.045	0.045	0.0	0.136	0.0	0.182	0.0	0.0
2.	2/1982	0.182	0.091	0.091	0.0	0.273	0.0	0.364	0.0	0.0
3.	3/1982	0.182	0.091	0.091	0.0	0.273	0.0	0.364	0.0	0.0
4.	4/1982	0.182	0.091	0.091	0.0	0.273	0.0	0.364	0.0	0.0
5.	5/1982	0.182	0.091	0.091	0.0	0.273	0.0	0.364	0.0	0.0
6.	6/1982	0.182	0.091	0.091	0.0	0.273	0.0	0.364	0.0	0.0
7.	7/1982	0.274	0.183	0.183	0.0	0.456	0.0	0.731	0.0	0.0
8.	8/1982	0.365	0.447	0.447	0.172	0.812	0.172	2.131	0.0	0.0
9.	9/1982	0.365	0.800	0.478	0.396	1.004	0.396	3.024	0.0	0.161
10.	10/1982	0.324	1.095	0.772	0.693	1.257	0.693	4.796	0.0	0.161
11.	11/1982	0.345	1.328	1.006	0.818	1.512	0.818	5.976	0.0	0.161
12.	12/1982	0.350	1.290	0.909	1.078	1.421	1.078	6.163	0.0	0.219
13.	1/1983	0.524	1.169	0.614	1.124	1.299	1.124	5.594	0.0	0.394
14.	2/1983	0.524	1.002	0.447	1.124	1.133	1.124	4.927	0.0	0.394
15.	3/1983	0.524	0.774	0.447	0.995	1.003	0.995	4.411	0.0	0.265
16.	4/1983	0.492	0.530	0.298	0.697	0.789	0.697	3.155	0.0	0.233
17.	5/1983	0.140	0.140	0.128	0.267	0.267	0.267	0.953	0.0	0.012
18.	6/1983	0.128	0.128	0.128	0.256	0.256	0.256	0.895	0.0	0.0
19.	7/1983	0.100	0.100	0.100	0.199	0.199	0.199	0.698	0.0	0.0

Further, requirements of typical floors for each plan month are presented:

- (1) requirements of typical floors via g_1 (Table 23),
- (2) requirements of typical floors via g_2 (Table 24),
- (3) requirements of typical floors via g_5 (Table 25),
- (4) requirements of typical floors via g_9 (Table 26),
- (5) requirements of typical floors via w_1 (Table 27),
- (6) requirements of typical floors via w_2 (Table 28),
- (7) requirements of typical floors via w_3 (Table 29),
- (8) requirements of typical floors via w_6 (Table 30), and
- (9) requirements of typical floors via w_7 (Table 31).

Table 23. Requirements of typical floors via g_1

No.	Month	Typical floor:	r_1	r_2	r_3	r_4	r_5	r_6	r_7	r_8
1.	1/1982		0.0	2.0	0.0	0.1	0.0	0.0	0.0	0.0
2.	2/1982		0.0	0.0	0.0	4.2	0.0	0.0	0.0	0.0
3.	3/1982		0.0	0.0	0.0	4.2	0.0	0.0	0.0	0.0
4.	4/1982		0.0	0.0	0.0	4.2	0.0	0.0	0.0	0.0
5.	5/1982		0.0	0.0	0.0	4.2	0.0	0.0	0.0	0.0
6.	6/1982		0.0	0.0	0.0	4.2	0.0	0.0	0.0	0.0
7.	7/1982		0.0	1.0	0.0	1.9	3.4	0.0	0.0	0.0
8.	8/1982		0.0	0.0	0.0	4.3	4.2	0.0	0.0	0.0
9.	9/1982		0.0	0.0	0.0	4.3	2.3	1.9	0.0	0.0
10.	10/1982		0.0	1.0	0.1	1.3	2.9	0.1	2.0	2.0
11.	11/1982		0.0	0.1	3.8	0.0	2.1	1.0	1.0	1.0
12.	12/1982		0.0	1.9	2.5	3.7	0.0	0.0	0.0	0.0
13.	1/1983		0.0	0.0	5.6	6.5	0.0	0.0	0.0	0.0
14.	2/1983		0.0	0.0	0.0	11.8	0.2	0.0	0.0	0.0
15.	3/1983		0.0	0.0	0.0	6.9	5.2	0.0	0.0	0.0
16.	4/1983		0.0	0.0	0.0	2.9	4.6	2.0	2.0	1.1
17.	5/1983		0.0	0.0	0.0	1.2	1.8	0.0	0.0	0.9
18.	6/1983		0.0	0.0	0.0	0.0	2.9	0.0	0.0	0.0
19.	7/1983		0.0	0.0	0.0	0.0	0.3	1.0	1.0	0.0

Table 24. Requirements of typical floors via g_2

No.	Month	Typical floor:	r_1	r_2	r_3	r_4	r_5	r_6	r_7	r_8
1.	1/1982		0.0	1.0	0.0	0.1	0.0	0.0	0.0	0.0
2.	2/1982		0.0	0.0	0.0	2.1	0.0	0.0	0.0	0.0
3.	3/1982		0.0	0.0	0.0	2.1	0.0	0.0	0.0	0.0
4.	4/1982		0.0	0.0	0.0	2.1	0.0	0.0	0.0	0.0
5.	5/1982		0.0	0.0	0.0	2.1	0.0	0.0	0.0	0.0
6.	6/1982		0.0	0.0	0.0	2.1	0.0	0.0	0.0	0.0
7.	7/1982		0.0	1.0	0.0	1.5	1.7	0.0	0.0	0.0
8.	8/1982		0.0	1.0	0.0	7.3	2.1	0.0	0.0	0.0
9.	9/1982		0.0	2.7	5.4	8.3	1.2	0.9	0.0	0.0
10.	10/1982		0.0	2.3	8.8	10.2	2.9	0.1	1.0	1.0
11.	11/1982		0.0	0.1	5.7	16.8	6.1	1.0	1.0	1.0
12.	12/1982		0.0	1.9	2.5	19.2	4.2	1.0	1.0	1.0
13.	1/1983		0.0	0.0	5.6	12.3	6.9	1.0	1.0	1.0
14.	2/1983		0.0	0.0	0.0	12.9	7.7	2.0	0.7	0.0
15.	3/1983		0.0	0.0	0.0	6.9	7.6	1.0	1.4	2.0
16.	4/1983		0.0	0.0	0.0	2.9	4.6	2.0	2.8	2.1
17.	5/1983		0.0	0.0	0.0	1.2	1.8	0.0	0.0	0.9
18.	6/1983		0.0	0.0	0.0	0.0	2.9	0.0	0.0	0.0
19.	7/1983		0.0	0.0	0.0	0.0	0.3	1.0	1.0	1.0

Table 25. Requirements of typical floors via g_5

No.	Month	Typical floor:	r_1	r_2	r_3	r_4	r_5	r_6	r_7	r_8
1.	1/1982		0.0	1.0	0.0	0.1	0.0	0.0	0.0	0.0
2.	2/1982		0.0	0.0	0.0	2.1	0.0	0.0	0.0	0.0
3.	3/1982		0.0	0.0	0.0	2.1	0.0	0.0	0.0	0.0
4.	4/1982		0.0	0.0	0.0	2.1	0.0	0.0	0.0	0.0
5.	5/1982		0.0	0.0	0.0	2.1	0.0	0.0	0.0	0.0
6.	6/1982		0.0	0.0	0.0	2.1	0.0	0.0	0.0	0.0
7.	7/1982		0.0	1.0	0.0	1.5	1.7	0.0	0.0	0.0
8.	8/1982		0.0	1.0	0.0	7.3	2.1	0.0	0.0	0.0
9.	9/1982		0.0	0.7	0.0	8.3	1.2	0.9	0.0	0.0
10.	10/1982		0.0	2.3	6.2	5.3	2.9	0.1	1.0	1.0
11.	11/1982		0.0	0.1	5.7	9.3	6.1	1.0	1.0	1.0
12.	12/1982		0.0	0.9	2.2	11.7	4.2	1.0	1.0	1.0
13.	1/1983		0.0	0.0	1.9	8.3	1.8	1.0	1.0	1.0
14.	2/1983		0.0	0.0	0.0	7.5	2.8	0.0	0.0	0.0
15.	3/1983		0.0	0.0	0.0	2.9	6.2	1.0	0.2	0.0
16.	4/1983		0.0	0.0	0.0	2.9	1.0	1.0	1.8	2.0
17.	5/1983		0.0	0.0	0.0	1.2	1.8	0.0	0.0	0.0
18.	6/1983		0.0	0.0	0.0	0.0	2.9	0.0	0.0	0.0
19.	7/1983		0.0	0.0	0.0	0.0	0.3	1.0	1.0	1.0

Table 26. Requirements of typical floors via g_9

No.	Month	Typical floor:	r_1	r_2	r_3	r_4	r_5	r_6	r_7	r_8
1.	1/1982		0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
2.	2/1982		0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
3.	3/1982		0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
4.	4/1982		0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
5.	5/1982		0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
6.	6/1982		0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
7.	7/1982		0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
8.	8/1982		0.0	1.0	0.0	3.0	0.0	0.0	0.0	0.0
9.	9/1982		0.0	2.4	2.7	4.0	0.0	0.0	0.0	0.0
10.	10/1982		0.0	1.6	8.0	6.4	0.0	0.0	0.0	0.0
11.	11/1982		0.0	0.2	5.2	9.2	4.0	0.0	0.0	0.0
12.	12/1982		0.0	2.8	4.6	14.5	1.0	1.0	1.0	1.0
13.	1/1983		0.0	0.0	7.5	15.7	2.5	0.0	0.0	0.0
14.	2/1983		0.0	0.0	0.0	16.8	7.7	1.0	0.4	0.0
15.	3/1983		0.0	0.0	0.0	9.8	10.1	2.0	0.9	1.0
16.	4/1983		0.0	0.0	0.0	5.9	4.6	2.0	3.7	3.1
17.	5/1983		0.0	0.0	0.0	2.4	3.5	0.0	0.0	0.9
18.	6/1983		0.0	0.0	0.0	0.0	5.9	0.0	0.0	0.0
19.	7/1983		0.0	0.0	0.0	0.0	0.6	2.0	2.0	2.0

Table 27. Requirements of typical floors via w_1

No.	Month	Typical floor:	r_1	r_2	r_3	r_4	r_5	r_6	r_7	r_8
1.	1/1982		0.0	3.0	0.0	0.2	0.0	0.0	0.0	0.0
2.	2/1982		0.0	0.0	0.0	6.3	0.0	0.0	0.0	0.0
3.	3/1982		0.0	0.0	0.0	6.3	0.0	0.0	0.0	0.0
4.	4/1982		0.0	0.0	0.0	6.3	0.0	0.0	0.0	0.0
5.	5/1982		0.0	0.0	0.0	6.3	0.0	0.0	0.0	0.0
6.	6/1982		0.0	0.0	0.0	6.3	0.0	0.0	0.0	0.0
7.	7/1982		0.0	2.0	0.0	3.4	5.2	0.0	0.0	0.0
8.	8/1982		0.0	1.0	0.0	11.5	6.3	0.0	0.0	0.0
9.	9/1982		0.0	1.7	2.7	12.5	3.5	2.8	0.0	0.0
10.	10/1982		0.0	3.3	7.7	9.1	5.8	0.2	3.0	0.0
11.	11/1982		0.0	0.2	9.4	13.1	8.2	2.0	2.0	0.0
12.	12/1982		0.0	2.8	4.7	19.1	4.2	1.0	1.0	0.0
13.	1/1983		0.0	0.0	7.5	16.0	4.4	1.0	1.0	0.0
14.	2/1983		0.0	0.0	0.0	19.4	5.4	1.0	0.4	0.0
15.	3/1983		0.0	0.0	0.0	9.8	11.4	1.0	0.8	0.0
16.	4/1983		0.0	0.0	0.0	5.9	5.6	3.0	3.8	0.0
17.	5/1983		0.0	0.0	0.0	2.4	3.5	0.0	0.0	0.0
18.	6/1983		0.0	0.0	0.0	0.0	5.9	0.0	0.0	0.0
19.	7/1983		0.0	0.0	0.0	0.0	0.6	2.0	2.0	0.0

Table 28. Requirements of typical floors via w_2

No.	Month	Typical floor:	r_1	r_2	r_3	r_4	r_5	r_6	r_7	r_8
1.	1/1982		0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
2.	2/1982		0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
3.	3/1982		0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
4.	4/1982		0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
5.	5/1982		0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
6.	6/1982		0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
7.	7/1982		0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
8.	8/1982		0.0	1.0	0.0	3.0	0.0	0.0	0.0	0.0
9.	9/1982		0.0	2.4	2.7	4.0	0.0	0.0	0.0	0.0
10.	10/1982		0.0	1.6	8.0	6.4	0.0	0.0	0.0	0.0
11.	11/1982		0.0	0.2	5.2	9.4	4.0	0.0	0.0	0.0
12.	12/1982		0.0	2.8	4.6	14.5	1.0	1.0	1.0	0.0
13.	1/1983		0.0	0.0	7.5	15.7	2.5	0.0	0.0	0.0
14.	2/1983		0.0	0.0	0.0	16.8	7.7	1.0	0.4	0.0
15.	3/1983		0.0	0.0	0.0	9.8	10.1	2.0	0.9	0.0
16.	4/1983		0.0	0.0	0.0	5.9	4.6	2.0	3.7	0.0
17.	5/1983		0.0	0.0	0.0	2.4	3.5	0.0	0.0	0.0
18.	6/1983		0.0	0.0	0.0	0.0	5.9	0.0	0.0	0.0
19.	7/1983		0.0	0.0	0.0	0.0	0.6	2.0	2.0	0.0

The planning problem (as coordination/balancing) can be considered as the following:

Find the schedule S and corresponding $\tilde{X} = \{X_{\tau_1}, \dots, X_{\tau_\epsilon}, \dots, X_{\tau_{19}}\}$
 such that $(\gamma_{d_1}(X_{\tau_\epsilon}), \dots, \gamma_{d_s}(X_{\tau_\epsilon})) \preceq \hat{\gamma}_0 \quad \forall \tau_\epsilon = \overline{1, 19}$.

In addition, various objective functions can be taking into account.

The solving scheme may be based of correction (improvement) of the initial schedule (here it is S^0). The following types of the correction operations of the initial schedule can be considered: (i) right shift of building a_ζ in the schedule, (ii) left shift of building a_ζ in the schedule, (iii) exchange of two buildings a_{ζ_1} and a_{ζ_2} in the schedule: (a) case 1: a_{ζ_1} and a_{ζ_2} belong to the same processor schedule, (b) case 2: a_{ζ_1} and a_{ζ_2} belong to the different processor schedules.

Note, the more long building contains less part of literal walls (panels) (type d_1).

In the considered example, the possible correction operations of S^0 are pointed out in Table 56. Here, estimates of profit (i.e., usefulness for the balancing) and “cost” have only illustrative character.

Table 56. Correction operations for $S^0 \implies S'$

No. ι	Building	Change/improvement item/operation	Binary variable	Profit $c_{\iota,j}$	“Cost” $b_{\iota,j}$
1.	a_6	V_1^1 : none	$y_{1,1}$	0.0	0.0
		V_2^1 : right shift, 3 days	$y_{1,2}$	0.5	1.0
		V_3^1 : right shift, 7 days	$y_{1,3}$	1.5	2.0
		V_4^1 : right shift, 14 days	$y_{1,4}$	2.5	3.0
		V_5^1 : right shift, 21 days	$y_{1,5}$	3.5	4.0
2.	a_7	V_1^2 : none	$y_{2,1}$	0.0	0.0
		V_2^2 : right shift, 3 days	$y_{2,2}$	0.3	0.5
		V_3^2 : right shift, 7 days	$y_{2,3}$	1.0	0.8
		V_4^2 : right shift, 14 days	$y_{2,4}$	1.5	1.0
3.	a_8	V_1^3 : none	$y_{3,1}$	0.0	0.0
		V_2^3 : right shift, 7 days	$y_{3,2}$	1.5	1.0
		V_3^3 : right shift, 14 days	$y_{3,3}$	2.5	1.5
		V_4^3 : right shift, 21 days	$y_{3,4}$	3.5	2.0
4.	a_3, a_6	V_1^4 : none	$y_{4,1}$	0.0	0.0
		V_2^4 : position exchange	$y_{4,2}$	1.5	2.0

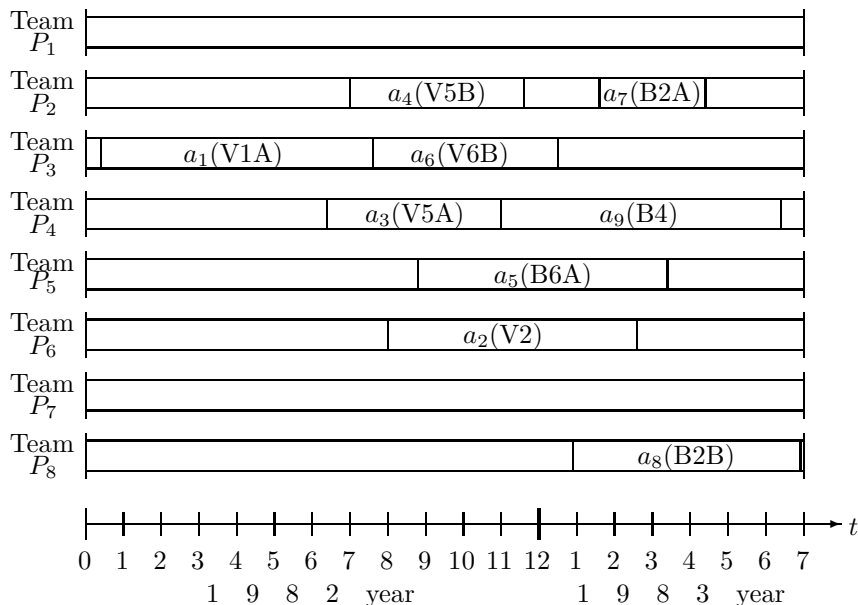


Fig. 13. New eight-processor schedule for assembly of buildings

First, it is assumed the correction operations are independent (in other case, it will be necessary to use morphological clique problem [101,102,103]). Thus, multiple choice problem can be used ($q_1 = 4, q_2 = 4, q_3 = 4, q_4 = 2$):

$$\max \sum_{\iota=1}^4 \sum_{j=1}^{q_\iota} y_{\iota,j} c_{\iota,j} \quad s.t. \quad \sum_{\iota=1}^4 \sum_{j=1}^{q_\iota} y_{\iota,j} b_{\iota,j} < b_2^{constr}, \quad \sum_{j=1}^{q_\iota} y_{\iota,j} \leq 1 \quad \forall \iota = \overline{1,4}, \quad \forall j = \overline{1, q_\iota} \quad \forall y_{\iota,j} \in \{0, 1\}.$$

Here, a simplified greedy heuristic can be used (i.e., series packing of items via value $\frac{c_{\iota,j}}{b_{\iota,j}}$). The illustration of the resultant improvement solution (as improvement of S^0): $I(S^0) = V_1^1 \star V_4^2 \star V_4^3 \star V_1^4$. The binary solution is $y_{1,1} = 0, y_{2,4} = 1, y_{3,4} = 1, y_{4,1} = 0$. The corresponding schedule S' is depicted in Fig. 13. Fig. 14 depicts an illustration for the analysis of balance by structural details production and requirements (by literal walls (panels) for initial schedule S^0 and for corrected (improved) schedule S').

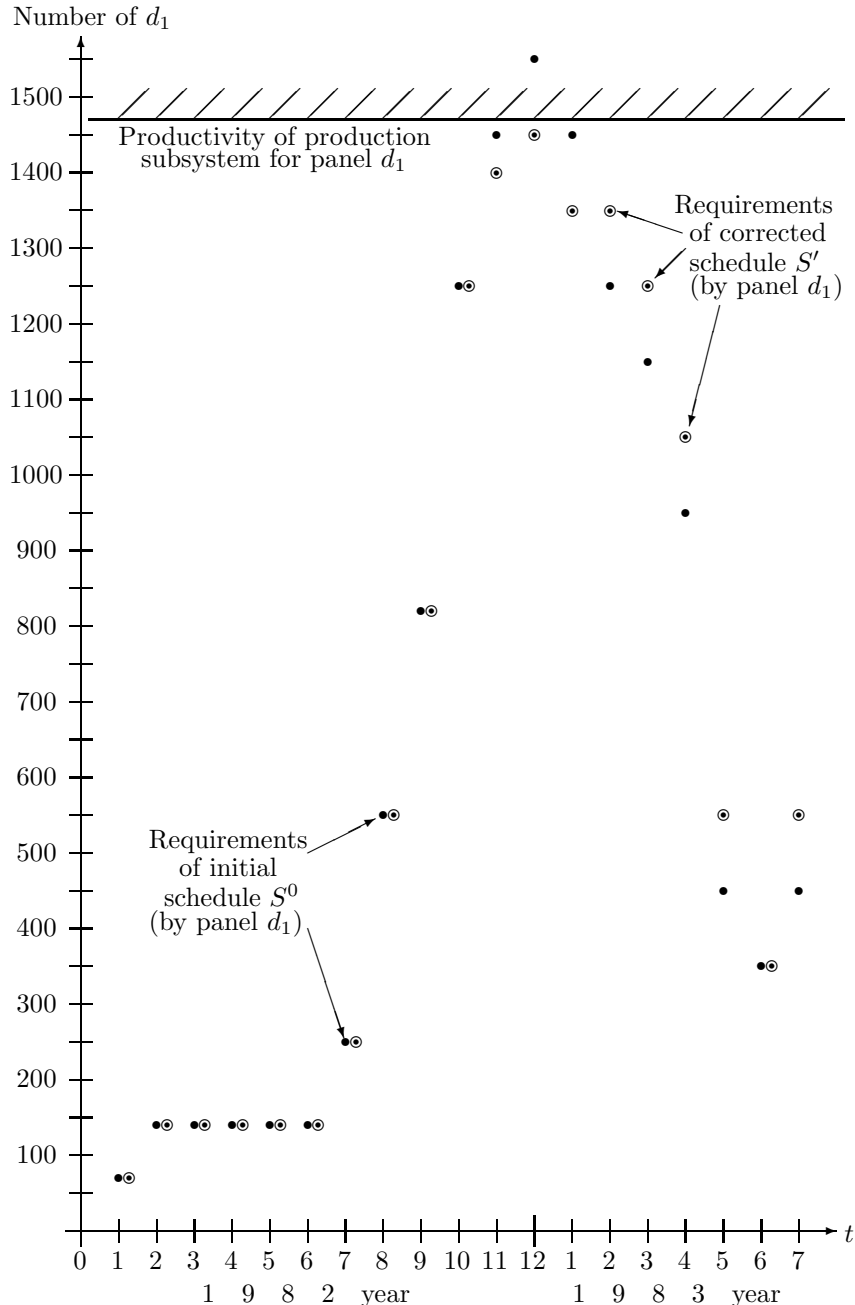


Fig. 14. Analysis of balance by structural details (by number of detail d_1)

5. Brief description of two other applications

5.1. General framework for supply chain management

A special generalized scheme for modular manufacturing and assembly supply chain is shown in Fig. 15. This scheme corresponds to multi-processor scheduling. The considered goal consists in coordination (i.e., balancing) between stage of modules manufacturing and transportation and stage of assemblies.

Thus, this approach may be considered as a version of coordinated supply chain management [181].

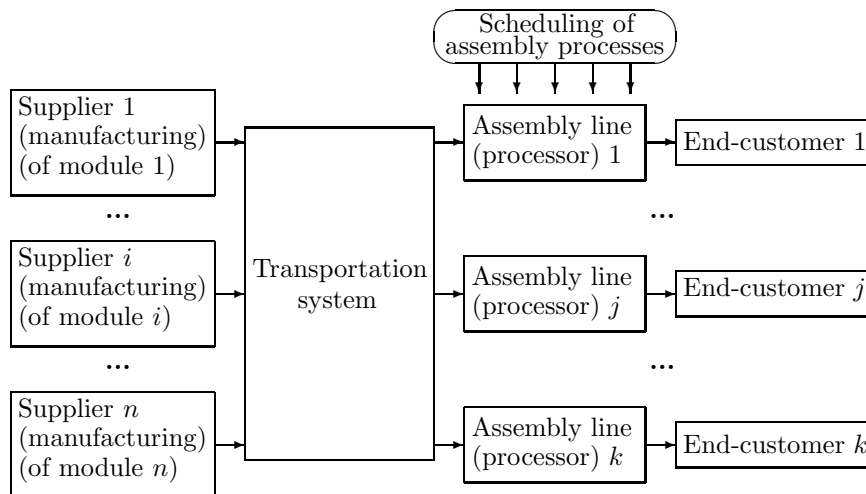


Fig. 15. Modular manufacturing and assembly (as supply chains)

5.2. Planning of multichannel flow in data transmission

There are n initial object-based message sequences (they correspond to data sources):

$A_1 = \langle a_{11}, a_{12}, a_{13}, \dots \rangle, \dots, A_i = \langle a_{i1}, a_{i2}, a_{i3}, \dots \rangle, \dots, A_n = \langle a_{n1}, a_{n2}, a_{n3}, \dots \rangle.$

Each message sequence A_i contains a set of standard objects/component (e.g., $b_{i1}, b_{i2}, b_{i3}, b_{i4}, \dots$) with precedence constraint (as a chain): $b_{i1} \leftarrow b_{i2} \leftarrow b_{i3} \leftarrow b_{i4} \leftarrow \dots$

The planning problem consists in scheduling of the messages on the basis of k sub-channels while taking into account special requirements as time-interval balancing by message objects (i.e., for time interval $\tau_1, \tau_2, \tau_3, \dots$). It is assumed each message can be sent via each subchannel and with a time shift (a delay).

A scheme of the considered time-balanced object-based message scheduling process is shown in Fig. 16.

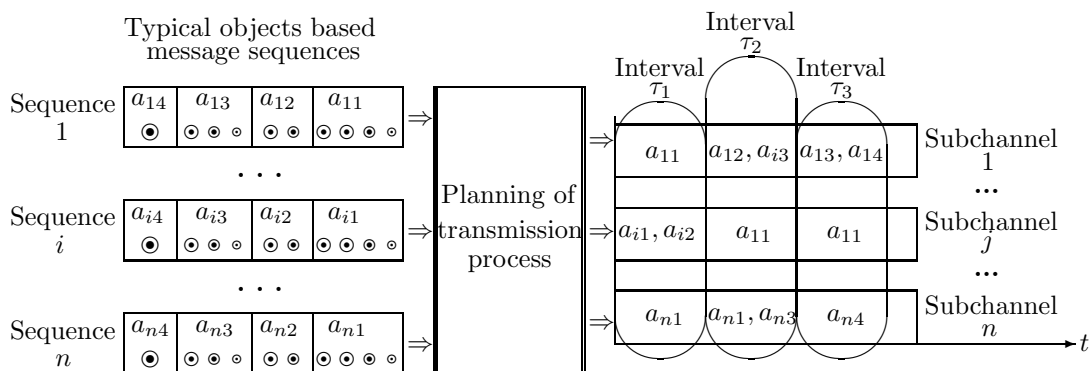


Fig. 16. Scheme of time-balanced object-based message scheduling

6. Conclusion

In the paper, a new problem of time-interval balancing in multi-processor scheduling of composite modular is proposed and described. A big illustrative real world example for scheduling in homebuilding is presented and two prospective applied domains are pointed out.

The following future research directions can be pointed out: (1) consideration of the suggested planning problem (and close just-in-time scheduling problems) from the viewpoint of restructuring of solutions [105]; (2) analysis and implementation of various solving frameworks for the considered planning problem; (3) taking into account uncertainty in the balancing models; (4) study of other possible application domains for the problem (e.g., in communication networking).

7. Acknowledgments

The research was partially supported by the Russian Science Foundation (grant of Institute for Information Transmission Problems of Russian Academy of Sciences 14-50-00150, “Digital technologies and their applications”).

REFERENCES

1. M.O. Adamu, O. Abass, Parallel machine scheduling to maximize the weighted number of just-in-time jobs. *J. of Applied Science and Technology*, 15(1–2), 27–34, 2010.
2. M.O. Adamu, A.O. Adewumi, Metaheuristics for scheduling on parallel machine to minimize weighted number of early and tardy jobs. *Int. J. of Physical Sciences*, 7(10), 1641–1652, 2012.
3. M.S. Akturk, F. Erhun, An overview of design and operational issues of kanban systems. *Int. J. of Prod. Res.*, 37(17), 3859–3881, 1999.
4. B. Alidaee, I. Dragan, A note on minimizing the weighted sum of tardy and early completion penalties in a single machine: a case of small common due date. *EJOR*, 96(3), 559–563, 1997.
5. G.A. Alvarez-Perez, J.L. Gonzalez-Valarde, J.W. Fowler, Cross-docking - just in time scheduling: an alternative solution approach. *J. of the ORS*, 60(4), 554–564, 2009.
6. R. Alvarez-Valdes, E. Crespo, J.M. Tamarit, F. Villa, Minimizing weighted earliness-tardiness on a single machine with a common due date using quadratic models. *TOP*, 20, 754–767, 2012.
7. R. Alvarez-Valdes, J.M. Tamarit, F. Villa, Minimizing weighted earliness-tardiness on parallel machines using hybrid metaheuristics. *Comp. and Oper. Res.*, 54, 1–11, 2015.
8. E. Angelelli, C. Filippi, On the complexity of interval scheduling with a resource constraint. *Theor. Comp. Sci.*, 412(29), 3650–3657, 2011.
9. E.M. Arkin, E.L. Silverberg, Scheduling jobs with fixed start and finish times. *Discr. Appl. Math.*, 18(1), 1–8, 1987.
10. K.R. Baker, Minimizing earliness and tardiness costs in stochastic scheduling. *EJOR*, 236(2), 445–452, 2014.
11. K.R. Baker, G.D. Scudder, Sequencing with earliness and tardiness penalties: a review. *Oper. Res.*, 38(1), 22–36, 1990.
12. J. Bank, F. Werner, Heuristic algorithms for unrelated parallel machine scheduling with a common due date, release dates, and linear earliness and tardiness penalties. *Mathematical and Computer Modelling*, 33(4–5), 363–383, 2001.
13. R. Bar-Yehuda, G. Polevoy, D. Rawitzz, Bandwidth allocation in cellular networks with multiple interferences. *Discr. Appl. Math.*, 194(23), 23–36, 2015.
14. T. Batu, P. Berenbrink, C. Cooper, Chains-into-bins processes. *J. of Discr. Alg.*, 14, 21–28, 2012.
15. R. Benmansour, H. Allaoui, A. Artiba, Stochastic single machine scheduling with random common due date. *Int. J. of Prod. Res.*, 50(13), 3560–3571, 2012.
16. E.G. Birgin, D.P. Ronconi, Heuristic methods for the single machine scheduling problem with different ready times and common due date. *Engineering Optimization*, 44(10), 2012.
17. A.R. Bolori Arabani, S.M. Fatemi Ghomi, M. Zandieh, A multi-criteria cross-docking scheduling with just-in-time approach. *Int. J. Adv. Manuf. Technol.*, 49(5), 741–756, 2010.
18. N. Boysen, S. Bock, Scheduling just-in-time part supply for mixed-model assembly lines. *EJOR*, 211(1), 15–25, 2011.

19. W. Bozejko, P. Rajba, M. Wodecki, Scheduling problem with uncertain parameters in just in time system. In: L. Rutkowski, M. Korytkowski, R. Scherer, R. Tadeusiewicz, L.A. Zadeh, J.M. Zurada (eds), *Artificial Intelligence and Soft Computing*, LNCS 8468, Springer, pp. 456–467, 2014.
20. M. Branda, J. Novotny, A. Olstad, Fixed interval scheduling under uncertainty - a tabu search algorithm for an extended robust coloring formulation. *Comp. and Ind. Eng.*, 93, 45–54, 2016.
21. N. Brauner, Y. Crama, The maximum deviation just-in-time scheduling problem. *Discr. Appl. Math.*, 134(1–3), 25–50, 2004.
22. X. Cai, S. Zhou, Scheduling stochastic jobs with asymmetric earliness and tardiness penalties. *Naval Res. Logist.*, 44, 531–557, 1997.
23. X. Cai, S. Zhou, Stochastic scheduling on parallel machines subject to random breakdowns to minimize expected costs for earliness and tardy jobs. *Oper. Res.*, 47(3), 422–437, 1999.
24. M.C. Carlisle, E.L. Lloyd, On the k -coloring of intervals. *Discr. Appl. Math.*, 59, 225–235, 1995.
25. M.W. Carter, C.A. Tovey, When is the classroom assignment problem hard? *Oper. Res.*, 40, 28–39, 1992.
26. O. Cepek, S.C. Sung, A quadratic time algorithm to maximize the number of just-in-time jobs on identical parallel machines. *Comp. & Oper. Res.*, 32(12), 3265–3271, 2005.
27. Z.-L. Chen, W.B. Powell, A column generation based decomposition algorithm for a parallel machine just-in-time scheduling problem. *EJOR*, 116(1), 220–232, 1999.
28. B. Chen, R. Hassan, M. Tzur, Allocation of bandwidth and storage. *IIE Trans.*, 34, 501–507, 2002.
29. Z.Z. Chen, T. Jiang, G.H. Lin, R. Rizzi, J.J. Wen, D. Xu, Y. Xu, More reliable protein NMR peak assignment via improved 2-interval scheduling. In: G. Di Battista, U. Zwick (eds), *Algorithms - ESA 2003*, LNCS 2832, Springer, pp. 580–592, 2003.
30. T.C.E. Cheng, Z.L. Chen, N.V. Shakhlevich, Common due date assignment and scheduling with ready times. *Comp. and Oper. Res.*, 29(14), 1957–1967, 2002.
31. S. Chetty, A.O. Adewumi, A study of the enhanced best performance algorithm for the just-in-time scheduling problem. *Discrete Dynamics in Nature and Society*, Vol. 2015, Art. ID 350308, 12 pages.
32. B.C. Choi, S.J. Yoon, Maximizing the number of just-in-time jobs in flow-shop scheduling. *J. of Scheduling*, 10 (4–5), 237–243, 2007.
33. B.C. Choi, J. Chung, Two-agent single-machine scheduling problem with just-in-time jobs. *Theor. Comp. Sci.*, 543, 37–45, 2014.
34. M. Christopher, *Logistics & Supply Chain Management.*, 4th ed., Prentice Hall, 2011.
35. D.Y. Chung, B.C. Choi, Just-in-time scheduling with competing agents. *Korean Oper. Res. Manag. Sci.*, 37, 19–28, 2012.
36. P. De, J.B. Ghosh, C.E. Wells, On the minimization of the weighted number of tardy jobs with random processing times and deadline. *Comp. and Oper. Res.*, 18(5), 457–463, 1991.
37. D. Dereniowski, W. Kubiak, Makespan minimization of multi-slot just-in-time scheduling on single and parallel machines. *J. of Scheduling*, 13(5), 479–492, 2010.
38. T.N. Dhamala, S.R. Khadka, A review on sequencing approaches for mixed-model just-in-time production systems. *Iranian J. of Optimization*, 1, 266–290, 2009.
39. I.G. Drobouchevich, J.B. Sidney, Minimization of earliness, tardiness and due date penalties on uniform parallel machines with identical jobs. *Comp. and Oper. Res.*, 39(9), 1919–1926, 2012.
40. A. Elysi, N. Salmasi, Stochastic scheduling with minimizing the number of tardy jobs using change constrained programming. *Mathematical and Computer Modelling*, 57(5–6), 1154–1164, 2013.
41. A. Elysi, N. Salmasi, Stochastic flow-shop scheduling with minimizing the expected number of tardy jobs. *The Int. J. of Adv. Manuf. Technol.*, 66(1–4), 337–346, 2013.
42. H. Emmons, Scheduling to a common due-date on parallel uniform processors. *Naval Research Logistics Quarterly*, 34, 803–810, 1987.
43. H. Emmons, M.L. Pinedo, Scheduling stochastic jobs with due dates on parallel machines. *EJOR*, 47, 49–55, 1990.
44. M.R. Garey, D.S. Johnson, *Computers and Intractability. The Guide to the Theory of NP-Completeness.* W.H. Freeman and Company, San Francisco, 1979.
45. M.R. Garey, R.E. Tarjan, G.T. Wilfong, One-processor scheduling with symmetric earliness and tardiness penalties. *Mathematics of Operations Research*, 13, 330–348, 1988.
46. E. Gerstl, G. Mosheiov, Due-window assignment problems with unit-time jobs. *Appl. Math. and*

- Computation, 220, 487–495, 2013.
47. E. Gerstl, G. Mosheiov, Due-window assignment with identical jobs on parallel uniform machines. *EJOR*, 229(1), 41-47, 2013.
 48. E. Gerstl, G. Mosheiov, An improved algorithm for due window assignment on parallel identical machines with unit-time jobs. *Information Processing Letters*, 113(19), 754-759, 2013.
 49. E. Gerstl, G. Mosheiov, Minmax weighted earliness-tardiness with identical processing times and two competing agents. *Comp. and Ind. Eng.*, 107, 171–177, 2017.
 50. F. Giordano, M.M. Schiraldi, On Just-In-Time Production Leveling. In: *Operations Management*, INTECH, pp. 141–162, 2015.
 51. D.Y. Golhar, C.L. Stamm, The just-in-time philosophy: a literature review. *The Int. J. of Prod. Res.*, 29(4), 657–676, 1991.
 52. V.S. Gordon, A note on optimal assignment of slack due-dates in single-machine scheduling. *EJOR*, 70(3), 311-315, 1993.
 53. V.S. Gordon, V.A. Strusevich, Earliness penalties on a single machine subject to precedence constraints: SLK due date assignment. *Comp. & Oper. Res.*, 26(2), 157-177, 1999.
 54. V.S. Gordon, J.M. Proth, C. Chu, A survey of the state-of-the-art of common due-date assignment and scheduling research. *EJOR*, 139(1), 1-25, 2002.
 55. V.S. Gordon, J.-M. Proth, V.A. Strusevich, Scheduling with due date assignment. In: J.Y. Leung (Ed.), *Handbook of Scheduling: Algorithms, Models and Performance Analysis*. Chapman & Hall/CRC Press, Boca Raton, FL, USA, Chapter 10, 2004.
 56. H. Groenevelt, The just-in-time systems. In: *Handbook in Operations Research and Management Science*, vol. 4, pp. 629–670, 1993.
 57. U.I. Gupta, D.T. Lee, J.Y.-T. Leung, An optimal solution the the channel-assignment problem. *IEEE Trans. on Computers*, 28, 807–810, 1979.
 58. N.G. Hall, M.E. Posner, Earliness-tardiness scheduling problems, I: Weighted deviation of completion times about a common due date. *Operations Research*, 39, 836-846, 1991.
 59. N.G. Hall, S.P. Sethi, C. Sriskandarajah, On the complexity of generalized due date scheduling problems. *EJOR*, 51(1), 100-109, 1991.
 60. D. Hermelin, D. Shabtay, N. Talmon, On the parameterized tractability of the just-in-time flow-shop scheduling problem. *Electr. prepr.*, 23 p., Sep. 13, 2017. <http://arxiv.org/abs/1709.04169> [cs.DS]
 61. K. Hiraishi, E. Levner, M. Vlach, Scheduling of parallel identical machines to maximize the weighted number of just-in-time jobs. *Comp. and Oper. Res.*, 29(7), 841–848, 2002.
 62. J.A. Hoogeveen, S.L. Van de Velde, Scheduling around a small common due date. *EJOR*, 55(2), 237–242, 1991.
 63. J.A. Hoogeveen, Multicriteria scheduling. *EJOR*, 167(3), 592–623, 2005.
 64. P.Y. Huang, L.P. Rees, B.W. Taylor III, A simulation analysis of the Japanese just-in-time techniques (with kanbans) for a multiline, multistage production systems. *Dec. Sci.*, 14(3), 326–344, 1983.
 65. R.-H. Huang, C.-L. Yang, H.-T. Huang, Parallel machine scheduling with common due-windows. *J. of the ORS*, 61, 640-646, 2010.
 66. R.-H. Huang, C.-L. Yang, W.-C. Cheng, Flexible job shop scheduling with due window - a two-phoromone ant colony approach. *Int. J. Prod. Econ.*, 141, 685-697, 2013.
 67. A. Janiak, M. Winczaszek, A single processor scheduling problem with a common due window assignment. In: H. Fleuren, D. den Hertog, P. Kort (eds), *Operations Research Proceedings*, pp. 213-220, 2004.
 68. A. Janiak, M.Y. Kovalyov, M. Marek, Soft due-window assignment and scheduling on parallel machines. *IEEE Trans. on SMC, Part A*, 37(5), 614-620, 2007.
 69. A. Janiak, R. Januszkiewicz, Scheduling of unit-time jobs distinct due windows on parallel processors. In: *Proc. 9th IFAC Workshop on Intelligent Manufacturing Systems*, pp. 118–121, 2008.
 70. A. Janiak, W. Janiak, M.K. Kovalyov, F. Werner, Soft due-window assignment and scheduling of unit-time jobs on parallel machines. *4OR*, 10, 347-360, 2012.
 71. A. Janiak, T. Kwiatkowski, M. Lichtenstein, Scheduling problems with a common due window assignment: a survey. *Applied Mathematics and Computer Science*, 23(1), 231–241, 2013.
 72. A. Janiak, W.A. Janiak, M.Y. Lovalyov, E. Kozan, E. Pesch, Parallel machine scheduling and common due window assignment with job independent earliness and tardiness costs. *Inf. Sci.*, 224, 109–117,

- 2013.
73. A. Janiak, W. Janiak, T. Krysiak, T. Kwiatkowski, A survey on scheduling problems with due windows. *EJOR*, 242(2), 347–357, 2015.
 74. C. Jia, Stochastic single machine scheduling with proportional job weights to minimize deviations of completion times from a common due date. In: 42rd IEEE Int. Conf. on Decision and Control, vol. 5, pp. 5124–5127, 2003.
 75. J. Josefowska, *Just-in-Time Scheduling: Models and Algorithms for Computer and Manufacturing Systems*. Springer, 2010.
 76. O.A. Joseph, R. Sridharan, Analysis of dynamic due-date assignment models in a flexible manufacturing systems. *J. of Manufacturing Systems*, 30(1), 28–40, 2011.
 77. T. Itoh, H. Ishii, Fuzzy due-date scheduling problem with fuzzy processing times. *Int. Trans. Oper. Res.*, 6, 639–647, 1999.
 78. I. Kacem, Fully polynomial time approximation scheme for the total weighted tardiness with a common due date. *Discr. Appl. Math.*, 158(9), 1035–1040, 2010.
 79. Ph. Kaminsky, D.S. Hochbaum, Due date quotation models and algorithms. In: J.Y. Leung (Ed.), *Handbook of Scheduling: Algorithms, Models and Performance Analysis*. Chapman & Hall/CRC Press, Boca Raton, FL, USA, Chapter 20, 2004.
 80. N.I. Karacapilidis, C.P. Pappis, Optimal due-date determination and sequencing n jobs on a single machine using the SLK method. *Computers in Industry*, 21(3), 335–339, 1993.
 81. V. Kayvanfar, G.H.M. Komaki, A. Aalaei, M. Zandieh, Minimizing total tardiness and earliness on unrelated parallel machines with controllable processing times. *Comput. Oper. Res.*, 41, 31–43, 2014.
 82. H. Kellerer, K. Rustogi, V.A. Strusevich, A fast FPTAS for single machine scheduling problem of minimizing total weighted earliness and tardiness about large common du date. *Omega*, 2018 (in Press).
 83. T. Keshavarz, M. Savelsbergh, N. Salmasi, A branch-and-bound algorithm for the single machine sequence-dependent group scheduling problem with earliness and tardiness penalties. *App. Math. Modelling*, 39(20), 6410–6424, 2015.
 84. A.W.J. Kolen, J.K. Lenstra, Ch.H. Papadimitriou, F.C.R. Spijksma, Interval scheduling: a survey. *Naval Res. Logist.*, 54(5), 530–543, 2007.
 85. A.J. Kootanaee, K.N. Babu, H.F. Talari, Just-in-tome manufacturing system: from introduction to implement. *Int. J. of Economics, Business and Finance*, 1(2), 7–25, 2013.
 86. C. Koulamas, Common due date assignment with generalized eaqliness/tardness penalties. *Comp. and Ind. Eng.*, 109, 79–83, 2017.
 87. M.Y. Kovalyov, W. Kubiak, A fully polynomial approximation scheme for the weighted earliness-tardiness problem. *Oper. Res.*, 47(5), 757–761, 1999.
 88. M.Y. Kovalyov, C.T. Ng, T.C.E. Cheng, Fixed interval scheduling: models, applications, computational complexity and algorithms. *EJOR*, 178(2), 331–342, 2007.
 89. F.J. Kramer, C.-Y. Lee, Common due-window scheduling. *Prod. Oper. Manag.*, 2(4), 262–275, 1993.
 90. F.J. Kramer, C.-Y. Lee, Due-window scheduling for parallel machines. *Mathematical and Computer Modeling*, 20, 69–89, 1994.
 91. G.N. Krieg, H. Kuhn, A decomposition method for multi-product kanban systems with setup times and lost sales. *IEE Transactions*, 34, 613–625, 2002.
 92. K.G. Kroon, M. Salomon, L.N. van Wassenhove, Exact and approximation algorithms for the tactical fixed interval scheduling problem. *Oper. Res.*, 45, 624–638, 1997.
 93. S.O. Krumke, C. Thielen, S. Westphal, Interval scheduling on related machines. *Comp. and Oper. Res.*, 38, 1836–1844, 2011.
 94. W. Kubiak, Minimizing variation of production rates in just-in-time systems: a survey. *EJOR*, 66(3), 259–271, 1993.
 95. W. Kubiak, S. Sethi, Optimal just-in-time schedules for flexible transfer lines. *Int. J. of Flexible Manufacturing Systems*, 6(2), 137–154, 1994.
 96. W. Kubiak, G. Steiner, J.S. Yeomans, Optimal level schedules for mixed-model, multi level just-in-time assembly systems. *Annals of Oper. Res.*, 69, 241–259, 1997.
 97. M. Laguna, J.L.G. Velarde, A search heuristic for just-in-time scheduling in parallel machines. *J. of Intell. Manuf.*, 2(4), 253–260, 1991.

98. V. Lauff, F. Werner, Scheduling with common due date, earliness and tardiness penalties for multi-machine problems: a survey. *Mathematical and Computer Modelling*, 40(5–6), 637–655, 2004.
99. M. Lawson, R. Ogden, C. Goodier, *Design in Modular Construction*. CRC Press, 2014.
100. M.Sh. Levin, Techno-Working Project: subsystem for generation of manufacturing plan based on house-building flow plans. Organization “Mosproekt-1”, Moscow, 108 pp., 1982 (in Russian).
101. M.Sh. Levin, *Combinatorial Engineering of Decomposable Systems*. Springer, 1998.
102. M.Sh. Levin, Multiset estimates and combinatorial synthesis. *Electr. prepr.*, 30 p., May 9, 2012. <http://arxiv.org/abs/1205.2046> [cs.SY]
103. M.Sh. Levin, *Modular System Design and Evaluation*, Springer, 2015.
104. M.Sh. Levin, Towards combinatorial clustering: preliminary research survey. *Electr. prepr.*, 102 p., May 28, 2015. <http://arxiv.org/abs/1505.07872> [cs.AI]
105. M.Sh. Levin, Towards integrated glance to restructuring in combinatorial optimization. *Electr. prepr.*, 31 p., Dec. 20, 2015. <http://arxiv.org/abs/1512.06427> [cs.AI]
106. M.Sh. Levin, On combinatorial clustering: literature review, methods, examples. *J. of Commun. Technol. and Electronics*, 60(12), 1403–1428, 2015.
107. M.Sh. Levin, On dynamic combinatorial clustering. *J. of Commun. Technol. and Electronics*, 62(6), 718–730, 2017.
108. M.Sh. Levin, Towards balanced clustering - part 1 (preliminaries). *Elec. prepr.*, 21 p., Jun. 9, 2017. <http://arxiv.org/abs/1706.03065> [cs.DS]
109. M.Sh. Levin, On balanced clustering (indices, models, examples). *J. of Communications Technology and Electronics*, 62(12), 1506–1515, 2017.
110. Y. Leyvand, D. Shabtay, G. Steiner, L. Yedidsion, Just-in-time scheduling with controllable processing times on parallel machines. *J. Comb. Optim.*, 19(3), 347–368, 2010.
111. L. Li, D.J. Fonesca, D.S. Chen, Earliness-tardiness production planning for just in time manufacturing: A unifying approach by goal programming. *EJOR*, 175(1), 508–515, 2006.
112. C.L. Li, G. Mosheiov, U. Yovel, An efficient algorithm for minimizing earliness, tardiness, and due-date costs for equal-sized jobs. *Comp. & Oper. Res.*, 35(11), 3612–3619, 2008.
113. S. Li, C.T. Ng, J. Yuan, Group scheduling and due date assignment on a single machine. *Int. J. Prod. Econ.*, 130, 230–235, 2011.
114. S.D. Liman, S.S. Panwalkar, S. Thongmee, Determination of common due window location in a single machine scheduling problem. *EJOR*, 93(1), 68–74, 1996.
115. S.D. Liman, S.S. Panwalkar, S. Thongmee, A single machine scheduling problem with common due window and controllable processing times. *Ann. Oper. Res.*, 70, 145–154, 1997.
116. S.D. Liman, S.S. Panwalkar, S. Thongmee, Common due window size and location determination in a single machine scheduling problem. *J. of the ORS*, 49(9), 1007–1010, 1998.
117. K. Liu, N. Abu-Ghazaleh, K.D. Kang, JiTS: Just-in-time scheduling for real-time sensor data dissemination. *Elec. prepr.*, 25 p., Aug. 16, 2006. <http://arxiv.org/abs/0608069> [cs.NI]
118. L. Liu, J.-J. Wang, F. Liu, M. Liu, Single machine due window assignment and resource allocation scheduling problems with learning and general positional effects. *J. of Manuf. Syst.*, 43, Part 1, 1–14, 2017.
119. B.A. Maksimenko, Method of catalogue big structural panel elements as a new stage in Moscow homebuilding. In: *Advanced Experience in Moscow Homebuilding*, no. 2, 7–9, 1982 (in Russian).
120. S. Martello, P. Toth, A heuristic approach to the bus driver scheduling problem. *EJOR*, 24, 106–117, 1986.
121. S. Meissner, Controlling just-in-sequence flow-production. *Logistics Research*, 2, 45–53, 2010.
122. M.P. McGrarry, M. Reisslein, C.J. Colbourn, M. Maier, F. Aurzada, M. Scheutzw, Just-in-time scheduling for multichannel EPONs. *IEEE Trans. of Lightwave Technology*, 26(10), 1204–1216, 2008.
123. P.R. McMullen, JIT sequencing for mixed-model assembly lines with setups using Tabu Search. *Production Planning & Control*, 9(5), 504–510, 1998.
124. R. M’Hallah, R.L. Bulfin, Minimizing the weighted number of tardy jobs on parallel processors. *EJOR*, 160, 471–484, 2005.
125. J. Miltenburg, Level schedules for mixed-model assembly lines in just-in-time production systems. *Manag. Sci.*, 35(2), 192–207, 1989.
126. J. Miltenburg, G. Steiner, S. Yeomans, A dynamic programming algorithm for scheduling mixed-

- model, just-in-time production systems. *Math. and Comp. Modell.*, 13(3), 57–66, 1990.
- 127.J. Mittenthal, M. Raghavachari, Stochastic single machine scheduling with quadratic early-tardy penalties. *Oper. Res.*, 41, 786–796, 1993.
- 128.J.N. Monette, Y. Deville, P. Van Hentenryck, Just-in-time scheduling with constrained programming. In: Nineteenth Int. Conf. on Automated Planning and Scheduling ICAPS 2009, pp. 241–248, 2009.
- 129.S.A. Mondel, A.K. Sen, Single machine weighted earliness-tardiness penalty problem with a common due date. *Comp. and Oper. Res.*, 28(7), 649–669, 2001.
- 130.Y. Monden, *Toyota Production System: An Integrated Approach to Just-In-Time*. 4th ed., CRC Press, 2011.
- 131.F. Mooeni, S.M. Sanchez, A.J. Vakharia, A robust design methodology for Kanban system design. *Int. J. of Prod. Res.*, 35, 2821–2838, 1997.
- 132.J.M. Moore, An n job, one machine sequencing algorithm for minimizing the number of late jobs. *Manag. Sci.*, 15, 102–109, 1968.
- 133.B. Mor, G. Mosheiov, D. Shabtay, A note: minmax due-date assignment problem with lead-time cost. *Comp. & Oper. Res.*, 40, 2161–2164, 2013.
- 134.B. Mor, G. Mosheiov, Scheduling a deteriorating maintenance activity and due-window assignment. *Comp. & Oper. Res.*, 57, 33–40, 2015.
- 135.G. Mosheiov, M. Shadmon, Minmax earliness-tardiness costs with unit processing time jobs. *EJOR*, 130(3), 638–652, 2001.
- 136.G. Mosheiov, D. Oron, Due-window assignment with unit processing time jobs. *Naval Research Logistics*, 51, 1005–1017, 2004.
- 137.G. Mosheiov, D. Oron, A note on the SPT heuristic for solving scheduling problems with generalized due-dates. *Comp. and Oper. Res.*, 31(3), 645–655, 2004.
- 138.G. Mosheiov, U. Yovel, Minimizing weighted earliness-tardiness and due date cost with unit processing time jobs. *EJOR*, 172(2), 528–544, 2006.
- 139.G. Mosheiov, D. Oron, A multi-criteria scheduling with due-window assignment problem. *Math. and Computer Modelling*, 48(5), 898–907, 2008.
- 140.G. Mosheiov, A. Sarig, Due-window assignment problem with position-dependent processing times. *J of the ORS*, 59(7), 997–1003, 2008.
- 141.G. Mosheiov, A. Sarig, Due-date assignment on uniform machines. *EJOR*, 193(1), 49–58, 2009.
- 142.G. Mosheiov, A. Sarig, Minmax scheduling problems with a common due-window. *Comput. Oper. Res.*, 36(6), 1886–1892, 2009.
- 143.G. Mosheiov, A. Sarig, Scheduling a maintenance activity and due-window assignment on a single machine. *Comput. Oper. Res.*, 36(9), 2541–2545, 2009.
- 144.G. Mosheiov, A. Sarig, Scheduling with a common due-window: polynomial solvable cases. *Inform. Sci.*, 180(8), 1492–1505, 2010.
- 145.M.A. Mullens, *Factory Design for Modular Homebuilding*. Constructability Press, 2011.
- 146.V.S. Nori, B.R. Sarker, Cyclic scheduling for a multi-product, single-facility production system operating under a just-in-time delivery policy. *J. of the ORS*, 47(7), 930–935, 1996.
- 147.S.S. Panwalkar, M.L. Smith, A. Seidmann, Common due date assignment to minimize total penalty for the one machine scheduling problem. *Operations Research*, 30, 391–399, 1982.
- 148.Ch.H. Papadimitriou, K. Steiglitz, *Combinatorial Optimization: Algorithms and Complexity*. Dover, 2013.
- 149.J. Pereira, O.C. Vasquez, The single machine weighted mean squared deviation problem. *EJOR*, 261(2), 515–529, 2017.
- 150.L.S. Pheng, T.S. Jayawickrama, Just-in-Time Management of a Building Project in the Middle-East. In: R. Rios-Mercado, Y.A. Rios-Solis (eds), *Just-in-Time Systems*. Springer, pp. 261–286, 2012.
- 151.M.L. Pinedo, Stochastic scheduling with release dates and due dates. *Oper. Res.*, 31, 559–572, 1983.
- 152.M.L. Pinedo, *Scheduling: Theory, Algorithms, and Systems*. 5th ed., Springer, New York, 2016.
- 153.R. Rios-Mercado, Y.A. Rios-Solis (eds), *Just-in-Time Systems*. Springer, 2012.
- 154.A. Roach, R. Nagi, A hybrid GA-SA algorithm for just-in-time scheduling of multi-level assemblies. *Comp. and Oper. Res.*, 30(4), 1047–1060, 1996.
- 155.A. Rohegov, L. Vaisman, New system of big structural panel based homebuilding in Moscow. *Building Industry and Architecture in Moscow*, no. 5, 4–7, 1980 (in Russian).

- 156.K. Van Rompaey, I. Bolsens, H. De Man, Just in time scheduling. In: Proc. IEEE 1992 Int. Conf. on Computer Design: VLSI in Computers and Processors ICCD'92, pp. 295–300, 1992.
- 157.D.P. Ronconi, M.S. Kawamura, The single machine earliness and tardiness scheduling problem: lower bounds and a branch-and-bound algorithm. *Comput. & Appl. Math.*, 29(2), 107-124, 2010.
- 158.D.P. Ronconi, E.G. Birgin, Mixed-Integer Programming Models for Flowshop Scheduling Problems Minimizing the Total Earliness and Tardiness. In: R. Rios-Mercado, Y.A. Rios-Solis (eds), *Just-in-Time Systems*. Springer, pp. 91–105, 2012.
- 159.B.F. Rosa, M.J.F. Souza, S.R. de Souza, M.F. de Franca Filho, Z. Ales, P.Y.P. Machelon, Algorithms for job scheduling problems with distinct time windows and general earliness/tardiness penalties. *Comp. and Oper. Res.*, 81, 203–215, 2017.
- 160.C.S. Sakuraba, D.P. Ronconi, F. Sourd, Scheduling in a two-machine flowshop for the minimization of the mean absolute deviation from a common due date. *Comp. and Oper. Res.*, 36(1), 60–72, 2009.
- 161.S.C. Sarin, E. Erel, G. Steiner, Sequencing stochastic jobs on a single machine with a common due date and stochastic processing times. *EJOR*, 51, 188–198, 1991.
- 162.A. Seidmann, S.S. Panwalkar, M.L. Smith, Optimal assignment of due-dates for a single processor scheduling problem. *Int. J. of Prod. Res.*, 19, 393-399, 1981.
- 163.C. Sendil Kumar, R. Panneerselvam, Literature review of JIT-KANBAN system. *Int. J. of Advanced Manuf. Technol.*, 393–408, 2007.
- 164.D.K. Seo, C.M. Klein, W. Jang, Single machine stochastic scheduling to minimize the expected number of tardy jobs using mathematical programming models. *Comp.and Ind. Eng.*, 48, 153–161, 2005.
- 165.D. Shabtay, The just-in-time scheduling problem in flow shop scheduling systems. *EJOR*, 216(3), 521–532, 2012.
- 166.D. Shabtay, G. Steiner, Optimal due-date assignment in multi-machine environments. *J. of Scheduling*, 11, 217-228, 2008.
- 167.D. Shabtay, G. Steiner, L. Yedidsion, Bicriteria problems to minimize maximum tardiness and due date assignment cost in various scheduling environments. *Discr. Appl. Math.*, 158, 1090-1103, 2010.
- 168.D. Shabtay, G. Steiner, Scheduling to maximize the number of just-in-time jobs: a survey. In: R.Z. Rios-Mercado, Y.A. Rios-Solis (eds), *Just-In-Time Systems*. Springer, pp. 3–20, 2012.
- 169.D. Shabtay, N. Gasper, Two-machine flow-shop scheduling with rejection. *Comp. and Oper. Res.*, 39, 1087-1096, 2012.
- 170.D. Shabtay, G. Steiner, R. Zhang, Optimal coordination of resource allocation, due date assignment and scheduling decisions. *Omega*, 65, 41–54, 2016.
- 171.J. Sidney, Optimal single-machine scheduling with earliness and tardiness penalties. *Oper. Res.*, 25, 62-69, 1977.
- 172.H.M. Soroush, Single machine scheduling with stochastic processing times or stochastic due-dates to minimize the number of early and tardy jobs. *Int. J. of Oper. Res.*, 3(2), 90–108, 2006.
- 173.H.M. Soroush, Minimizing the weighted number of early and tardy jobs in a stochastic single machine scheduling problem. *EJOR*, 181(1), 266–287, 2007.
- 174.A. Soukhal, N.H. Toung, Just-in-Time Scheduling with Equal-Size Jobs. In: R. Rios-Mercado, Y.A. Rios-Solis (eds), *Just-in-Time Systems*. Springer, pp. 107–146, 2012.
- 175.F. Sourd, S. Kedad-Sidhoum, A faster branch-and-bound algorithm for the earliness-tardiness scheduling problem. *J. of Scheduling*, 11(1), 49–58, 2008.
- 176.C. Sriskandarajah, A note on the generalized due dates scheduling problems. *Naval Research Logistics*, 37, 587-597, 1990.
- 177.G. Steiner, J.S. Yeomans, Level schedules for mixed-model, just-in-time processes. *Manag. Sci.*, 39(6), 728–735, 1993.
- 178.S.C. Sung, M. Vlach, Maximizing weighted number of just-in-time jobs on unrelated parallel machines. *J. of Sched.*, 8(5), 453–460, 2005.
- 179.S. Tanaka, An exact algorithm for the single-machine earliness-tardiness scheduling problem. In: R. Rios-Mercado, Y.A. Rios-Solis (eds), *Just-in-Time Systems*. Springer, pp. 21–40, 2012.
- 180.H.Y. Tang, C.L. Zhao, C.D. Cheng, Single machine stochastic JIT scheduling problem subject to machine breakdowns. *Science in China Series A: Mathematics*, 51(2), 273–292, 2008.
- 181.D.J. Thomas, P.M. Griffin, Coordinated supply chain management. *EJOR*, 94(1), 1–15, 1996.

- 182.V. Tkindt, J.-C. Billaut, *Multicriteria Scheduling: Theory, Models and Algorithms*. 2nd ed., Springer, 2006.
- 183.D. Trietsch, K. Baker, Minimizing the number of tardy jobs with stochastically-ordered processing times. *J. of Scheduling*, 11(1), 71–73, 2008.
- 184.N.H. Tuong, A. Soukhal, Some new polynomial cases in just-in-time scheduling problems with multiple due dates. In: *Proc. of the Sixth Int. Conf. on Research, Innovation and Vision for the Future in Computing and Communications Technologies (RIVF08)*, pp. 36-41, 2008.
- 185.N.H. Tuong, A. Soukhal, Polynomial cases and PTAS for Just-in-Time scheduling on parallel machines around a common due-date. In: *11-th Int. Workshop on Project Management and Scheduling (PMS08)*. pp. 152-155, 2008.
- 186.N.H. Tuong, A. Soukhal, Due dates assignment and JIT scheduling with equal-size jobs. *EJOR*, 205(2), 280-289, 2010.
- 187.E. Vallada, R. Ruiz Scheduling Unrelated Parallel Machines with Sequence Dependent Setup Times and Weighted Earliness/Tardiness Minimization. In: R. Rios-Mercado, Y.A. Rios-Solis (eds), *Just-in-Time Systems*. Springer, pp. 67–90, 2012.
- 188.J.M.S. Valente, R.A.F.S. Alves, Efficient polynomial algorithms for special cases of weighted early/tardy scheduling with release dates and a common due date. *Pesquisa Operacional*, 23(3), 443–456, 2003.
- 189.J.M.S. Valente, J.F. Goncalves, A genetic algorithm approach for the single machine scheduling problem with linear earliness and quadratic tardiness penalties. *Comp. and Oper. Res.*, 36(10), 2707–2715, 2009.
- 190.J.-B. Wang, M.-Z. Wang, Single machine multiple common due dates scheduling with learning effects. *Computers and Mathematics with Applications*, 60(11), 2998–3002, 2010.
- 191.X.-Y. Wang, M.-Z. Wang, Single machine common flow allowance scheduling with a rate-modifying activity. *Comp. and Ind. Eng.*, 59(4), 898-902, 2010.
- 192.D. Wang, Y. Yin, T.C.E. Cheng, A bicriterion approach to common flow allowances due window assignment and scheduling with controllable processing times. *Naval Res. Logist.*, 64(1), 41–63, 2017.
- 193.J.Y. Wei, R.I. McFarland, Just-in-time signaling for WDM optical burst switching networks. *J. of Lightwave Technology*, 18(12), 2019–2037, 2000.
- 194.R. West, Y. Zhang, K. Schwan, C. Poellabauer, Dynamic window-constrained scheduling of real-time streams in media servers. *IEEE Trans. on Computers*, 53(6), 744–759, 2004.
- 195.G.J. Woeginger, On-line scheduling of jobs with fixed start and end times. *Theor. Comp. Sci.*, 130, 5–16, 1994.
- 196.S.-J. Yang, H.-T. Lee, J.-Y. Guo, Multiple common due dates assignment and scheduling problems with resource allocation and general position-dependent deterioration effect. *Int. J. Adv. Manuf. Technol.*, 67, 181-188, 2013.
- 197.D.-L. Yang, C.-J. Lai, S.-J. Yang, Scheduling problems with multiple due windows assignment and controllable processing times on a single machine. *Int. J. Prod. Econ.*, 150, 96–103, 2014.
- 198.W.K. Yeung, C. Oguz, T.C.E. Cheng, Single-machine scheduling with a common due window. *Comp. and Oper. Res.*, 28, 157-175, 2001.
- 199.W.K. Yeung, C. Oguz, T.C.E. Cheng, Two-stage flow shop earliness and tardiness machine scheduling involving a common due window. *Int. J. Prod. Econ.*, 90, 421-434, 2004.
- 200.W.K. Yeung, C. Oguz, T.C.E. Cheng, Two-machine flow shop scheduling with a common due window to minimize weighted number of early and tardy jobs. *Naval Res. Log.*, 180, 1492-1505, 2009.
- 201.Y. Yin, M. Liu, T.C.E. Cheng, C.-C. Wu, S.-R. Cheng, Four single-machine scheduling problems involving due date determination decisions. *Inf. Sci.*, 251, 164–181, 2013.
- 202.Y. Yin, T.C.E. Cheng, C.-C. Wu, S.-R. Cheng, Single-machine due window assignment and scheduling with a common allowance and controllable job processing time. *J. of the ORS*, 65, 1-13, 2014.
- 203.Y. Yin, D.-J. Wang, T.C.E. Cheng, C.-C. Wu, Bi-criterion single machine scheduling and due-window assignment with common flow allowances and resource-dependent processing times. *J. of the ORS*, 67(9), 1169–1183, 2016.
- 204.B. Yuce, F. Fruggiero, M.S. Packianather, D.T. Pham, E. Mastrocinque, A. Lambiase, M. Fera, Hybrid Genetic Bees Algorithm applied to single machine scheduling with earliness and tardiness penalties. *Comp. and Ind. Eng.*, 113, 842–858, 2017.
