

# Agile Scrum Development in an *ad hoc* Software Collaboration

A. L. Baxter,<sup>1, a</sup> S. Y. BenZvi,<sup>2</sup> W. Bonivento,<sup>3</sup> A. Brazier,<sup>4</sup> M. Clark,<sup>1</sup> A. Coleiro,<sup>5</sup> D. Collom,<sup>6</sup> M. Colomer-Molla,<sup>5, 7</sup> B. Cousins,<sup>8, 9, b</sup> A. Delgado Orellana,<sup>10</sup> D. Dornic,<sup>11</sup> V. Ekimtcov,<sup>12</sup> S. ElSayed,<sup>13</sup> A. Gallo Rosso,<sup>14</sup> P. Godwin,<sup>15, 9</sup> S. Griswold,<sup>2</sup> A. Habig,<sup>16</sup> R. Hill,<sup>14</sup> S. Horiuchi,<sup>17</sup> D. A. Howell,<sup>6, 18</sup> M. W. G. Johnson,<sup>12</sup> M. Jurić,<sup>19</sup> J. P. Kneller,<sup>20</sup> A. Kopec,<sup>1</sup> C. Kopper,<sup>21</sup> V. Kulikovskiy,<sup>22</sup> M. Lamoureux,<sup>23</sup> R. F. Lang,<sup>1</sup> S. Li,<sup>1</sup> M. Lincetto,<sup>11</sup> W. Lindstrom,<sup>6</sup> M. W. Linvill,<sup>1</sup> C. McCully,<sup>6</sup> J. Migenda,<sup>24</sup> D. Milisavljevic,<sup>1</sup> S. Nelson,<sup>19</sup> R. Novoseltseva,<sup>25</sup> E. O'Sullivan,<sup>26</sup> D. Petravick,<sup>12</sup> B. W. Pointon,<sup>27, 28</sup> N. Raj,<sup>28</sup> A. Renshaw,<sup>29</sup> J. Rumleskie,<sup>14</sup> T. Sonley,<sup>30</sup> R. Tapia,<sup>8, 9</sup> J. C. L. Tseng,<sup>31</sup> C. D. Tunnell,<sup>32, 33</sup> G. Vannoye,<sup>11</sup> C. F. Vigorito,<sup>34</sup> C. J. Virtue,<sup>14, 30</sup> C. Weaver,<sup>21</sup> K. E. Weil,<sup>1</sup> L. Winslow,<sup>35</sup> R. Wolski,<sup>13</sup> X. J. Xu,<sup>36</sup> and Y. Xu<sup>32</sup>

(The SCiMMA and SNEWS 2.0 Collaborations)

<sup>1</sup>*Department of Physics and Astronomy, Purdue University, West Lafayette, IN 47907, USA*

<sup>2</sup>*Department of Physics and Astronomy, University of Rochester, Rochester, NY 14627, USA*

<sup>3</sup>*INFN sezione di Cagliari Istituto Nazionale, Complesso Universitario di Monserrato - S.P. per Sestu Km 0.700, I-09042 Monserrato (Cagliari), Italy*

<sup>4</sup>*Center for Advanced Computing, Cornell University, Ithaca, NY 14853, USA*

<sup>5</sup>*Université de Paris, CNRS, AstroParticule et Cosmologie, F-75013, Paris, France*

<sup>6</sup>*Las Cumbres Observatory, Goleta, CA 93117, USA*

<sup>7</sup>*Instituto de Física Corpuscular (CSIC - Universitat de València) c/ Catedrático José Beltrán, 2 E-46980 Paterna, Valencia, Spain*

<sup>8</sup>*Institute for Computational and Data Sciences, The Pennsylvania State University, University Park, PA 16802, USA*

<sup>9</sup>*Department of Physics, The Pennsylvania State University, University Park, PA 16802, USA*

<sup>10</sup>*Pontificia Universidad Católica de Chile, Santiago, Región Metropolitana, Chile*

<sup>11</sup>*Aix Marseille Univ, CNRS/IN2P3, CPPM, Marseille, France*

<sup>12</sup>*National Center for Supercomputing Applications, University of Illinois at Urbana-Champaign, Urbana, IL 61801, USA*

<sup>13</sup>*Department of Computer Science, University of California Santa Barbara, CA 93106, USA*

<sup>14</sup>*Department of Physics, Laurentian University, Sudbury ON P3E 2C6, Canada*

<sup>15</sup>*Institute for Gravitation and the Cosmos, The Pennsylvania State University, University Park, PA 16802, USA*

<sup>16</sup>*Department of Physics and Astronomy, University of Minnesota Duluth, Duluth, MN, 55812, USA*

<sup>17</sup>*Center for Neutrino Physics, Department of Physics, Virginia Tech, Blacksburg, VA 24061, USA*

<sup>18</sup>*University of California Santa Barbara, CA 93106, USA*

<sup>19</sup>*DiRAC Institute and the Department of Astronomy,*

*University of Washington, Seattle, WA 98195, USA*

<sup>20</sup>*Department of Physics, NC State University, Raleigh, NC 27695, USA*

<sup>21</sup>*Department of Physics and Astronomy, Michigan State University, East Lansing, MI 48824, USA*

<sup>22</sup>*INFN Sezione di Genova, Via Dodecaneso 33, Genova, 16146 Italy*

<sup>23</sup>*INFN Sezione di Padova & Università di Padova, Dipartimento di Fisica, Padova, Italy*

<sup>24</sup>*Department of Physics, King's College London, London WC2R 2LS, UK*

<sup>25</sup>*Baksan Neutrino Observatory, Institute for Nuclear Research of Russian Academy of Sciences, Neytrino, Kabardino-Balkarian Republic, Russia, 361609*

<sup>26</sup>*Department of Physics and Astronomy, Uppsala University, Box 516, S-75120 Uppsala, Sweden*

<sup>27</sup>*Department of Physics, British Columbia Institute of Technology, Burnaby, BC, V5G 3H2, Canada*

<sup>28</sup>*TRIUMF, Vancouver, BC V6T 2A3, Canada*

<sup>29</sup>*Department of Physics, University of Houston, Houston, TX 77204, USA*

<sup>30</sup>*SNOLAB, Sudbury, ON P3Y 1N2, Canada*

<sup>31</sup>*Department of Physics, University of Oxford, Keble Road, Oxford OX1 3RH, UK*

<sup>32</sup>*Department of Computer Science, Rice University, 6100 Main St, Houston, TX, 77005, USA*

<sup>33</sup>*Department of Physics, Astronomy, Rice University, 6100 Main St, Houston, TX, 77005, USA*

<sup>34</sup>*Department of Physics, University of Torino & INFN, via Pietro Giuria 1, 10125 Torino, Italy*

<sup>35</sup>*Massachusetts Institute of Technology, Cambridge, MA 02139, USA*

<sup>36</sup>*Université Libre de Bruxelles, 1050 Bruxelles, Belgium*

Developing sustainable scientific software for the needs of the scientific community requires expertise in both software engineering and domain science. This can be challenging due to the unique needs of scientific software, the insufficient resources for modern software engineering practices in the scientific community, and the complexity of evolving scientific contexts for developers. These difficulties can be reduced if scientists and developers collaborate. We present a case study wherein scientists from the SuperNova Early Warning System collaborated with software developers from the Scalable Cyberinfrastructure for Multi-Messenger Astrophysics project. The collaboration addressed the difficulties of scientific software development, but presented additional risks to each team. For the scientists, there was a concern of relying on external systems and lacking control

in the development process. For the developers, there was a risk in supporting the needs of an user-group while maintaining core development. We mitigated these issues by utilizing an Agile Scrum framework to orchestrate the collaboration. This promoted communication and cooperation, ensuring that the scientists had an active role in development while allowing the developers to quickly evaluate and implement the scientists’ software requirements. While each system was still in an early stage, the collaboration provided benefits for each group: the scientists kick-started their development by using an existing platform, and the developers utilized the scientists’ use-case to improve their systems. This case study suggests that scientists and software developers can avoid some difficulties of scientific computing by collaborating and can address emergent concerns using Agile Scrum methods.

## I. INTRODUCTION

The development of scientific computing applications must address several challenges unique to the scientific software context. Unlike commercial software, a scientific application must often provide a precise solution to a problem before the software is modified or discarded [1]. Because the application may need to embody the science it serves, the development team must contain scientists who may not be trained to generate software which follows a well-planned software life-cycle. Indeed, scientists spend about 30% of their time developing scientific software and often learn the development tools they need during the development process itself [2, 3]. Moreover, budgetary constraints or time limitations often make it impractical to employ professional developers to take responsibility for the integrity of the software alongside the scientists. The timescales of scientific projects can be decades long with high personnel turnover, producing challenges for software sustainability. In particular, scientists who fulfill a development role can create legacy technical debt when they change roles or projects as they exploit new career opportunities. Efforts to introduce a new career trajectory of “research software engineer” attempt to address this problem [4]. However, the predominant approach to improving software sustainability is to increasingly depend upon community supported software and projects that “outlive” the tenure of any one developer.

These problems are intensified, rather than ameliorated, by computer service technologies such as cloud computing. “The Cloud” removes a dependency between scientific developers and the Information Technology (IT) personnel who must provision and configure the required computational resources, but the Cloud is inherently designed to run long-lived, supported web services. Moreover, cloud computing introduces a conflict with the short timelines of typical scientific budget cycles: the costs of hardware procurement and administration are more predictable and manageable in a scientific context. Thus, in exchange for a reduced IT burden, scientific developers - who may be transient - must adopt an asynchronous, networked programming model that is specifically de-

signed to produce generalizable, long-lived applications with longer-term budgetary considerations [5, 6]. That is, while cloud computing reduces the IT burden, it shifts some of that burden to developers, thereby creating additional sustainability risks.

Cloud computing and its ancillary software models require scientists to consider the life-cycle of the code they generate in addition to the publications that the code is designed to support [7]. Doing so introduces three concerns into the software development process that the application design must take into account. First, the software must modularize the parts of the code that focus on a specific scientific result in order to extend the life-cycle of the service beyond that of a particular scientific experiment. Second, the software must incorporate and depend on other lower-level systems, such as “cloud infrastructure as a service”, both in development and in execution as a “service mesh”. Finally, the resulting service mesh that contains an application designed to be maintainable throughout changes to software dependencies like security patches, software releases, and infrastructure upgrades. While the modularization concern is similar to the concerns that developers have when using scientific libraries, the other two are not common to scientific application development. Moreover, for budgetary reasons, many of the dependencies in a scientific web-service based application are available as open-source. Open-source is freely available and community maintained, but the release and maintenance life-cycles are not coordinated between technologies and services. Thus, the maintenance procedures for an application that contains multiple open-source technologies must be able to account for and manage the different software life-cycles of its dependencies.

These additional complexities are often unaddressed in modern scientific software development contexts since addressing them introduces additional risks to a positive scientific outcome. Simply introducing the tooling necessary to develop and maintain long-lived services can slow the time to scientific solution due to the time required to both learn and apply this tooling. Introducing maintenance and operations support into an application that leverages a service mesh can impact both the time to solution and possibly the application’s execution performance. Additionally, since the science requirements and codebase are often developing in parallel, there is a risk that when the scientific project requires a feature from

<sup>a</sup> SNEWS corresponding author: adepoian@purdue.edu

<sup>b</sup> SCiMMA corresponding author: bfc5288@psu.edu

a software dependency, it could be unavailable and not planned for in the immediate future. Finally, a service mesh architecture depends on the availability and correct execution of all services in the overall ensemble. If a constituent dependency fails, the application development could be halted since the developers are unable to directly remediate the external issue.

These risks have led to a “chasm” between scientific computing and formal software development [8, 9]. Service-based scientific applications often consist of deep, bespoke software stacks that have few external service dependencies. The development teams are small and, once in production, may consist of only a single expert developer who knows the system well-enough to provide support for issues or modifications in production. The use of auditing, life-cycle, and management tooling in scientific applications, like version control and issue tracking, varies over a large range from absent to proficient, with many implementations either budding or unused [10]. As a result, scientific applications, particularly those that serve large communities of scientists, have yet to take full advantage of the innovations that the commercial sector has developed for scalable applications design.

In this paper, we describe our experiences with a scientific application development effort that utilizes a collaboration to address the challenges of scientific computing. In particular, we describe the experience of scientific computing developers [11] who collaborate with a professional software development team [12] to develop a scientific application [13] that depends on a cloud-based service created independently by the software developers [14]. This collaboration allowed the scientific team to mitigate the risk of legacy software [15] by establishing an upstream dependency on a development project that is committed to supporting external users for its cloud-based services. However, the development project itself was also in an early prototyping phase, which increased the need for effective coordination between the two projects.

To implement this coordination, the collaboration established a second Agile process for a scientific development effort that tracked the ongoing Agile development of the cloud-based service; we describe the coordination required to successfully manage these two parallel, but dependent, Agile processes. We focus primarily on the downstream Agile process that this collaboration created and outline the effects this had on the ongoing, upstream Agile process. We also discuss the software engineering procedures we employed to ensure that the scientists could trust and depend on the in-progress upstream cloud-based service.

We review traditional and Agile software development procedures in Section II. We overview the two groups and the Agile abstractions we use in Section III. The formation of the collaboration and its risks are described in Section IV. Our approach to using Agile Scrum to resolve these risks is described in Section V. We assess the collaboration’s Agile Scrum framework and the outcomes

for each organization are described in Section VI. We provide connections between this case study and other related works in Section VII. Section VIII summarizes the takeaways of this case study for the scientific computing community.

## II. SOFTWARE DEVELOPMENT METHODOLOGIES

The overall scientific application development effort is focused on the introduction of commercial software engineering best practices as part of a collaboration between scientists and professional software developers [9]. The goal is for the scientists on the development team to use their domain expertise to explain software requirements to the software developers, allowing the two groups to utilize their collective knowledge to generate software requirements from the scientific use-case [16].

Such a partnership may introduce productivity risks for the professional developers, in addition to risks in the scientific development process. In this project, the professional development team had to maintain core development timelines and goals for its original stakeholder base, while at the same time developing new features and mechanisms to support the evolving scientific software development.

One approach to mitigate these issues is the use of an Agile Scrum software development framework [9, 16], described in Section III B. Agile software engineering practices are designed to be flexible to rapidly changing requirements, unlike a traditional Waterfall methodology. With a Waterfall engineering approach, the stakeholders and developers establish software requirements at the beginning of the project and then develop to meet those requirements [17]. If the requirements change during the development period, the software is obsolete when delivered. To avoid immediate obsolescence in this case, Waterfall developers must correct the requirements and then refactor the software during a release. If the requirements change rapidly enough or the refactoring time is too long, software delivery can be indefinitely postponed.

The Agile framework is designed to mitigate the risks associated with Waterfall engineering practices. It is an iterative approach to software development, wherein week- to month-long development tasks are favored over large, long-term goals for the end product [18, 19]. Moreover, the goal of an Agile development effort is to have a releasable product at the end of each short development period, called a “sprint”. In this way, as requirements change, the software is never more than a sprint’s duration away from a partially-featured releasable state.

Agile’s emphasis on short-term goals might not seem reasonable for large-scale scientific projects that often have long-term science goals on the timescale of decades. The key observation in this context is that while the long-term science goals may remain relatively fixed, the requirements for the software that is developed to meet

these science goals may change as scientific insights emerge. Agile software engineering encourages such incremental progress by organizing development into “User Stories”, individual tasks created and completed as emergent software requirements are discovered [19, 20].

The Scrum approach is one method to adopt Agile practices into a project [16, 19]. Scrum is a process framework that structures a project into a planning phase, design phase, and development phase to provide an incremental and emergent approach to Agile development [21]. These elements are particularly relevant in the scientific computing software development communities given their evolving software requirements [16, 22–26]. Despite these potential advantages, Agile practices tend to be rarely implemented [8, 9, 27] or incorrectly adapted [16] in the scientific computing community.

### III. ORGANIZATIONS AND BACKGROUND

The SuperNova Early Warning System (SNEWS) is an open, public alert system that is built to provide an early warning for core-collapse supernova in the Milky Way Galaxy [28]. The first indication of a potential stellar explosion will be the arrival of a burst of neutrinos [29]. SNEWS will issue an alert to its subscribers, which include astronomical observatories, neutrino detectors, and amateur astronomers and citizen scientists, if several detectors report a potential supernova within minutes of each other.

There are seven neutrino experiments participating in the current SNEWS framework and about 20 neutrino detectors worldwide that are planned to participate in the new SNEWS 2.0 framework, which is the basis of this work. The neutrino detectors have individual data formats that the SNEWS framework must be able to combine to identify neutrino burst coincidences. Additionally, these neutrino detectors will be active within SNEWS at different times. With these specific requirements, SNEWS is one of the few successful examples, to date, of cyberinfrastructure spanning major neutrino experiments [11]. In the current era of multi-messenger astrophysics (MMA), there are new opportunities for SNEWS to optimize its science reach for the next Galactic supernova. To achieve this goal, SNEWS depends on developing and sustaining software with a number of integrated components [11].

SNEWS represents one agent in an ever-growing community of MMA organizations that rely heavily on cyberinfrastructure to support their science requirements [30–37]. These requirements include prompt, reliable, and efficient alerting in addition to seamless support for different message formats and conventions [37–40]. The requirements also pertain to multiple detectors, institutes, and nations, and would be unrealistic for any individual group to address [41].

These challenges are not unique to the SNEWS effort. The MMA science community has developed var-

ious technologies, usually focused on a single project or experiment, that promote the sharing of results, collaboration among projects, and provenance. However, the emergence of a common set of functionalities across otherwise separately developed point-solutions prompted the creation of the multi-institute Scalable Cyberinfrastructure for Multi-Messenger Astrophysics (SCiMMA) project [12]. SCiMMA has been addressing the cyberinfrastructure needs of multiple MMA organizations and science efforts by engaging with the user community [42, 43], developing a shared, openly available, multi-format data distribution software [44], and providing cloud-based functionality “as a service” as well as packaged software infrastructure for MMA data acquisition and management [14, 45].

To develop these services, SCiMMA employs an Agile Scrum framework staffed by a small number of professional software developers resulting in a set of useful and successful practices for MMA software development [44, 46, 47]. SCiMMA’s development has focused initially on addressing the general need for the coordination of alerts and data between MMA organizations, such as the Vera C. Rubin Observatory’s Legacy Survey of Space and Time [30], the advanced Laser Interferometer Gravitational-Wave Observatory [48], and IceCube [49]. SCiMMA’s goal is to provide these services for the MMA science community through ongoing cyberinfrastructure efforts.

#### A. Collaboration Opportunity

While both SNEWS and SCiMMA had separately developed substantial cyberinfrastructure, each group was engaged in new development. SNEWS was seeking a software client and network infrastructure to prototype a modernized data distribution platform for a new release of the framework, SNEWS 2.0. The SNEWS team had already created software requirements as part of a Waterfall methodology, and was exploring technology options for a purely in-house development effort [11]. At the same time, SCiMMA was in the midst of its first release cycle for a new cyberinfrastructure component called HOPSKOTCH using an Agile methodology based on Scrum [14, 44]. While SCiMMA had already been working towards the use-cases of its current stakeholders, the management team identified an opportunity to tailor its development to support the SNEWS effort. Doing so would accelerate the development and also demonstrate wider community impact [12].

The connection between SNEWS and SCiMMA began when a member of SNEWS met with members of the SCiMMA team at a National Science Foundation “Harnessing the Data Revolution” grant meeting [50]. During the discussions, it became clear that HOPSKOTCH either provided or would provide the functionality required by the new SNEWS requirements. Together, they proposed an informal, remote cooperation between SNEWS

and SCiMMA given the clear overlap of interests and the clear possibility to use HOPSKOTCH as a core dependency for SNEWS 2.0.

Initially, the cooperation began experimentally without direct collaboration between the groups (Phase 0 in Figures 1 and 3). To test the hypothesis that HOPSKOTCH would meet SNEWS requirements, the SNEWS developers carried out their own development using publicly-available code from SCiMMA [44] without engaging the SCiMMA development team. To become more familiar with the code, the SNEWS team engaged with one of SCiMMA’s virtual community workshops to further assess the value of a collaboration [43].

Later, the partnership evolved into a dedicated bilateral collaboration (Phases 1 and 2 in Figures 1 and 3) involving members from both SNEWS and SCiMMA. This direct engagement ultimately catalyzed development for both organizations, but both teams were concerned with the inherent risks due to the collaboration’s novel structure and the fact that each organization’s development was at an early, prototyping stage. The main concerns were:

- Can SNEWS rely on pre-alpha, externally-supported systems to sustainably accomplish the scientific goals for SNEWS 2.0? Would the scientific requirements be communicated and addressed adequately on a short time-frame in a collaboration?
- Can SCiMMA temporarily prioritize a single user-group without derailing the ongoing development needed to support the broader MMA community? Would early user-engagement be feasible and beneficial in the long-term?

These risks could not be confronted until the SNEWS developers first ensured that SCiMMA’s work would be useful in their own efforts. Since SCiMMA had made its codebase openly available and promoted its development efforts via technical workshops for the MMA community, SNEWS could assess an active collaboration with SCiMMA prior to committing to such an engagement. We believe that this initial trust-establishing step was key to the ultimate success of the effort. Without it, much more of the collaboration itself would have focused on trust building and maintenance rather than on productivity and risk management.

Having decided to collaborate in this way, both teams agreed to acknowledge and address the risks to success through several stages of two-sided development and progress evaluations. The concerns of each group (Section IV) provided an outline for the nature of the collaboration. To address these concerns (Section V), the collaboration adopted its own Agile Scrum framework to promote communication and drive software development in response to both changes in the SNEWS requirements and changes introduced by the original SCiMMA stakeholders.

## B. Review of Agile Abstractions and Personnel Roles

An Agile development effort requires the participants to fulfill specific functional roles that manipulate a set of abstractions representing the software throughout its development life-cycle. We briefly summarize definitions of these abstractions and roles as our collaboration used them in practice.

*Scrum* – The overall organizational abstraction for an Agile project is the Scrum. For the collaboration between SNEWS and SCiMMA, the Scrum consisted of a *sprint planning*, a *sprint*, and a *sprint retrospective*. During a sprint planning meeting the specific development tasks are discussed and decided. A sprint is a discrete period of software development during which the developers carry out the tasks identified during the sprint planning meeting. Finally, during a sprint retrospective meeting the team reviews the previous sprint to identify uncompleted tasks and review team productivity.

A key element to this approach is that each sprint leads to the completion of the tasks identified during sprint planning even if the requirements change mid-sprint. That is, adapting the development in response to changing requirements occurs during sprint planning and sprint retrospectives.

Additionally, all Scrum participants meet daily for a check-in meeting. During each check-in, each project member gives a short statement of what they worked on the day before, what they will work on in the current day, and any blockers where other tasks are limiting their progress. In this collaboration, because the developers are from geographically distributed academic institutions, we used an online real-time messaging system (Slack [51]) for daily check-ins.

*Abstractions* – The principle abstractions in the Agile process in this collaboration are the *Epic*, the *User Story*, the *task*, and the *Backlog*. An Epic is an overarching functionality road-map for the software. It is expressed in terms of User Stories and the relationships between them. A User Story is a description of a specific functionality a user would like to have the software implement. Typically, a User Story consists of the identification of the user’s role, the functionality, and the expected outcome. The collection of User Stories for the Scrum describe the expected user experience for the software. A task is a specific software development item that is necessary to complete the functionality described in one or more User Stories. Each task is scoped so that it can be completed within the time allocated to a sprint and each developer takes responsibility for completing one or more tasks. That is, tasks are not co-implemented by multiple developers. The Backlog is the collection of tasks that have yet to be claimed by a developer in a given sprint. At the beginning of a sprint, the Backlog contains all tasks to be completed during that sprint. All developers share the Backlog of tasks during a sprint. A Backlog is created during each sprint planning meeting,

and any uncompleted tasks remaining in the Backlog at the conclusion of a sprint are analyzed during the sprint retrospective.

**Personnel Roles** – A Scrum involves personnel that fulfill one of three roles: *Scrum Master*, *Product Owner*, or *Team Member*. Additionally, the project identifies *Stakeholders* who represent those invested in the success of the software, but do not take an active role in the Scrum meetings. The Scrum Master runs the Scrum, chairing all meetings, ultimately creating the Backlog for each sprint, and managing the analysis of uncompleted tasks in a sprint retrospective. In practice, our project created each Backlog collaboratively, discussing the decomposition of each User Story into tasks that could be completed within each sprint’s time frame. The Product Owner represents the interests of the Stakeholders and users. In our collaboration, the Product Owner and Scrum Master identified the specific User Stories that were to be tasked during each sprint. Finally, the Team Members comprise the developers who implement tasks during each sprint.

#### IV. INITIAL SNEWS PLANNING

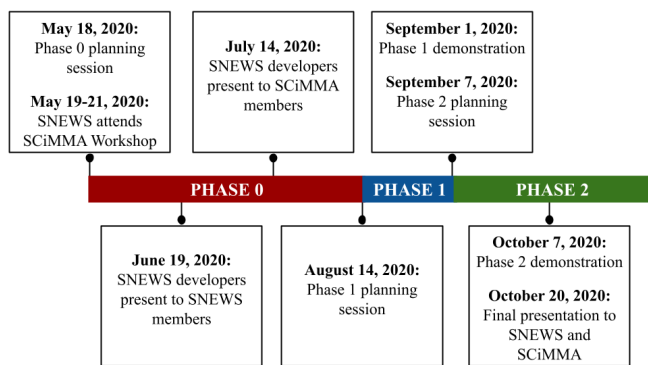


FIG. 1. Timeline of events that led to the development of the SNEWS-SCiMMA collaboration and the SNEWS 2.0 prototype. Indicated on the timeline are the three phases of the collaboration. The conclusion of each phase marked an evaluation period for each organization, which provided a decision point on whether to continue the collaboration.

SNEWS was preparing to upgrade its alert software framework from the current version of SNEWS to SNEWS 2.0. SNEWS 2.0 would require a scalable and reliable publish-subscribe system, potentially based on cloud-hosted web-services. SNEWS could either (1) build these systems from scratch, or (2) explore existing software and systems. Each option would offer both advantages and challenges. Option 1 would allow SNEWS to maintain direct control over the development and ensure their needs were met, but it would impose the burdens of long-term development, support, and maintenance entirely on SNEWS developers. This could ultimately become problematic as SNEWS scientists did

not always have formal best practices for software engineering and maintenance. Option 2 would avoid these burdens by offloading the core programming to an external software group, but it would reduce SNEWS’ control in the process and potentially limit their representation and communication during development. While considering these two options, a new possibility arose: SNEWS could instead collaborate with a development team to leverage existing expertise and systems. In particular, SCiMMA was creating HOPSKOTCH [14], a publish-subscribe system based on Apache Kafka [52, 53] that can use SCiMMA’s stand-alone `hop-client` [44] to connect to a locally-hosted Kafka server or authenticate to the cloud-hosted HOPSKOTCH instance.

##### A. Concerning the reliance on external software

Upon learning about SCiMMA and HOPSKOTCH, SNEWS considered using these services for their own development prototyping. This would allow SNEWS to kick-start its initial development using the already-existing systems and resources provided by SCiMMA, which would be supported and maintained by professional software developers long-term. However, the main concern of the SNEWS team was that the development priorities of SCiMMA may not align with SNEWS’ feature requests and bug reports, which could cause a potential latency or disconnect between SNEWS’ requirements and SCiMMA’s implementation. Moreover, the software could become unmaintainable if the SNEWS team wasn’t engaged in the development process. Nonetheless, SCiMMA’s available features and end goal appeared to fit all of the initially identified needs, so SNEWS decided to proceed.

SNEWS carried out the initial development which began in Phase 0 (Figure 1). During this stage, SNEWS developers attended the SCiMMA 2020 Virtual Workshop software demonstration session [43]. This allowed the SNEWS developers to utilize the SCiMMA `hop-client` application template, a customizable interface to HOPSKOTCH, as the basis to prototype SNEWS 2.0 using SNEWS’ previous software requirements. They extended the template with additional SNEWS-specific functionality, maintained the codebase in a private GitHub repository, and ran local tests in Python. During development, SCiMMA added the SNEWS developers to the SCiMMA Slack channel to provide user support and debugging as SNEWS developed the prototype, though the development itself was driven entirely by SNEWS. This phase resulted in a successful re-deployment of SNEWS functionality using SCiMMA’s `hop-client`.

Once SNEWS developed their prototype to the extent possible with `hop-client`, SNEWS presented a status update at SCiMMA’s July 2020 Public Teleconference [54]. This presentation highlighted SNEWS’ current implementation, usage requirements, and desired features during Phase 0 of Figure 1. Some requested features were

not currently in SCiMMA’s software, such as a database for message storage or a customizable message format. The SNEWS team considered three options: develop the missing requirements themselves, wait until SCiMMA developed these requirements in their own timeline, or seek a collaboration with SCiMMA to develop the requirements together. After the SNEWS status update, it was not clear which path forward SNEWS should take.

### B. Concerning available development effort

The SNEWS status update prompted a period of internal assessment for SCiMMA to evaluate the feasibility and utility of collaborating with SNEWS. The potential benefits of a collaboration were promising, as SNEWS would serve as SCiMMA’s first development partner and provide a practical use-case for its cyberinfrastructure. SCiMMA proposed a short period of focused development with SNEWS after the SNEWS status update near the end of Phase 0. However, this collaboration presented a risk to SCiMMA’s core goals given its limited number of developers. To mitigate this risk and ensure that development would not be derailed, the SCiMMA team formally integrated the collaboration into its own Agile sprint structure. The team created an Epic and User Stories specifically for SNEWS development support, and assigned this project to two developers. These SCiMMA developers remained active in core SCiMMA tasks and assessed the SNEWS codebase, but did not commit any time towards SNEWS software development during the remainder of Phase 0. After SNEWS’ presentation to SCiMMA and the SCiMMA developers’ internal sprint presentation, it became clear that collaborating with SNEWS would support SNEWS’ development goals while providing an informative use-case for SCiMMA’s own development. While there were still concerns about allocating effort away from core development, SCiMMA proposed a short period of focused collaboration with SNEWS (Phase 1 in Figure 1) given the many synergies between the projects. Both groups then decided to actively work together to further the development of the SNEWS 2.0 prototype.

### C. Concerning the communication during collaboration

SNEWS agreed to move forward with a focused collaboration in Phase 1 since Phase 0 confirmed both that HOPSKOTCH was a valuable technology for supporting SNEWS 2.0 and that SCiMMA was willing to work with SNEWS to meet their requirements and timeline. However, given the concerns of each organization, the structure of the collaboration would need to meet several constraints. Foremost, the workload would need to be shared between organizations. This would ensure that SNEWS would have the understanding required to sus-

tain the codebase after SCiMMA’s involvement, allow the SCiMMA developers to understand the existing SNEWS codebase on a short timescale, and avoid software duplication. This collaboration would also change SCiMMA’s previous community engagement model, wherein MMA organizations served only as end-users rather than collaborative developers. This would increase the importance of reliable communication between SNEWS and SCiMMA to identify and evaluate ideas emerging from the collaborative development. The emergent nature of these constraints, along with the short timescale, suggested that an Agile Scrum framework would benefit the collaboration.

## V. AGILE SCRUM FRAMEWORK

The collaboration was structured to address the concerns of SNEWS and SCiMMA to ensure the combined effort would benefit each individual group. The initial two-week period of focused collaborative development (Phase 1 of Figure 1) provided informative requirements for the collaboration structure, which evolved into more formal project management structures in the four-week Phase 2. Each phase proceeded only after a consensus between organizations was reached, so that the conclusion of each phase allowed each organization to evaluate whether to continue the collaboration. This approach ensured that the collaboration was addressing the evolving needs and perspectives of each organization.

### A. Addressing simultaneous development efforts

As the Phase 1 collaboration began, SCiMMA created an Epic for a collaboration with SNEWS that would run in parallel to SCiMMA’s main development efforts and dedicated two SCiMMA developers full time on this Epic. SCiMMA integrated the collaboration with SNEWS into the regular SCiMMA Agile Scrum status updates during daily check-ins and sprint retrospectives, ensuring that the SNEWS collaboration would be synchronized with SCiMMA core development, similar to using a Scaled Agile Framework to coordinate multiple teams [55]. The regular status updates provided an active dialogue throughout Phase 1, allowing SCiMMA to remain in-sync with emergent feedback and ready to adjust its development plans in response. This dialogue involved multiple new User Stories generated from bugs and feature requests during Phase 1. SCiMMA noted that many of these User Stories were of general MMA interest and decided to transfer some of these stories from the SNEWS Backlog to the their own Backlog. This synergy suggested that dedicating more effort for a focused collaboration could continue benefiting core SCiMMA development, even if it reduced total effort available in the short-term. Moreover, core development could still proceed even if several developers were focused exclusively



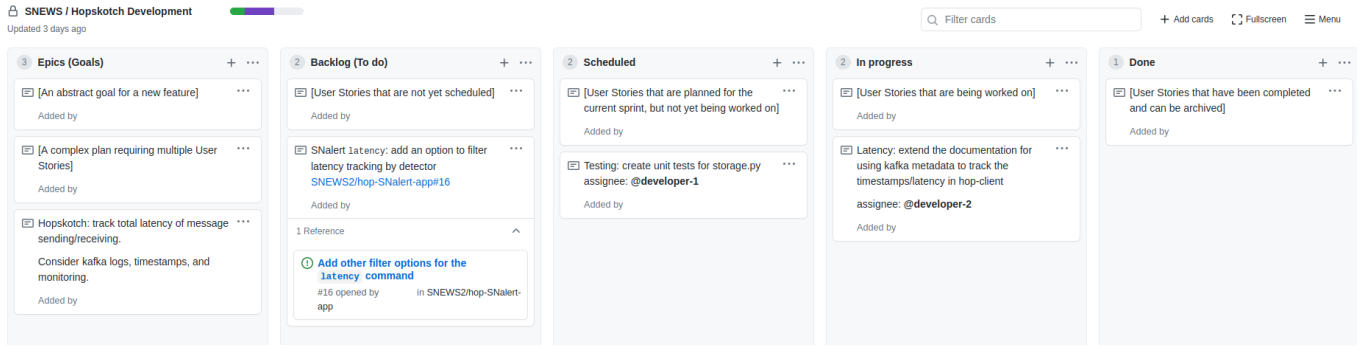


FIG. 2. An example of the GitHub Project Board used for the SNEWS-SCiMMA development collaboration. At the beginning of Phase 1 and 2, developers would brainstorm Epics in the first column based on feedback from the two organizations. During each sprint, the Scrum Master would work with developers to generate new User Stories from the Epics. These User Stories would remain in the *Backlog* column until they were assigned to a specific developer and later moved to the *Scheduled*, *In-progress*, or *Done* columns over the course of the sprint.

on an external collaboration, as the rest of the team could work on infrastructure components that were independent of the SNEWS development, such as the cloud-based message streaming system.

### B. Addressing communication & reliance on external software

To implement Agile methods for Phase 1, a SCiMMA developer took the role of Scrum Master to coordinate meetings and organize User Story creation. Developers from each team actively engaged during Phase 1, which was structured around regular communication via a dedicated Slack channel and project management via a GitHub Project Board (Figure 2) [56]. The two teams conducted one-week sprints, consisting of a review meeting each week to informally check progress and create User Story task cards on the project board. These meetings continued in-parallel with SCiMMA’s ongoing bi-weekly sprint meetings, with additional virtual pair-programming sessions for *ad hoc* code debugging and technical questions.

The collaboration involved two SCiMMA developers and four SNEWS members. The Scrum Master organized Scrum meetings and check-ins, and consulted with the product owner and Scrum Master from the primary SCiMMA sprint. One SNEWS member took the Agile role of product owner, who was responsible for ensuring that the SNEWS 2.0 prototype was within specifications and communicating the needs of SNEWS to SCiMMA during sprints. The other developers worked on improving the prototype and deploying it on test systems.

This framework ensured bilateral effort for the collaboration and provided regular communication between the organizations. It gave SNEWS an active role in the development, allowing for feature requests and bugs to be relayed through the SCiMMA developers to the ongoing SCiMMA sprint. This also allowed for SNEWS to

become familiar with the software, reducing the risk of unsustainable software after the collaboration. The Agile Scrum framework also supported timely development by allowing large goals to be translated into smaller tasks, promoting iterative development.

### C. Addressing timeline constraints

Phase 1 concluded with a demonstration of the software to the SNEWS and SCiMMA stakeholders. After reviewing the collaboration progress, it was clear that there was mutual benefit and that the initial concerns were being mitigated and appeared to be manageable. Both organizations agreed to a second, four-week period of focused development (Phase 2 of Figure 1). However, at the end of Phase 1, there were clear timeline constraints: SNEWS was seeking to begin the transition to production operation of the software and SCiMMA expected to focus more effort on the development tasks resulting from the collaboration. These new constraints prompted several changes to the collaboration structure.

Phase 2 continued to use the GitHub Project Board and daily check-ins on Slack as in Phase 1, but the sprints were restructured to better reflect timeline constraints. Four one-week sprints were set up, with a weekly sprint meeting consisting of review and planning sections, in addition to the ongoing daily check-ins. In the review section, the developers gave short, round-table updates on their progress and blockers from the previous week based on the cards they were assigned. In the planning section, the Scrum Master evaluated the status of the *Scheduled* and *In-progress* task cards in the project board (Figure 2), marking them as *Done* or *In-progress*. The developers then created new Backlog cards by discussing the existing Epics and self-assigned them to work on in the upcoming week. This revised format matched the Agile Scrum development model, as the short-term iterative development progress could be checked against



the longer-term Epics during each week.

While the one-week sprint cadence differed from SCiMMA’s two-week sprint schedule, this allowed the SNEWS effort to stage its planning and evaluation meetings both between SCiMMA sprint meetings and also immediately after them. In this way, the SNEWS effort was able to respond to requirement changes introduced by the core SCiMMA effort. If the Agile timelines had been the same, there was a risk that the SNEWS effort would respond during a two week sprint only to find that the core effort had already introduced specification changes, and thus SNEWS would never be able to remain in-sync with the SCiMMA development. This allowed SNEWS to keep a separate timeline for its own deliverables without depending on the timeline for core SCiMMA development.

The second purpose allowed SNEWS to pick a specific release date set for the end of Phase 2. The intention of the SNEWS team was for Phase 2 to result in a product that could be effectively released to SNEWS for further enhancement and operational deployment. After this release, SNEWS would contribute to SCiMMA as a community member through existing interaction mechanisms such as workshops, but not through direct collaboration. Thus the developers on both teams decided on multiple week-long sprints to achieve the end goal for the software.

As with Phase 1, Phase 2 concluded with a demonstration of the software to the stakeholders, which was recorded as an endpoint marking the conclusion of the dedicated software development period [57].

## VI. DISCUSSION

Phase 0	Phase 1	Phase 2
<b>Goal:</b> Rewrite SNEWS using the hop-client	<b>Goal:</b> Test prototype components locally	<b>Goal:</b> Add features and test prototype components remotely
<b>Outcome:</b> Prototype of SNEWS 2.0 working with initial publishing, subscribing, and decision making frameworks	<b>Outcome:</b> Prototype working with distributed components via local installations and containerized servers	<b>Outcome:</b> Prototype working with new features and distributed components via remote installations and cloud servers

FIG. 3. Illustration of the goals and outcomes for each phase of the SNEWS-SCiMMA collaboration. Each phase proceeded after a progress review and consensus within each organization.

Both phases of the collaboration were structured around technical demonstrations after each phase to iteratively evaluate progress, assess current goals, and plan out goals for the next phase. Both phases utilized weekly meetings coordinated via a GitHub Project Board (Figure 2) for task and project management.

The main goal of Phase 0 was to rewrite the current SNEWS publish-subscribe system using the

hop-client [44] (Figure 3). This phase was marked successful by the demonstration of a working prototype that included sample publishing and subscribing of messages with the SNEWS decision making framework. This established the system’s baseline prior to any collaborative development and gave SNEWS the confidence to rely on external software.

Phase 1 was then planned around a goal to develop a prototype of the system running locally (Figure 3). To capture SNEWS’ large goals from Phase 0, the developers created five broad Epics. These were translated into 10 User Stories over the course of Phase 1. Some of these Stories were relatively broad and took more than one week or developer to complete since the teams were learning how best to collaborate and manage the project. Nonetheless, eight of the Stories were completed by merging five pull-requests and resolving four issues during Phase 1. The teams then assessed the progress of this phase via a demonstration of a prototype that used local containerized services and a local installation of the SNEWS 2.0 app. The prototype at this stage replicated most of the current SNEWS functionality. Both teams approved of the collaboration’s progress: SNEWS had a new implementation of their server and SCiMMA improved the hop-client features beyond their initial scope. Both collaborations agreed to proceed with a second round of collaboration, Phase 2.

Phase 2 built on the Phase 1 goal of a local prototype by extending the prototype using distributed systems, with cloud servers to demonstrate robustness of remote but integrated components (Figure 3). The developers reviewed the remaining Epics and User Stories from Phase 1, and determined that two Epics were no longer in-scope with the teams’ goals after the Phase 1 demonstration. The remaining three Epics and two User Stories were determined to still be relevant and were carried over into Phase 2. This phase began with six new Epics based on the assessment of the Phase 1 demonstration, focusing on measuring the prototype’s performance and improving client authentication. This phase allowed SCiMMA to test a service that used their cloud servers and SNEWS was able to create a fully-functioning prototype. The Epics were translated into 29 User Stories over the course of Phase 2. Of these, 15 were completed by merging eight pull-requests and resolving three issues during Phase 2. Both organizations reconvened for a demonstration of the remote prototype, which met the initial goal and concluded Phase 2. After the demonstration, seven of the nine Epics were completed. The remaining two were either ill-defined or out-of-scope for the collaboration. Fourteen of the 29 User Stories were incomplete: five *Backlog*, six *Scheduled*, and three *In-Progress*. The developers continued working on four of these User Stories independently after the collaboration; the remaining 10 User Stories were considered out-of-scope for the collaboration period since the desired Epics had already been met.

After the demonstration and evaluation of Phase 2,

the collaboration had successfully produced a prototype of SNEWS 2.0 using SCiMMA’s `hop-client` publish-subscribe system [13]. The prototype established directions for future development for each group, allowing the organizations to remain in contact even after the phases of focused collaboration had concluded. It has provided direction for SCiMMA’s authentication and permission management infrastructure, and has helped SNEWS begin prototyping their detector network using the SCiMMA `hop-client`. The next steps after the development of the prototype include having SNEWS members from outside the development team test the software using tutorials provided by the SCiMMA developers. This beta testing would ensure that the software is user-friendly, with few or no bugs in the codebase. After this testing, SNEWS plans to integrate all of its neutrino experiments into the SNEWS 2.0 network. This will happen during a dedicated workshop wherein SNEWS will implement Agile methods, similar to those utilized during Phase 2 to drive the development. Specifically, the workshop will take place over a four-week sprint and will include daily check-in meetings to discuss progress. Additionally, Epics and User Stories will be defined to keep the integration plans on track.

The collaboration promoted the general development efforts for each group. SNEWS utilized SCiMMA’s systems and software engineering expertise to quickly develop their prototype, allowing SNEWS to avoid the difficulties of scientific computing and software development. The coordination between the two software development efforts unexpectedly accelerated the pace of SCiMMA’s core development since SNEWS’ use-case contained features that were of broader MMA interest. Additionally, it provided an exemplar for future engagements: SCiMMA plans to integrate this approach for future collaborations within the MMA community. While another engagement would be adapted to meet a potential collaborator’s development status and might involve a trial period as in Phase 1, SCiMMA would emphasize an Agile structure similar to Phase 2 for core development.

## VII. RELATED WORK

Our work shares much with the work described in [24] in that both are experiential case studies describing the interaction between scientists and development engineers. Our work differs in that the teams involved do not belong to a single organization nor are they focused on the completion of a single mission. Further, the author of [24] cites difficulty in creating effective specifications as a key impediment to a successful collaboration. The adoption of an Agile process for our project seems to have alleviated this difficulty as it was designed to do. However, it introduced additional risks to the success of the collaboration that the previous work did not report.

In [2], the authors conduct and report on a survey of scientific development teams and organizations to de-

termine how these teams build software. They report features of scientific development described in their survey that our collaboration also embodies, such as the “trust” in community-maintained software when the community is large, such as SCiMMA’s use of public Kafka libraries [53]. Our work is largely complementary, however, as we adopted a specific approach without a controlled comparison with other alternative approaches. As such, our work would constitute a single, successful data point within this previous survey.

In [20], the authors survey climate scientists to determine their common software development practices. They find that, philosophically and culturally, many development teams resonate with the tenets of Agile development. Our work seems to support this hypothesis, albeit in a different scientific context, in that the teams involved in our study successfully adopted an Agile framework without much difficulty.

In [26], the author advances a theoretical framework that suggests the use of Agile practices, such as test-driven development and refactoring, as useful approaches to scientific software development. Our work offers no additional theoretical basis in this context, but could serve as empirical support for this framework given the utility of Agile methods in supporting our scientific software development collaboration.

Our work also advances an Agile coordination mechanism between ongoing development projects where development of the “upstream” project must proceed ahead of the “downstream” project that depends on it. In [55], the authors suggest an additional Agile abstraction designed to extend Scrum to organize multiple Agile teams, called the Scaled Agile Framework. Our work differs in two key ways. First, we articulate a specific methodology based on the Agile abstractions. That is, the upstream project developed Epics and User Stories that were incorporated into its Backlog. The completion of those Backlog tasks would then prompt the creation of User Stories in the downstream Backlog. Secondly, we were only able to observe the effectiveness of this methodology in a bilateral context with a single organizational dependency, rather than many dependencies across a number of teams.

## VIII. CONCLUSION

The development of software to support collaborative science projects requires risk mitigation between the teams involved. This case study describes the risks that the project members identified and the way in which the collaboration confronted them. In this collaboration, the emergent concerns and needs of each organization were addressed by adopting Agile Scrum practices with an active dialogue between organizations. By working in sprints, the high-level goals of each organization were translated into manageable development tasks. The software developers utilized the practical use-case from the science team to further its software and infrastruc-

ture to support the broader MMA community. The science team gained a functional and maintainable prototype of their desired software while also gaining valuable software development experience. The collaboration allowed both organizations to gain useful experience and furthered their science programs in ongoing and future work. From this work we outline the following key take-aways:

- Bi-lateral effort in collaborative software development can promote engagement, reduce code duplication, and improve communication of requirements and concerns.
- Agile Scrum practices allow for software development to be flexible to rapidly changing requirements, which is particularly important when creating scientific applications.
- Collaborations between scientists and software developers can accelerate the creation of scientific software applications while also promoting knowledge transfer between domains.
- The adoption of Cloud technologies may prove beneficial for scientific applications if the deployment and cost are managed by an external organization.

The framework described herein proved to be beneficial in this study, which involved  $\mathcal{O}(10)$  people across two teams and time frames  $\mathcal{O}(\text{months})$ . Note that these strategies may not generalize to larger-scale or well-established development projects, which may struggle to either implement Agile practices or respond to rapidly-emerging software requirements. However, these practices could still alleviate some of the general difficulties of scientific software engineering, such as interdisciplinary communication, creating sustainable software without relying on external code, and constrained resources and timelines. These emergent and iterative frameworks can additionally support the need for rapid results and ever-changing requirements of the scientist user-group community. This case study indicates that a collaborative development approach centered on an Agile Scrum framework can benefit both the scientific user-group and the software developer team while mitigating some of the difficulties facing the scientific software engineering community.

## AUTHOR CONTRIBUTIONS

The alphabetic-order author list reflects a variety of contributions from members in the SCiMMA and SNEWS organizations. Particular contributions to this paper and the SCiMMA-SNEWS collaboration are noted as follows. BC, ALB, and RW made primary contributions to the text. BC and ALB led the demonstrations after each phase of development. BC organized and led the development sprints, supported software development during Phases 1 and 2, and implemented the software on cloud infrastructure. ALB served as a SNEWS product owner, supported software development during Phases 0, 1 and 2, and contributed substantially during development sprints. YX led the SNEWS software development process during Phase 0, 1 and 2. PG led the SCiMMA software development during Phases 1 and 2. Together, PG and YX contributed substantially during development sprints. MWL supported software development during Phases 1 and 2, and implemented the software on prototype infrastructure. AH served as a SNEWS product owner and provided substantial input during development sprints. AB, AH, MJ, RFL, CDT and RW each provided substantial input during progress reviews after each phase. AB, MJ, and CDT proposed the initial collaboration at a National Science Foundation “Harnessing the Data Revolution” grant proposal meeting.

The SCiMMA Agile Scrum team (AB, DC, BC, VE, SE, PG, DAH, MJ, WL, CM, SN, DP, RT, CW, and RW) supported core SCiMMA software development prior to and during the collaboration. Additional SCiMMA members (MWGJ, CK) have continued support of the SCiMMA project. The SNEWS Signal Prediction, Alert Formation, and Follow-up working group members (ALB, SYB, WB, MC, AC, MCM, ADO, DD, AGR, SG, AH, RH, SH, JPK, AK, VK, ML, RFL, SL, ML, MWL, JM, DM, RN, EO, BWP, NJ, AR, JR, TS, JCLT, CDT, CFV, CJV, KEW, LW, XJX, YX) supported SNEWS software development prior to and during the collaboration.

## ACKNOWLEDGMENTS

This work is supported by the National Science Foundation “Windows on the Universe: The Era of Multi-Messenger Astrophysics” program: “WoU-MMA: Collaborative Research: A Next-Generation Supernova Early Warning System for Multimessenger Astronomy” through grants 1914448, 1914409, 1914447, 1914418, 1914410, 1914416, 1914426; and via the “HDR-Harnessing the Data Revolution” program, grant 1940209; and with the “Office of Advanced Cyberinfrastructure” through grant 1934752.

- [1] F. P. Brooks, *Commun. ACM* **39**, 61–68 (1996).
- [2] J. E. Hannay *et al.*, in *Proceedings of the 2009 ICSE Workshop on Software Engineering for Computational Science and Engineering*, SECSE '09 (IEEE Computer Society, USA, 2009) p. 1–8.
- [3] Z. Merali, *Nature* **467**, 775 (2010).
- [4] US RSE, The us research software engineer association, <https://us-rse.org> (2021).
- [5] M. Armbrust, A. Fox, R. Griffith, A. D. Joseph, R. H. Katz, A. Konwinski, G. Lee, D. A. Patterson, A. Rabkin, I. Stoica, *et al.*, *Above the clouds: A berkeley view of cloud computing*, Tech. Rep. (Technical Report UCB/EECS-2009-28, EECS Department, University of California ... , 2009).
- [6] D. Nurmi, R. Wolski, C. Grzegorzczak, G. Obertelli, S. Soman, L. Youseff, and D. Zagorodnov, in *IEEE Cluster Computing and the Grid* (2009).
- [7] D. Chawla, *Nature* **529**, 115 (2016).
- [8] D. F. Kelly, *IEEE Software* **24**, 120 (2007).
- [9] T. Storer, *ACM Computing Surveys* **50**, 1 (2017).
- [10] G. Wilson *et al.*, *PLOS Biology* **12**, 1 (2014).
- [11] S. Al Kharusi *et al.* (SNEWS) (2020) arXiv:2011.00035 [astro-ph.HE].
- [12] P. Chang *et al.*, *Cyberinfrastructure Requirements to Enhance Multi-messenger Astrophysics* (2019), arXiv:1903.04590 [astro-ph.IM].
- [13] P. Godwin *et al.*, SNEWS2/hop-SNalert-app: Release 1.0 For Zenodo reference, <https://doi.org/10.5281/zenodo.4437579> (2021).
- [14] SCiMMA Collaboration, Hopskotch, <https://hop.scimma.org> (2021).
- [15] K. Bennett, *IEEE Software* **12**, 19 (1995).
- [16] J. Segal and C. Morris, *Handbook of Research on Computational Science and Engineering: Theory and Practice* (2011).
- [17] A. A. Adenowo and B. A. Adenowo, *International Journal of Scientific & Engineering Research* **4**, 427 (2013).
- [18] K. M. Beck *et al.*, *Manifesto for Agile Software Development* (2013), <https://agilemanifesto.org>.
- [19] D. Kane *et al.*, *BMC bioinformatics* **7**, 273 (2006).
- [20] S. M. Easterbrook and T. C. Johns, *Computing in science & engineering* **11**, 65 (2009).
- [21] K. Schwaber, *Business Object Design and Implementation*, edited by J. Sutherland, C. Casanave, J. Miller, P. Patel, and G. Hollowell (Springer London, London, 1997) pp. 117–134.
- [22] M. Sletholt *et al.*, *Proceedings - International Conference on Software Engineering* 10.1145/1985782.1985784 (2011).
- [23] J. Segal, in *SECSE 08, First International Workshop on Software Engineering in Computational Science and Engineering* (2008) workshop co-located with ICSE 08 <http://oro.open.ac.uk/17673/>.
- [24] J. Segal, *Empirical Software Engineering* **10** (2005).
- [25] C. A. Crabtree, A. G. Koru, C. Seaman, and H. Erdogmus, in *2009 ICSE Workshop on Software Engineering for Computational Science and Engineering* (2009) pp. 22–27.
- [26] P. C. Lane and F. Gobet, *Journal of Experimental & Theoretical Artificial Intelligence* **24**, 421 (2012).
- [27] M. Umarji *et al.*, in *2009 22nd Conference on Software Engineering Education and Training* (2009) pp. 216–223.
- [28] P. Antonioli *et al.*, *New J. Phys.* **6**, 114 (2004), arXiv:astro-ph/0406214.
- [29] K. Nakamura *et al.*, *Mon. Not. Roy. Astron. Soc.* **461**, 3296 (2016), arXiv:1602.03028 [astro-ph.HE].
- [30] Ž. Ivezić *et al.* (LSST), *Astrophys. J.* **873**, 111 (2019), arXiv:0805.2366 [astro-ph].
- [31] B. P. Abbott *et al.*, *Astrophys. J. Lett.* **848**, L12 (2017), arXiv:1710.05833 [astro-ph.HE].
- [32] M. J. Graham *et al.*, *Publ. Astron. Soc. Pac.* **131**, 078001 (2019), arXiv:1902.01945 [astro-ph.IM].
- [33] M. Smith *et al.*, *Astropart. Phys.* **45**, 56 (2013), arXiv:1211.5602 [astro-ph.HE].
- [34] M. Ageron *et al.*, *Astropart. Phys.* **35**, 530 (2012), arXiv:1103.4477 [astro-ph.IM].
- [35] E. Huerta *et al.*, *Nature Rev. Phys.* **1**, 600 (2019), arXiv:1911.11779 [gr-qc].
- [36] M. G. Aartsen *et al.* (IceCube), *Astropart. Phys.* **92**, 30 (2017), arXiv:1612.06028 [astro-ph.HE].
- [37] International Astronomical Union, The Transient Name Server, <https://www.wis-tns.org/> (2015).
- [38] S. D. Barthelmy *et al.*, *AIP Conference Proceedings* **526**, 731 (2000), <https://aip.scitation.org/doi/pdf/10.1063/1.1361631>.
- [39] C. Gabriel, C. Arviset, D. Ponz, and S. Enrique (2006).
- [40] R. Rutledge, *Publ. Astron. Soc. Pac.* **110**, 754 (1998), arXiv:astro-ph/9802256.
- [41] G. Allen *et al.* (2018) arXiv:1807.04780 [astro-ph.IM].
- [42] SCiMMA Collaboration, Scimma google groups, <https://groups.google.com/g/scimma> (2020).
- [43] SCiMMA Collaboration, Scimma virtual workshop, <https://scimma.org/events/virtual2020> (2020).
- [44] P. Godwin *et al.*, scimma/hop-client: v0.2 release of scimma/hop-client, <https://doi.org/10.5281/zenodo.4033483> (2020).
- [45] SCiMMA Collaboration, Scimma infrastructure repository, <https://github.com/scimma/scimma-admin> (2020).
- [46] M. A. Heroux and J. M. Willenbring, in *Proceedings of the 2009 ICSE Workshop on Software Engineering for Computational Science and Engineering*, SECSE '09 (IEEE Computer Society, USA, 2009) p. 15–21.
- [47] SCiMMA Collaboration, Scimma containerization repository, <https://github.com/scimma/scimma-server-container> (2020).
- [48] J. Aasi, B. Abbott, R. Abbott, T. Abbott, M. Abernathy, K. Ackley, C. Adams, T. Adams, P. Addesso, R. Adhikari, *et al.*, *Classical and quantum gravity* **32**, 074001 (2015).
- [49] M. G. Aartsen, M. Ackermann, J. Adams, J. Aguilar, M. Ahlers, M. Ahrens, D. Altmann, K. Andeen, T. Anderson, I. Ansseau, *et al.*, *Journal of Instrumentation* **12** (03), P03012.
- [50] National Science Foundation, Harnessing the data revolution at nsf, <https://www.nsf.gov/cise/harnessingdata/> (2020).
- [51] Slack Technologies, Slack, <https://slack.com> (2021).
- [52] M. J. Sax, Apache kafka, in *Encyclopedia of Big Data Technologies* (Springer International Publishing, Cham, 2018) pp. 1–8, [https://doi.org/10.1007/978-3-319-63962-8\\_196-1](https://doi.org/10.1007/978-3-319-63962-8_196-1).

- [53] Confluent Inc., Confluent's python client for apache kafka, <https://github.com/confluentinc/confluent-kafka-python> (2021).
- [54] A. Depoian, Using SCiMMA architecture for SNEWS 2.0, <https://www.youtube.com/watch?v=GJLTCycvknE> (2020).
- [55] R. Brenner and S. Wunder, in *2015 IEEE Eighth International Conference on Software Testing, Verification and Validation Workshops (ICSTW)* (IEEE, 2015) pp. 1–2.
- [56] GitHub, About project boards, <https://docs.github.com/en/github/managing-your-work-on-github/about-project-boards> (2021).
- [57] B. Cousins and A. Depoian, SNEWS 2.0 Prototyping with SCiMMA, <https://www.youtube.com/watch?v=ZZ04CIqUTcY> (2020).
